

AECTPL/ENV/KPL/HYC/2023/20

Date: 31.07.2023

To,
The General Manager (Marine Services)
Kamarajar Port Limited,
23, Rajaji Salai, Chennai - 600 001

Dear Sir,

Sub: Development of container terminal at Kamarajar Port Limited on DBFOT basis, KPL awarded to Adani Ennore Container Terminal Private Limited (AECTPL)-
Submission of Half yearly Compliance (January 2023 to June 2023) of Environmental Clearance issued to Kamarajar Port Limited in various stages of development with regards to Container Terminal - Reg.


- Ref:** 1. Vide order no: 10-28/2005-IA-III dated 19th May, 2006
2. Vide order no: 10-28/2005-IA-III dated: 10/09/2007 and validity extension date: 31.03/2017
3. Vide order no: 10-28/2005-IA-III dated: 24/12/2014

With reference to the above captioned subject, **Adani Ennore Container Terminal Private Limited** is submitting the **Half yearly compliance report** (for the period **January 2023 to June 2023**) of applicable conditions to the Environmental & CRZ Clearance obtained by the M/s. Kamarajar Port Limited in various stages of development as referred above.

Kindly acknowledge receipt of the same.

For M/s. Adani Ennore Container Terminal Private Limited,


A. Subramanian
Environment Department



Encl.: As above.

Adani Ennore Container Terminal Pvt Ltd
Adani House
C/o. Kamarajar Port Limited
Ponneri Taluk, Tiruvallur District
Tamil Nadu- 600 120.

Tel +91 44 2824 3062

info@adani.com
www.adani.com

CIN: U61200GJ2014PTC078795

Registered Office: Ramcon Fortuna Towers, 4th floor No 1/2, Kodambakkam High Road, Nungambakkam, Chennai- 600034

Subramanian A

From: Subramanian A
Sent: Monday, July 31, 2023 6:01 AM
To: V G Sravan Kumar
Cc: M R Rao; kkannan.epl; G M Balan; Kenni Bhoopathy
Subject: RE: Half yearly Environmental compliance report-regarding-Reg.
Attachments: Half Yearly EC Complainece_AECTPL-Jan'23 to Jun'23.pdf; a. AECTPL EC Compliance 19052006- (Jan'23 to Jun'23).xlsx; c. AECTPL EC Compliance 24122014- (Jan'23 to Jun'23).xlsx; b. AECTPL EC Compliance 10092007- (Jan'23 to Jun'23).xlsx

Dear Sir,

Sub: Development of container terminal at Kamarajar Port Limited on DBFOT basis, KPL awarded to Adani Ennore Container Terminal Private Limited (AECTPL)- **Submission of Half yearly Compliance (January 2023 to June 2023) of Environmental Clearance issued to Kamarajar Port Limited in various stages of development with regards to Container Terminal - Reg.**

Ref: 1. Vide order no: 10-28/2005-IA-III dated 19th May, 2006
2. Vide order no: 10-28/2005-IA-III dated: 10/09/2007 and validity extension date: 31.03/2017
3. Vide order no: 10-28/2005-IA-III dated: 24/12/2014

With reference to the above captioned subject, **Adani Ennore Container Terminal Private Limited** is submitting the **Half yearly compliance report** (for the period **January 2023 to June 2023**) of applicable conditions to the Environmental & CRZ Clearance obtained by the M/s. Kamarajar Port Limited in various stages of development as referred above.

Kindly acknowledge receipt of the same.

For M/s. **Adani Ennore Container Terminal Private Limited,**

Thanks & Regards,

Subramanian A
Assistant Manager- Environment & Sustainability

Marine Infrastructure Developer Private Limited | Adani Ennore Container Terminal Pvt Ltd.
(M) +91 91509 44421 | (O) 69018 | subramanian.A@adani.com | www.adani.com



Growth
with
Goodness

Our Values: Courage | Trust | Commitment



AECTPL/ENV/KPL/HYC/2023/20

Date: 31.07.2023

To,
The General Manager (Marine Services)
Kamarajar Port Limited,
23, Rajaji Salai, Chennai - 600 001

Dear Sir,

Sub: Development of container terminal at Kamarajar Port Limited on DBFOT basis, KPL awarded to Adani Ennore Container Terminal Private Limited (AECTPL)-
Submission of Half yearly Compliance (January 2023 to June 2023) of Environmental Clearance issued to Kamarajar Port Limited in various stages of development with regards to Container Terminal - Reg.

Ref: 1. Vide order no: 10-28/2005-IA-III dated 19th May, 2006
2. Vide order no: 10-28/2005-IA-III dated: 10/09/2007 and validity extension date: 31.03/2017
3. Vide order no: 10-28/2005-IA-III dated: 24/12/2014

With reference to the above captioned subject, **Adani Ennore Container Terminal Private Limited** is submitting the **Half yearly compliance report** (for the period **January 2023 to June 2023**) of applicable conditions to the Environmental & CRZ Clearance obtained by the M/s. Kamarajar Port Limited in various stages of development as referred above.

Kindly acknowledge receipt of the same.

For M/s. **Adani Ennore Container Terminal Private Limited,**



A. Subramanian
Environment Department



Encl.: As above.

Adani Ennore Container Terminal Pvt Ltd
Adani House
C/o. Kamarajar Port Limited
Ponneri Taluk, Tiruvallur District
Tamil Nadu- 600 120.

Tel +91 44 2824 3062

info@adani.com
www.adani.com

CIN: U61200GJ2014PTCO78795



Ports and
Logistics

**ADANI ENNORE CONTAINER TERMINAL PRIVATE LIMITED (AECTPL)
C/o. KAMARAJAR PORT LIMITED, VALLUR POST,
PONNERI TALUK, ENNORE, TIRUVALLUR DISTRICT, CHENNAI- 600 120
TAMIL NADU**



CRZ & Environmental Clearance
[File no: 10-28/2005- IA.III dated: 19/05/2006]
Compliance Report
for the Period
JANUARY 2023 TO JUNE 2023

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

Index

Sr.No.	Details of Annexure		Page No.
1.	CRZ & Environmental Clearance Compliance Report [File no: 10-28/2005- IA.III dated: 19/05/2006]		1
	CRZ & Environmental Clearance Compliance Report [Order no: 10-28/2005-IA-III dated: 10/09/2007 and validity extension date: 31.03/2017]		12
	CRZ & Environmental Clearance Compliance Report [Vide order no: 10-28/2005-IA-III dated: 24/12/2014]		19
2.	Enclosures		
	Annexure I	Environmental Monitoring reports for the period January 2023 to June 2023	
	Annexure II	Environmental Statement – Form V for the FY 2021-22	

CRZ & ENVIRONMENTAL CLEARANCE COMPLIANCE REPORT

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

**Half yearly Compliance report on conditions stipulated in CRZ & Environmental Clearance
[File no: 10-28/2005- IA.III dated: 19/05/2006]**

S. No.	Conditions	Compliance Status
Specific Conditions		
I.	All the conditions stipulated in the NOC from TNPCB vide their letter No. T12/TNPCB/Misc./F.3322/TVLR/05, dated 07.12.2005 should be strictly implemented.	Status by KPL.
II.	Groins and other suitable structures should be constructed to prevent the closing of the mouth of Ennore Creek.	Status by KPL.
III.	The DPR and the technical details to be awarded to the BOT operator should provide to MoEF for post project monitoring within 6 months from the date of receipt of this letter.	Complied. Container Terminal DPR submitted vide letter number EPL/MS/49/2008 dt. 13/03/2008.
IV.	The marine terminal should be set up outside CRZ area.	Status by KPL.
V.	Recommendations of Risk Analysis report should be strictly implemented, and a comprehensive quantitative Risk Analysis should be carried out before operationalizing the project.	Complied Operational Risk Assessment carried out and the recommendations are being implemented. Operational Risk Assessment report submitted vide Letter No.AECTPL/KPL/EC-compliance/Env/02 dt. 13.07.2018.
VI.	Approval form Chief Controller of Chief Explosives should be obtained for hazardous chemicals storage, transfer and related activities.	Not Applicable. AECTPL is not storing any Hazardous chemicals. Hence not applicable.
VII.	The reclamation of the port area should be carried out with the dredged materials. Dredged material should not be dumped into the sea. No reclamation should be carried outside the port limits.	Status by KPL.

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

**Half yearly Compliance report on conditions stipulated in CRZ & Environmental Clearance
[File no: 10-28/2005- IA.III dated: 19/05/2006]**

S. No.	Conditions	Compliance Status
VIII.	The coastal protection works should be carried out after detailed hydrodynamic modelling studies and it should be ensured that no erosion or accretion takes place in the shore protection works.	Status by KPL.
IX.	Reclamation of 500 acres should be carried out only for the port development. The height of the reclaimed area will be maintained above the maximum flood level.	Status by KPL.
X.	The wave tranquillity study and the ship manuring studies carried out should be taken into account while operating the port.	Status by KPL.
XI.	The project proponent should ensure that doing construction and operation of the port there will be impact on the livelihood of the fisherman. The fishermen should be provided free access to carry out the fishing activity.	Status by KPL.
XII.	All necessary precaution while undertaking construction and operation of the port should be taken keeping in view the bathymetric changes caused due to tsunami.	Status by KPL.
XIII.	All development in the port should be accordance with the Coastal Regulation Zone Notification, 1991 and approved Coastal Zone Management Plan of Tamil Nadu.	Status by KPL.

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

**Half yearly Compliance report on conditions stipulated in CRZ & Environmental Clearance
[File no: 10-28/2005- IA.III dated: 19/05/2006]**

S. No.	Conditions	Compliance Status
XIV.	The project proponent should undertake a comprehensive hydrodynamic modelling study with regard to river diversion and submit the report to the Ministry within 6 months from the date of receipt of this letter. Further the unit should comply with all the findings/recommendations of the study.	Status by KPL.
XV.	Construction labour camps should be located outside of CRZ area and should be provided with adequate cooking and sanitation facilities.	Complied. Construction of container terminal is completed, and the terminal is under operation
XVI.	The project affected people, of any should be properly compensated and rehabilitated.	Status by KPL.

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

**Half yearly Compliance report on conditions stipulated in CRZ & Environmental Clearance
[File no: 10-28/2005- IA.III dated: 19/05/2006]**

S. No.	Conditions	Compliance Status
GENERAL CONDITIONS:		
I.	Development of the proposed channel should be undertaken meticulously conforming to the existing Central/Local rules and regulations including CRZ Notification, 1991 and its amendments. All the construction designs/drawings relating to the proposed development activities must have approvals of the concerned State Govt. Depts./Agencies.	Status by KPL.
II.	A well-equipped laboratory with suitable instruments to monitor the quality of air and water shall be set up as to ensure that the quality of ambient air and water conforms to the prescribed standards. The laboratory will also equipped with qualified manpower including a marine biologist so that the marine water quality is regularly monitored in order to ensure that the marine life is not adversely affected as a result of implementation of the said project. The quality of ambient air and water shall be monitored periodically in all the seasons and the results should be properly maintained for inspection of concerned pollution control agencies. The periodic monitoring reports at least once in 6 months must be send to this Ministry (RO at Bangalore) and Pollution Control Committee.	<p>Complied.</p> <p>AECTPL is engaging NABL accredited laboratory for regular monitoring of Ambient Air Quality, Ambient Noise Level, DG Stack Emission, Meteorological data, Soil Quality, Marine Surface & Bottom Water quality and Sea Sediment quality. The monitored results are submitted to KPL and Tamil Nadu Pollution Control Board on monthly basis and also as part of Six-monthly compliance report. Monitoring reports are properly maintained and made available for inspection to Pollution Control Agencies, as and when required.</p> <p>Environment Monitoring report for the period January 2023 – June 2023 is attached as Annexure - I.</p>

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

**Half yearly Compliance report on conditions stipulated in CRZ & Environmental Clearance
[File no: 10-28/2005- IA.III dated: 19/05/2006]**

S. No.	Conditions	Compliance Status																														
III.	Adequate provisions for infrastructure facilities such as water supply, fuel for cooking, sanitation etc. must be provided for the labourers during the construction period in order to avoid damage to the environment. Colonies for the labourers should not be located in CRZ area. It should also be ensured that the construction workers do not cut trees including mangroves for fuel wood purpose.	Complied. Construction of the terminal is completed, and terminal is in operation.																														
IV.	To prevent discharge of sewage and other liquid wastes into the water bodies, adequate system for collection and treatment of the waste must be provided. No Sewage and other liquid wastes without treatment should be allowed to enter into the water bodies.	Complied. AECTPL is operating 25 KLD capacity Sewage Treatment Plant to treat the domestic effluent being generated from various sources such as washing water from canteen and toilet flushing water from office buildings. The entire treated sewage water is reused for green belt maintenance within the port premises after confirming permissible limit. Inlet & outlet characteristic of Sewage water is regularly monitored and analysed by NABL accredited laboratory. The monitoring results for the period January'23 to June'23 is enclosed as Annexure - I . Summary of STP treated water analysis results during compliance period as mentioned below. <table><tr><th>Parameter</th><th>Unit</th><th>Min</th><th>Max</th><th>TNPCB Limit</th></tr><tr><td>pH</td><td>-</td><td>7.08</td><td>7.92</td><td>6.5 to 9</td></tr><tr><td>TSS</td><td>mg/l</td><td>21</td><td>26</td><td>30</td></tr><tr><td>BOD</td><td>mg/l</td><td>14</td><td>18</td><td>20</td></tr><tr><td>COD</td><td>mg/l</td><td>58</td><td>88</td><td>100</td></tr><tr><td>Faecal Coliform</td><td>MPN/100ml</td><td>110</td><td>130</td><td><1000</td></tr></table>	Parameter	Unit	Min	Max	TNPCB Limit	pH	-	7.08	7.92	6.5 to 9	TSS	mg/l	21	26	30	BOD	mg/l	14	18	20	COD	mg/l	58	88	100	Faecal Coliform	MPN/100ml	110	130	<1000
Parameter	Unit	Min	Max	TNPCB Limit																												
pH	-	7.08	7.92	6.5 to 9																												
TSS	mg/l	21	26	30																												
BOD	mg/l	14	18	20																												
COD	mg/l	58	88	100																												
Faecal Coliform	MPN/100ml	110	130	<1000																												

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

**Half yearly Compliance report on conditions stipulated in CRZ & Environmental Clearance
[File no: 10-28/2005- IA.III dated: 19/05/2006]**

S. No.	Conditions	Compliance Status
		All the parameters are well within the prescribed norms.
V.	Appropriate facility should be created for the collection of solid and liquid wastes generated by the barges/vessels and their safe treatment and disposal should be ensured to avoid possible contamination of the water bodies.	Status by KPL.
VI.	Necessary navigational aids such as channel markers should be provided to prevent accidents. Internationally recognized safety standards shall be applied in case of barge/vessel movements.	Status by KPL.
VII.	The project authorities should take appropriate community development and welfare measures for villagers in the vicinity of the project site, including drinking water facilities. A separate fund should be allocated for the purpose.	<p>Status by KPL.</p> <p>However, AECTPL has implemented CSR activities like Evening Education centre(638 Students benefited), Computer SMART Lab for +1 & +2 Students with 20 computer system, Mobile Health Care Unit, Comprehensive Eye Camps, Suposhan Program, Supporting for Organic Farming to 300 farmers in 300 acres, conducted technical workshop for farmers on Soil fertility, Constructed community toilets, Installed RO plants, De-siltation of Kattupalli Pond, etc., in the vicinity of the Port area.</p> <p>Expenses incurred for CSR during the compliance period is Rs.164.47 Lakhs and the breakup details are as follows;</p>


Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

**Half yearly Compliance report on conditions stipulated in CRZ & Environmental Clearance
[File no: 10-28/2005- IA.III dated: 19/05/2006]**

S. No.	Conditions	Compliance Status																		
		<table> <tr> <th>S.No</th><th>Description</th><th>Amount (Rs in Lakhs)</th></tr> <tr> <td>1</td><td>Education</td><td>24.01</td></tr> <tr> <td>2</td><td>Health</td><td>29.97</td></tr> <tr> <td>3</td><td>Sustainable Livelihood Development</td><td>90.38</td></tr> <tr> <td>4</td><td>Community Infrastructure Development</td><td>20.11</td></tr> <tr> <td colspan="2">Total</td><td>164.47</td></tr> </table>	S.No	Description	Amount (Rs in Lakhs)	1	Education	24.01	2	Health	29.97	3	Sustainable Livelihood Development	90.38	4	Community Infrastructure Development	20.11	Total		164.47
S.No	Description	Amount (Rs in Lakhs)																		
1	Education	24.01																		
2	Health	29.97																		
3	Sustainable Livelihood Development	90.38																		
4	Community Infrastructure Development	20.11																		
Total		164.47																		
VIII.	The quarrying material required for the construction purpose should be obtained only from the approved quarries/borrow areas. Adequate safeguards measures shall be taken to ensure that the overburden and rocks at the quarry site do not find their way in water bodies.	<p>Complied</p> <p>Construction of terminal is completed, and terminal is in operation.</p>																		
IX.	For employing unskilled, semi-skilled and skilled workers for the project, preference should be given to local people.	<p>Complied.</p> <p>AECTPL has considered local people during construction phase & also during Operation Phase through Contracts.</p>																		
X.	The recommendations made in the EMP and DMP, as contained in the EIA and RA reports of the projects shall be effectively implemented.	<p>Status by KPL.</p>																		

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

**Half yearly Compliance report on conditions stipulated in CRZ & Environmental Clearance
[File no: 10-28/2005- IA.III dated: 19/05/2006]**

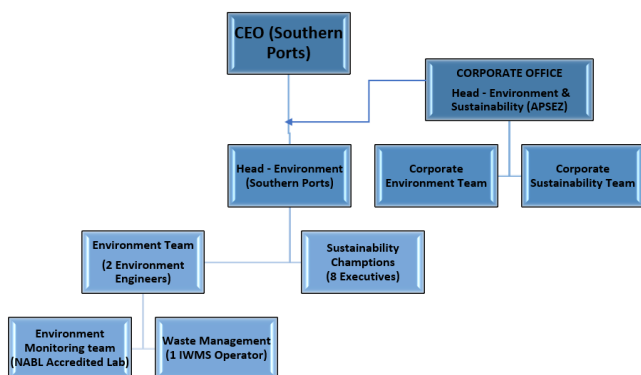S. No.	Conditions	Compliance Status
XI.	A separate EMC with suitable qualified staff to carry out various environment should be set up under the charge of a Senior Executive who will report directly to Chief Executive of the Company.	<p>Complied.</p> <p>A separate EMC with suitable qualified staff has been put in place by AECTPL for taking care of various day-to-day Environmental monitoring compliance and allied activities. Environment Department is headed by Deputy General Manager – Environment, who is reporting directly to Chief Executive Officer of the company. He is well supported by Environment Management Team at H.O.</p> <p>ENVIRONMENT TEAM - ORGANOGRAM</p>  <pre> graph TD CEO[CEO (Southern Ports)] --> HEnv[Head - Environment (Southern Ports)] CEO --> CO[CORPORATE OFFICE Head - Environment & Sustainability (APSEZ)] CO --> CET[Corporate Environment Team] CO --> CST[Corporate Sustainability Team] HEnv --> ET[Environment Team (2 Environment Engineers)] HEnv --> SC[Sustainability Champions (8 Executives)] ET --> EMT[Environment Monitoring team (NABL Accredited Lab)] ET --> WM[Waste Management (1 IWMS Operator)] </pre>

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

**Half yearly Compliance report on conditions stipulated in CRZ & Environmental Clearance
[File no: 10-28/2005- IA.III dated: 19/05/2006]**

S. No.	Conditions	Compliance Status																					
XII.	The funds earmarked for environment protection measures should be maintained in a separate account and there should be no diversion of these funds for any other purpose. A year-wise expenditure on environmental safeguards should be reported to this Ministry.	<p>Complied</p> <p>Separate budget for the Environment Protection is earmarked every year. All the expenses are recorded in advanced accounting system of the organization. Expenditure for Environment Management measures during January 2023 to June 2023 is Rs. 19.25 Lakhs. The breakup details are as follows;</p> <table> <tr> <th>S.No</th><th>Description</th><th>Amount (Rs in Lakhs)</th></tr> <tr> <td>1</td><td>Environmental Monitoring</td><td>6.97</td></tr> <tr> <td>2</td><td>Greenbelt</td><td>2.44</td></tr> <tr> <td>3</td><td>STP – O&M</td><td>2.38</td></tr> <tr> <td>4</td><td>Housekeeping</td><td>4.22</td></tr> <tr> <td>5</td><td>Integrated Waste Management</td><td>3.26</td></tr> <tr> <td colspan="2">Total</td><td>19.25</td></tr> </table>	S.No	Description	Amount (Rs in Lakhs)	1	Environmental Monitoring	6.97	2	Greenbelt	2.44	3	STP – O&M	2.38	4	Housekeeping	4.22	5	Integrated Waste Management	3.26	Total		19.25
S.No	Description	Amount (Rs in Lakhs)																					
1	Environmental Monitoring	6.97																					
2	Greenbelt	2.44																					
3	STP – O&M	2.38																					
4	Housekeeping	4.22																					
5	Integrated Waste Management	3.26																					
Total		19.25																					
XIII.	Full support should be extended to the officers of the Ministry's Regional office at Bangalore and the officer of the Central and SPCB by the project proponent during this inspection for monitoring purposes, by furnishing full details and action plans including the action plans including the action taken reports in respect if mitigative measures and other environmental protection activities.	<p>Noted for compliance.</p> <p>Full support is being extended to the officers of IRO, MoEF & CC, Chennai, CPCB & TNPCB during their inspection and site visit. During the compliance period monthly visits were made by TNPCB Officials and all the necessary supports were extended and the same shall be continued in future also.</p>																					

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

**Half yearly Compliance report on conditions stipulated in CRZ & Environmental Clearance
[File no: 10-28/2005- IA.III dated: 19/05/2006]**

S. No.	Conditions	Compliance Status
XIV.	In case there is an intension of deviation or alternation in the project including the implementing agency, a fresh reference should be made to this Ministry for modification in the clearance conditions or imposition of new ones for ensuring environmental protection. The project proponents should be responsible for implementing the suggested safeguard measures.	Noted for compliance
XV.	The Ministry reserves right to revoke this clearance, if any of the conditions stipulated are not compiled with to the satisfaction of this Ministry.	Noted.
XVI.	This Ministry or any other competent authority may stipulate additional conditions subsequently, if deemed necessary for environmental protection, which shall be complied with.	Noted for Compliance

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

**Half yearly Compliance report on conditions stipulated in CRZ & Environmental Clearance
[File no: 10-28/2005- IA.III dated: 19/05/2006]**

S. No.	Conditions	Compliance Status
XVII.	The project proponent should advertise at least in two local newspapers widely circulated in the region around the project, one of which shall be in the vernacular language of the locality concerned available with the SPCB and may also be seen at Website of the Ministry of Environment & Forests at http://www.envforenic.in . The advertisement should be made within 7 days from the date of issue of the clearance letter and a copy of the same should be forwarded to the Regional Office of the Ministry at Bangalore.	Status by KPL.
XVIII.	The project proponents should inform the RO as well as the Ministry the date of financial closure and final approval of the project by the concerned authorities and the date of start of Land Development Work.	Status by KPL.

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

Half yearly Compliance report on conditions stipulated in CRZ & Environmental Clearance
[Vide order no: 10-28/2005-IA-III dated: 10/09/2007 and validity extension date: 31.03/2017]

A. SPECIFIC CONDITIONS:

S.No	Environmental Clearance conditions	Compliance Status
i	It should be ensured that no mangroves are destroyed during reclamation.	Status by KPL.
ii	The proposed extension to the project should not cause any shoreline change abutting Ennore Port.	Status by KPL.
iii	Adequate provision for beach nourishment and sand bypass should be provided.	Status by KPL.
iv	The dredged material obtained should be utilized for filling up of back up area.	Status by KPL.
v	All conditions stipulated in the environmental clearance letter of even number dated 19.05.2006 should be strictly complied with.	Complied All stipulated conditions applicable to AECTPL in the environmental clearance letter of even number dated 19.05.2006 are being complied and compliance reports are regularly submitted to KPL. Last compliance report for the period July 2022 to December 2022 was submitted to KPL vide letter No. AECTPL/ENV/ KPL / HYC / 2023 / 03 dated 30.01.2023.
vi	The additional dredged material of 4 million cu. Mts. obtained from the project should not be disposed of into the sea.	Status by KPL.
vii	The reclaimed area should be used as containers stack yard only.	Status by KPL.


Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

S.No	Environmental Clearance conditions	Compliance Status
viii	Adequate drainage facilities should be provided in the reclaimed area along with collection and treatment system for treating the run off from the container stack yards.	Status by KPL.
ix	Necessary approvals/clearances should be obtained from the Tamil Nadu Coastal Zone Management Authority and Tamil Nadu Pollution Control Board before implementing the project.	Complied TNCZMA recommendation was obtained by KPL. Tamil Nadu Pollution Control Board accorded Renewal of Consent to Operate orders vide their order nos: 2108136876855 & 2108236876855 under Water and Air Acts dated: 24.08.2021 valid till 31.03.2026

B. GENERAL CONDITIONS:

S.No	Environmental Clearance conditions	Compliance Status
i	Construction of the proposed structures should be undertaken meticulously confirming to the existing Central/ local rules and regulations including Coastal Regulation Zone Notification 1991 & its amendments. All the construction design drawings relating to the proposed construction activities must have approvals of the concerned State Government Departments / Agencies.	Status by KPL.
ii	Adequate provisions for infrastructure facilities such as water supply, fuel, sanitation etc. should be ensured for construction workers during the construction phase of the project so as to avoid felling of trees/ Mangroves and pollution of water and the surroundings.	Complied. Construction of container terminal was completed and project is in operation phase.

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

S.No	Environmental Clearance conditions	Compliance Status
iii	<p>The project authorities must make necessary arrangements for disposal of solid wastes and for the treatment of effluents by providing a proper wastewater treatment plant outside the CRZ area. The quality of treated effluents, solid wastes and noise level etc. must conform to the standards laid down by the competent authorities including the Central/State Pollution Control Board and the Union Ministry of Environment and Forests under the Environment (Protection) Act, 1986, whichever are more stringent.</p>	<p>Complied</p> <p>AECTPL has installed and operating 25 KLD sewage treatment plant to collect and treat the sewage generated from the terminal. The entire treated sewage water is reused for green belt maintenance within the port premises after confirming permissible limit. Inlet & outlet characteristic of Sewage water is regularly monitored and analysed by NABL accredited laboratory.</p>  <p>AECTPL has implemented Integrated Waste Management System (IWMS) - Waste Segregation Yard.</p> <p>All the Solid waste generated is being handled in line to Solid Waste Management Rules, 2016 as amended. AECTPL vision is based on adoption of 5R principle of waste management i.e Reduce, Reuse, Reprocess, Recycle & Recover. All waste is being handled inline to 5R principle.</p>

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

S.No	Environmental Clearance conditions	Compliance Status
iv	The proponent shall obtain the requisite consents for discharge of effluents and emission under the Water (Prevention and Control of Pollution) Act, 1974 and the Air (Prevention and Control of Pollution) Act, 1981 from the Tamil Nadu Pollution control Board before commissioning of the project and a copy of each of these shall be sent to this Ministry.	<p>Complied</p> <p>Tamil Nadu Pollution Control Board accorded Renewal of Consent to Operate orders vide their order nos: 2108136876855 & 2108236876855 under Water and Air Acts dated: 24.08.2021 valid till 31.03.2026</p>
v	The proponent shall provide for a regular monitoring mechanism so as to ensure that the treated effluents conform to the prescribed standards. The records of analysis reports must be properly maintained and made available for inspection to the concerned State/Central officials during their visits.	<p>Complied</p> <p>AECTPL has awarded Environmental Monitoring services to NABL accredited laboratory. Monitoring of Ambient Air Quality, Noise, Stack, STP, Drinking Water, Marine Surface Water, Sea Sediment is carried out on regular basis. The reports are being submitted to KPL and Tamil Nadu Pollution Control Board on monthly basis and also as part of Six monthly compliance report. Environment Monitoring report for the period January 2023 – June 2023 is attached as Annexure - I.</p> <p>Reports are made available for inspection to the concerned State/Central officials during their visits.</p>
vi	In order to carry out the environmental monitoring during the operational phase of the project, the project authorities should provide an environmental laboratory well equipped with standard equipment and facilities and qualified manpower to carry out the testing of various environmental parameters.	<p>Complied</p> <p>Environmental Monitoring is being carried out through NABL accredited laboratory. Monitoring of Ambient Air Quality, Noise, Stack, STP, Drinking Water, Marine Surface Water, Sea Sediment is carried out on regular basis.</p> <p>The reports are being submitted to KPL and Tamil Nadu Pollution Control Board on monthly basis and also as part of Six monthly compliance reports. Environment Monitoring report for the period January 2023 – June 2023 is attached as Annexure - I.</p>

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

S.No	Environmental Clearance conditions	Compliance Status																					
vii	The sand dunes and mangroves, if any, on the site should not be disturbed in any way.	Status by KPL.																					
viii	A copy of the clearance letter will be marked to the concerned Panchayat/Local NGO, if any from whom any suggestion/representation has been received while processing the proposal.	Status by KPL.																					
ix	The Tamil Nadu Pollution Control Board should display a copy of the clearance letter at the Regional Office, District Industries Centre and Collector's Office/Tehsildar's Office for 30 days.	Status by KPL.																					
x	The funds earmarked for environment protection measures should be maintained in a separate account and there should be no diversion of these funds for any other purpose. A year wise expenditure on environmental safeguards should be reported to this Ministry's Regional Office at Bangalore and the State Pollution Control Board.	Complied Environmental Expenditure carried out during January 2023 – June 2023 is Rs. 19.25 Lakhs. Breakup details are as follows; <table border="1"> <thead> <tr> <th>S.No</th><th>Description</th><th>Amount (Rs in Lakhs)</th></tr> </thead> <tbody> <tr> <td>1</td><td>Environmental Monitoring</td><td>6.97</td></tr> <tr> <td>2</td><td>Greenbelt</td><td>2.44</td></tr> <tr> <td>3</td><td>STP – O&M</td><td>2.38</td></tr> <tr> <td>4</td><td>Housekeeping</td><td>4.22</td></tr> <tr> <td>5</td><td>Integrated Waste Management System</td><td>3.24</td></tr> <tr> <td align="right" colspan="2">Total</td><td>19.25</td></tr> </tbody> </table>	S.No	Description	Amount (Rs in Lakhs)	1	Environmental Monitoring	6.97	2	Greenbelt	2.44	3	STP – O&M	2.38	4	Housekeeping	4.22	5	Integrated Waste Management System	3.24	Total		19.25
S.No	Description	Amount (Rs in Lakhs)																					
1	Environmental Monitoring	6.97																					
2	Greenbelt	2.44																					
3	STP – O&M	2.38																					
4	Housekeeping	4.22																					
5	Integrated Waste Management System	3.24																					
Total		19.25																					

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

S.No	Environmental Clearance conditions	Compliance Status
xi	Full support should be extended to the officers of this Ministry's Regional office at Bangalore and the officers of the Central and State Pollution Control Boards by the project proponents during their inspection for monitoring purposes, by furnishing full details and action plans including the action taken reports in respect of mitigative measures and other environmental protection activities.	Noted for compliance. TNPCB Officials have visited our Port on monthly basis. There was no visit of officials from RO-MoEF&CC and CPCB during the compliance period. All the necessary support is provided during their site visit.
xii	In case of deviation or alteration in the project including the implementing agency, a fresh reference should be made to this Ministry for modification in the clearance conditions or imposition of new ones for ensuring environmental protection.	Noted.
xiii	This Ministry reserve the right to revoke this clearance, if any of the conditions stipulated are not complied with to the satisfaction of this Ministry.	Noted.
xiv	This Ministry or any other component authority may stipulate any other additional conditions subsequently, if deemed necessary, for environmental protection, which shall be complied with.	Noted.

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

S.No	Environmental Clearance conditions	Compliance Status
xv	The project proponent should advertise at least in two local newspapers widely circulated in the region around the project, one of which shall be in the vernacular language of the locality concerned informing that the project has been accorded environmental clearance and copies of clearance letters are available with the State Pollution Control Board and may also be seen at Website of the Ministry of Environment & Forests at http://www.envfornic.in . The advertisement should be made within 7 days from the date of issue of the clearance letter and a copy of the same should be forwarded to the regional Office of this Ministry at Bangalore.	Status by KPL.
xvi	The Project proponents should inform the Regional Office at Bangalore as well as the Ministry the date of financial closure and final approval of the project by the concerned authorities and the date of start of Land Development Work.	Status by KPL.

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

**Half yearly Compliance report on conditions stipulated in CRZ & Environmental Clearance
[Vide order no: 10-28/2005-IA-III dated: 24/12/2014]**

A. SPECIFIC CONDITIONS:

S.No	Environmental Clearance conditions	Compliance Status
i	"Consent to Establish" for the present project, shall be obtained from State Pollution Control Board under Air (Prevention and Control of Pollution) Act, 1981 and Water (Prevention and Control of Pollution) Act 1974.	Complied. Tamil Nadu Pollution Control Board accorded Renewal of Consent to Operate orders vide their order nos: 2108136876855 & 2108236876855 under Water and Air Acts dated: 24.08.2021 valid till 31.03.2026.
ii	Quality of Cargo should be handled in accordance with the details provided in the Form-I.	Complied. AECTPL is handling only containerized cargo, as approved.
iii	All the recommendations and conditions stipulated by Tamil Nadu Coastal Zone Management Authority (TNCZMA) No. 30060/EC.3/2005-1 dated 06.12.2005 shall be complied with.	Status by KPL.
iv	All the conditions as prescribed in the earlier Clearance letter no. 10-28/2005-IA-III dated 19.05.2006 and 10.09.2007 shall be complied with.	Status by KPL.
v	All the recommendation of the EIA/EMP & Risk Assessment and Disaster Management Report shall be complied with letter and spirit. All the mitigation measures submitted in the EIA report shall be prepared in the matrix format and the compliance for each mitigation plan shall be submitted to MoEF & CC along with half yearly compliance report to MoEF&CC- RO.	Status by KPL.

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

vi	The commitment made by the proponent to the issue raised during Public Hearing shall be implemented by the Proponent.	Status by KPL.
vii	<p>Corporate Environmental Responsibility:</p> <p>a. The Company shall have a well laid down Environmental Policy approved by the Board of Directors.</p> <p>b. The Environment Policy shall prescribe for standard operating process/procedures to bring into focus any infringements/deviation/violation of the environmental or forest norms/conditions.</p> <p>c. The hierarchical system or Administrative Order of the company to deal with environmental issues and for ensuring compliance with the environmental clearance conditions shall be furnished.</p> <p>d. To have proper checks and balances, the company shall have a well laid down system of reporting of non-compliances / violations of environmental norms to the Board of Directors of the company and / or shareholders or stakeholders at large.</p>	<p>a. AECTPL having approved QHSE policy.</p> <p>b. AECTPL having approved SOPs.</p> <p>c. Status by KPL.</p> <p>d. Standard procedures are made available to address corrective & preventive deviation and violations.</p>

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

B. GENERAL CONDITIONS:

S.No	Environmental Clearance conditions	Compliance Status
i	Appropriate measures must be taken while undertaking digging activities to avoid any likely degradation of water quality.	Complied Construction completed and project is under operation.
ii	Full support shall be extended to the officers of the Ministry/Regional Office at Chennai by the project proponent during inspection of the project for monitoring purposes by furnishing full details and action plan including action taken reports in respect of mitigation measures and other environmental protection activities.	Noted for compliance. TNPCB Officials have visited our Port on monthly basis. There was no visit of officials from RO-MoEF&CC and CPCB during the compliance period. All the necessary support is provided during their site visit.
iii	A six-Monthly monitoring report shall be need to be submitted by the project proponents to the Regional Office of this Ministry at Chennai regarding the implementation of the stipulated conditions.	Status by KPL.
iv	Ministry of Environment, Forests & Climate Change or any other competent authority may stipulate any additional conditions or modify the existing ones, if necessary in the in the interest of environment and the same shall be complied with.	Noted for compliance.
v	The Ministry reserves the rights to revoke this clearance if any of the conditions stipulated are not complied with satisfaction of the Ministry.	Noted.
vi	In the event of a change in project profile or change in the	Noted.

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

	implementation agency, a fresh reference shall be made to the Ministry of Environment, Forests & Climate Change.																						
vii	The project proponents shall inform the Regional Office as well as the Ministry, the date of financial closure and final approval of the project by the concerned authorities and the date of start of land development work.	Noted.																					
viii	A copy of the clearance letter shall be marked to concerned Panchayat/ Local NGO, if any, from whom any suggestion/ representation has been made received while processing the proposal.	Status by KPL.																					
ix	The project proponent shall set up separate environmental management cell for effective implementation of the stipulated environmental safeguards under the supervision of a Senior Executive.	Complied. A separate EMC with suitable qualified staff has been put in place by AECTPL for taking care of various day to day Environmental monitoring, compliance and allied activities. Environment Department is headed by Senior Manager – Environment, reporting directly to Chief Executive Officer. EMC is well supported by Environment Management Cell, HO.																					
x	The funds earmarked for environment management plan shall be included in the budget and this shall not be diverted for any other purposes.	Complied Environmental Expenditure carried out during January 2023 – June 2023 is Rs. 19.25 Lakhs. Breakup details are as follows; <table border="1"> <thead> <tr> <th>S.No</th><th>Description</th><th>Amount (Rs in Lakhs)</th></tr> </thead> <tbody> <tr> <td>1</td><td>Environmental Monitoring</td><td>6.97</td></tr> <tr> <td>2</td><td>Greenbelt</td><td>2.44</td></tr> <tr> <td>3</td><td>STP – O&M</td><td>2.38</td></tr> <tr> <td>4</td><td>Housekeeping</td><td>4.22</td></tr> <tr> <td>5</td><td>Integrated Waste Management System</td><td>3.24</td></tr> <tr> <td colspan="2">Total</td><td>19.25</td></tr> </tbody> </table>	S.No	Description	Amount (Rs in Lakhs)	1	Environmental Monitoring	6.97	2	Greenbelt	2.44	3	STP – O&M	2.38	4	Housekeeping	4.22	5	Integrated Waste Management System	3.24	Total		19.25
S.No	Description	Amount (Rs in Lakhs)																					
1	Environmental Monitoring	6.97																					
2	Greenbelt	2.44																					
3	STP – O&M	2.38																					
4	Housekeeping	4.22																					
5	Integrated Waste Management System	3.24																					
Total		19.25																					

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

5.	These stipulations would be enforced among others under the provisions of Water (Prevention and Control of Pollution) Act, 1974, the Air (Prevention and Control of Pollution) Act, 1981, the Environment (Protection) Act, 1986, the Public Liability (Insurance) Act, 1991 and EIA Notification 1994, including the amendments and rules made thereafter.	Noted.
6.	All other statutory clearances such as the approvals for storage of diesel from Chief Controller of Explosives, Fire Department, Civil Aviation Department, Forest conservation Act, 1980 and Wildlife (Protection) Act, 1972 etc. shall be obtained, as applicable by project proponents from the respective competent authorities.	Noted.
7.	The project proponent shall advertise at least in two local newspapers widely circulated in the region around the project, one of which shall be in the vernacular language of the locality concerned informing that the project has been accorded Environmental and CRZ clearance and copies of clearance letters are available with the Tamil Nadu State Pollution Control Board and may also be seen at Website of the Ministry of Environment, Forests and Climate Change at http://www.envforin.in . The advertisement should be made within Seven days from the date of issue of the clearance letter and a copy of the same should be forwarded to the regional Office of this Ministry at Chennai.	Status by KPL.

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

8.	The clearance is subject to final order of the Hon'ble Supreme Court of India in the matter of Goa Foundation Vs. Union of India in Writ Petition (Civil) No. 460 of 20014 as may be applicable this project.	Noted.
9.	Any appeal against this clearance shall lie with the National Green Tribunal, if preferred, with a period of 30 days as prescribed under Section 16 of the National Green Tribunal Act 2010.	Noted.
10.	Status of compliance to the various stipulated environment conditions and environmental safeguards will be uploaded by the project proponent in its website.	Complied. The compliance to the various conditions stipulated for environmental safeguards are uploaded in our Company website and KPL website. https://www.adaniports.com/Downloads and https://ennoreport.gov.in/content/innerpage/environment.php
11.	A copy of the clearance letter shall be sent by the proponent to concerned Panchayat, Zilla Parisad /Municipal Corporation, Urban Local Body and the Local NGO, if any, from whom suggestions/representations, if any, were received while processing the proposal. The clearance letter shall also be put on the website of the company by the proponent.	Status by KPL.
12.	The proponent shall upload the status of compliance of the stipulated Clearance conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent to the Reginal Office of MoEF, the respective Zonal Office of CPCB and the SPCB.	Status by KPL. The compliance to the various conditions stipulated for environmental safeguards are uploaded in our Company website and KPL website.

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

13.	The project proponent shall also submit six monthly reports on the status of compliance of the stipulated Clearance conditions including results of monitored data (both in hard copies as well as by e-mail) to the respective Regional Office of MoEF, the respective Zonal Office of CPCB and the SPCB.	Status by KPL.
14.	The Environmental Statement for each financial year ending 31 st March in Form-V as is mandated to be submitted by the project proponent to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company along with the status of compliance of Clearance conditions and shall also be sent to the respective Regional Office of MoEF & CC by email.	Complied. Environment Statement (Form V) submitted FY 2021-22 vide our Letter No. AECTPL/TNPCB/2022-23/128 dated 22.09.2022 is enclosed as Annexure – II.

Name of the Project: Ennore Port Expansion Proposals – Development of Terminals for Marine Liquids, Coal, Iron and Containers in Second Phase and associated capital dredging at Ennore Port Environment Clearance.

Enclosures:

Annexure Number	Details of Annexure
Annexure I:	Environmental Monitoring reports for the period January 2023 to June 2023
Annexure II:	Environmental Statement – Form V for the FY 2021-22

ANNEXURE – 1

(Environment Monitoring Report Jan'23 – Jun'23)

REPORT ON
COMPREHENSIVE ENVIRONMENTAL MONITORING
FOR
ADANI ENNORE CONTAINER TERMINAL PRIVATE LIMITED
(AECTPL) (WITHIN KAMARAJAR PORT LIMITED)
VALLUR POST, PONNERI TALUK,
CHENNAI -600120



JANUARY TO JUNE 2023

Index for Table

S. No	Index	Page No
I.	Introduction	
II.	Location of the project	
III.	Scope of work	
IV.	Methodology	
V.	Environmental studies	
i.	Meteorological Data	
ii.	Ambient Air Quality	
iii.	Ambient Noise Level Intensity	
iv.	DG Set Emission	
v.	STP Water Sample Analysis	
vi.	Drinking water Sample Analysis	
vii.	Marine sampling	

List of Figures

Fig. No	Description
1	Location Map
2	Ambient Air Sampling Station Location Map
3	Ambient Air Sampling Station with respect to Wind
4	Noise Level Sampling Location Map
5	Water and Marine Sampling Location Map

I. INTRODUCTION

M/s. Adani Ennore Container Terminal Pvt Ltd (AECTPL) located inside Kamarajar Port, Ennore is operating container berth and handling containerized Import/Export cargoes.

AECTPL have engaged M/s. Green Chem Solutions (P) Ltd, an Accredited Consultant by NABL to carry out the Comprehensive Environmental monitoring studies in the AECTPL continuously as per the statutory requirement. This report covers the monitored environmental data for the month of January to June 2023.

II. LOCATION OF THE PROJECT

The Project site is located at Port area inside the Kamarajar Port Limited.

The location map is shown in Fig - 1

Fig - 1 - Location Map



III. SCOPE OF WORK

The scope of Comprehensive Environmental monitoring includes the following environmental components.

- | | |
|------------------------|-------------------------|
| 1. Meteorological data | 2. Ambient Air Quality. |
| 3. Ambient Noise Level | 4. Marine Sampling |
| 5. Treated STP Water | 6. Portable Water |
| 7. DG Set emission | |

The parameters covered under the scope for each of the above attributes are given below:

SCOPE OF WORK

S. No	Attribute	Scope	Frequency
1.	Meteorological Data	Collection of micrometeorological data on hourly basis by installing an auto weather monitoring station at plant site covering the following parameters: <ul style="list-style-type: none"> • Wind speed • Wind direction • Rainfall • Relative Humidity • Temperature • Barometric pressure • Solar Radiation 	Daily
2.	Ambient Air Quality	Sampling of ambient air at 03 stations for analyzing the following parameters: <ul style="list-style-type: none"> • PM10 • PM2.5 • SO2 • NO2 • CO • Lead • Ozone • Ammonia • Benzene • Benzo Pyrene • Arsenic • Nickel 	Weekly Twice
3.	Ambient Noise	Collection of Noise levels on hourly basis at 3 locations <ul style="list-style-type: none"> • Leq - Day (Max and Min) • Leq - Night (Max and Min) 	Monthly Once
4.	Marine sampling		
4a.	Surface and Bottom Water	Collection of Surface and Bottom Water analyzed for -1location <ul style="list-style-type: none"> • Temperature • pH @ 25 °C • Total Suspended Solids • BOD at 27 °C for 3 days • Dissolved oxygen • Salinity at 25 °C 	

		<ul style="list-style-type: none"> • Oil & Grease • Nitrate as NO_3 • Nitrite as NO_2 • Ammoniacal Nitrogen as N • Total phosphates as PO_4 • Total Nitrogen, • COD • Turbidity • Total Iron as Fe • Colour • Odour • Mercury as Hg • Cadmium as Cd • Total Chromium as Cr • Copper as Cu • Lead as Pb • Nickel as Ni • Iron • Zinc • Particulate Organic Carbon • Petroleum Hydrocarbons 	
4b.	Sea Sediment	<p>Collection of sea sediment analyzed for - 2 location</p> <ul style="list-style-type: none"> • pH • Organic Matter • Moisture Content • Conductivity • Iron • Sodium • Copper • Nickel • Zinc • Manganese • Lead • Boron • Phosphate • Chloride • Sulphate • Sulphide • Pesticide • Potassium • Total Chromium • Petroleum Hydrocarbon • Aluminium • Total Nitrogen • Organic Nitrogen • Phosphorus 	

		<ul style="list-style-type: none"> Texture 	
4c.	Phytoplankton Monitoring	<ul style="list-style-type: none"> Total Count No. of species Chlorophyll-a Major Species 	Monthly Once
4d.	Zooplankton Monitoring	<ul style="list-style-type: none"> Total Count No. of species Major 	Monthly Once
4e.	Microbiological Monitoring	<ul style="list-style-type: none"> Total Bacteria count Total Coliform Faecal Coliform E.Coli Enterococcus Salmonella Sheigella Vibrio Cholera Vibrio parahaemolyticus 	Monthly Once
4f.	Primary Productivity Monitoring	<ul style="list-style-type: none"> Gross primary productivity Net Primary productivity 	Monthly Once
4g.	Phytobenthos Monitoring data	<ul style="list-style-type: none"> Fungus Total Count No. of species Diversity Index Major species 	Monthly Once
4h.	Total Fauna Monitoring	<ul style="list-style-type: none"> Name of phylum Class Number of Individuals encountered Total no. of species encountered Total fauna 	Monthly Once
5	STP Treated Water	Collection of STP Treated water analyzed for - 1 locations <ul style="list-style-type: none"> pH TSS BOD Faecal Coliforms 	Monthly Once
6	Potable Water analysis	Collection of Drinking water analyzed for - 1 location - As per IS 10500 2012 - 36 Parameters	Monthly Once
7	DG Set Emissions	Sampling of Emission at 03 stations for analyzing the following parameters: <ul style="list-style-type: none"> PM Carbon Monoxide NOx - NO2 SO2 	Monthly Once

IV. METHODOLOGY

Methodologies adopted for sampling and analysis for each of the above parameters are detailed below.

1	Meteorological parameters	
	Auto weather station	
2	Ambient Air Quality	
	Parameters	Method
	Respirable Suspended Particulate Matter (PM10)	IS5182 Part23:2006(Reaff.2017)
	Particulate Matter PM2.5	IS5182 Part24:2019
	Sulphur di-oxide as SO ₂	IS5182 Part02:2001(Reaff.2017)
	Oxides of Nitrogen as NO ₂	IS5182 Part06:2006(Reaff.2017)
	Lead as Pb	IS5182 Part22:2004(Reaff.2019)
	Arsenic as As	GCS/Lab/SOP/089, CPCB Guidelines
	Nickel as Ni	IS5182 Part26:2020
	Carbon monoxide as CO	IS5182 Part10:1999(Reaff.2019)
	Ozone as O ₃	IS5182 Part09:1974(Reaff.2017)
	Ammonia as NH ₃	IS5182 Part25:2018
	Benzene (α) pyrene	IS5182 Part12: 2004 (Reaff.2017)
	Benzene as C ₆ H ₆	IS5182 Part11:2006(Reaff.2019)
3	Ambient Noise Monitoring	
	L _{eq} Day& Night	Instrument Manual, GCS/LAB/SOP/Noise/001
4	Marine Sampling	
	Surface and Bottom Water	APHA Methods 23 rd Edition, 2017 Standard Methods for examination of Water and Wastewater and IS 3025 & USEPA Test Methods
	Sea Sediment	
	Phytoplankton Monitoring	
	Zooplankton Monitoring	
	Microbiological Monitoring	
	Primary Productivity Monitoring	
	Phyto benthos Monitoring data	
Total Fauna Monitoring		
5	STP Water Analysis	
	pH, TSS, BOD, Faecal Coliforms	APHA Methods 23 rd Edition, 2017 Standard Methods for examination of Water and Wastewater and IS 3025
6	Emission Monitoring	
	PM, Carbon Monoxide, NO _x - NO ₂ , SO ₂	IS 11255 Methods of measurement of emissions from Stationary source

S.No	ATTRIBUTE	SCOPE
1.	Meteorological parameters	Collection of micrometeorological data at project site on daily basis with hourly frequency
2.	Ambient Air Quality	Collection of ambient air at 3 locations.
3.	STP water	Collection of STP Inlet and outlet water at one location
4.	Ambient Noise	Collection of Ambient noise levels for day and night at 3 locations
5.	Marine Water and Marine Sediments	Collection of Marine water and Marine Sediments at One location
6.	DG Set Emissions	Collection of DG Set Emission at 4 locations.

i. METEOROLOGICAL DATA

Meteorological data was collected on hourly basis by installing an auto weather monitoring station at Plant site. The report depicted hereunder presents the data for January to June 2023.

The following parameters were recorded.

- Wind speed
- Wind direction
- Temperature
- Pressure
- Relative humidity
- Rainfall

January 2023

Date	Ambient Temperature (oC)			Atmospheric Pressure (mbar)			Predominant Wind Direction (Blowing from)	Wind Speed (m/s)			Relative Humidity (%)			Rainfall (mm)
	Min	Max	Avg	Min	Max	Avg		Min	Max	Avg	Min	Max	Avg	
01.01.2023	-	-	-	1004	1010	1007	E	0	10.8	2.46	-	-	-	0.0
02.01.2023	-	-	-	1004	1010	1007	E	0	10.8	2.56	-	-	-	0.0
03.01.2023	-	-	-	1004	1010	1007	E	0	13.3	3.47	-	-	-	0.0
04.01.2023	-	-	-	1009	1014	1011	NNE	0	22	6.58	-	-	-	0.0
05.01.2023	-	-	-	1004	1009	1006	E	0	19.8	7.95	-	-	-	0.0
06.01.2023	-	-	-	1005	1011	1008	NNE	0.36	20.5	7.29	-	-	-	0.0
07.01.2023	-	-	-	1010	1004	1007	NNE	0	18.9	7.39	-	-	-	0.0
08.01.2023	-	-	-	1004	1009	1006	NNE	0	17.8	5.11	-	-	-	0.0
09.01.2023	-	-	-	1005	1010	1007	NNE	0	15.8	5.95	-	-	-	0.0
10.01.2023	-	-	-	1004	1010	1007	NNE	0	15.8	6.63	-	-	-	0.0
11.01.2023	-	-	-	1002	1008	1005	NNE	0	13.9	4.2	-	-	-	0.0
12.01.2023	-	-	-	1001	1007	1004	W	0	13	2.97	-	-	-	0.0
13.01.2023	-	-	-	1002	1009	1006	E	0	9.72	1.44	-	-	-	0.0
14.01.2023	26	34.25	30.77	1004	1010	1007	E	0	16	2.86	67.6	99.9	82	0.0
15.01.2023	25.4	33.65	30.11	1003	1009	1006	E	0	11.2	2.21	72.2	99.9	85.8	0.0
16.01.2023	25.8	34	30.49	1004	1010	1007	E	0	12.6	3.44	71.5	99.9	85.4	0.0
17.01.2023	30.8	34.5	32.6	1005	1010	1008	E	0	11.2	4.34	69.2	80.5	75.4	0.0
18.01.2023	27	34.6	31.37	1006	1012	1009	E	0	13	3.68	69.6	99.9	82.5	0.0
19.01.2023	-	-	-	1006	1012	1009	NNE	0	10.8	3.31	-	-	-	0.0
20.01.2023	28.2	34.5	31.39	1005	1011	1008	E	0	15.8	4.19	84.4	99.9	93.8	0.0
21.01.2023	31.3	35.4	32.62	1005	1010	1007	E	0.54	16.9	6.72	75.7	96.9	88.2	0.0
22.01.2023	31	35	32.31	1004	1010	1007	E	0.18	20.2	5.69	73.9	90.4	83.4	0.0
23.01.2023	31.1	35.25	32.43	1003	1009	1006	E	0	19.8	6.32	78.3	94.6	89.4	0.0
24.01.2023	31.35	34.9	32.54	1004	1009	1006	E	0	14.8	5.64	70.8	94.1	83.3	0.0
25.01.2023	31.7	35	33.05	1004	1008	1006	E	0	13.5	5.57	70.5	86.3	78.5	0.0
26.01.2023	27.2	34.2	31.41	1004	1009	1006	NNE	0	17.3	5.74	76.6	99.9	89.3	0.0
27.01.2023	27.5	34.85	31.95	1003	1009	1006	NNE	0	13.3	4.09	71.3	99.9	82.7	0.0
28.01.2023	27.4	33.75	31.07	1003	1009	1006	NNE	0	16.2	5.85	86.6	99.9	95.3	0.0
29.01.2023	29.4	35.5	32.55	1001	1007	1004	E	0	20.2	6.32	80.5	99.9	92.3	0.0
30.01.2023	31.6	35.7	33.08	1003	1008	1005	E	0	19.8	6.91	84.3	99.9	95.2	0.0
31.01.2023	31.7	35.3	32.67	1002	1008	1005	NNE	1.08	21.1	9.8	85.5	99.9	97.1	0.0

Remark: Temp sensor problem in 01.01.2023 to 13.01.2023

February 2023

Date	Ambient Temperature (oC)			Atmospheric Pressure (mbar)			Predominant Wind Direction (Blowing from)	Wind Speed (m/s)			Relative Humidity (%)			Rainfall (mm)
	Min	Max	Avg	Min	Max	Avg		Min	Max	Avg	Min	Max	Avg	
01.02.2023	30.5	34.7	32.6	1002	1007	1005	NNE	0	23	10	88.6	99.9	96.8	0.0
02.02.2023	32.2	34.8	32.9	1003	1008	1005	NNE	0	22.1	8.7	83.7	98.5	91	0.0
03.02.2023	28.6	35.4	31.4	1002	1009	1006	NEN	0	18.4	6.3	70	99.4	85	0.0
04.02.2023	27.8	31.7	29.1	1002	1007	1005	NNE	0	15.1	5.1	63	75.1	69.7	0.0
05.02.2023	23.8	31.2	28.2	1002	1007	1005	E	0	11.5	3.3	62.3	88.9	72.3	0.0
06.02.2023	23.8	31.5	27.8	1002	1008	1005	E	0	13.5	3.2	67.4	90.7	78.5	0.0
07.02.2023	24.0	31.9	28.2	1002	1008	1005	ESE	0	14.4	4.3	64.4	93.7	76.2	0.0
08.02.2023	23.9	30.8	27.9	1002	1008	1005	E	0	11.5	3	61.5	90.8	71.9	0.0
09.02.2023	23.6	31.2	27.5	1003	1008	1006	ESE	0	14	2.7	60.8	87.8	73.5	0.0
10.02.2023	23.4	31.5	27.9	1003	1009	1006	ESE	0	12.8	3.7	57.1	89.6	71.9	0.0
11.02.2023	23.5	31.0	27.4	1004	1010	1007	E	0	12.2	2.8	60.7	86	74.8	0.0
12.02.2023	22.9	32.3	27.3	1004	1010	1007	WSW	0	11	3.4	59.8	92.8	76	0.0
13.02.2023	22.2	31.2	27.2	1004	1010	1007	East	0	13.7	3.5	62.6	91.1	76.2	0.0
14.02.2023	22.8	30.9	27.4	1003	1010	1007	East	0	13	4.2	62.2	90.9	76.9	0.0
15.02.2023	23.1	31.1	27.7	1003	1008	1005	East	0	14	3.9	67.6	91.2	77.9	0.0
16.02.2023	23.3	31.0	27.6	1003	1009	1006	ESE	0	13.3	2.7	64.4	95.6	77.3	0.0
17.02.2023	23.4	31.5	25.6	1004	1009	1006	W	0	8.28	1.3	62	93.2	84.9	0.0
18.02.2023	23.0	32.1	26.4	1005	1010	1007	ESE	0	10.8	1.8	64.7	92.9	81.4	0.0
19.02.2023	25.0	31.8	28.3	1005	1010	1007	ESE	0	14	3.5	65.6	92.4	78.8	0.0
20.02.2023	23.6	31.8	28.4	1004	1009	1006	ESE	0	15.5	4	63.2	94.2	75.1	0.0
21.02.2023	23.6	32.7	28.2	1004	1009	1006	WSW	0	16.6	4.9	58.6	92.7	76.1	0.0
22.02.2023	24.2	33.0	28.4	1003	1009	1006	ESE	0	11.9	3.5	52.7	96.6	77.3	0.0
23.02.2023	23.4	31.5	28.2	1003	1009	1006	ESE	0	15.8	4.8	64	94.5	76.1	0.0
24.02.2023	24.2	33.3	28.4	1004	1010	1007	ESE	0	16.9	4.1	59.2	94.4	75.3	0.0
25.02.2023	23.4	31.4	27.6	1005	1011	1008	E	0	14	3.3	66.7	95	78.9	0.0
26.02.2023	23.7	31.8	27.9	1007	1012	1009	E	0	13.5	3.4	64.9	95.7	79.1	0.0
27.02.2023	23.3	32.1	28.0	1007	1013	1010	W	0	14.9	4.6	65.6	96	80	0.0
28.02.2023	24.8	32.7	29.3	1007	1013	1009	E	0	14	4.8	69.5	93.9	79.5	0.0

March 2023

Date	Ambient Temperature (oC)			Atmospheric Pressure (mbar)			Predominant Wind Direction (Blowing from)	Wind Speed (m/s)			Relative Humidity (%)			Rainfall (mm)
	Min	Max	Avg	Min	Max	Avg		Min	Max	Avg	Min	Max	Avg	
01.03.2023	28.6	32.9	30.7	1007	1012	1010	E	1.1	17.6	5.8	66.4	77.8	72.3	0.0
02.03.2023	24.5	32.6	29.6	1007	1013	1010	E	0.0	13.0	4.5	60.3	92	70.2	0.0
03.03.2023	24.0	32.5	28.9	1007	1013	1010	NNE	0.0	13.9	3.6	57.2	91.8	73.9	0.0
04.03.2023	27.1	31.9	29.5	1007	1013	1010	E	0.0	13.3	4.0	66.9	84.1	75.4	0.0
05.03.2023	25.3	32.2	29.2	1007	1013	1009	NNE	0.0	15.8	4.7	74.4	97.7	83.9	0.0
06.03.2023	24.3	32.1	28.8	1005	1011	1008	WNW	0.0	10.8	2.9	70.0	99.9	83.6	0.0
07.03.2023	24.9	32.3	29.2	1005	1010	1008	E	0.0	12.2	4.1	66.9	97	78	0.0
08.03.2023	26.0	32.4	29.7	1005	1010	1007	E	0.0	17.8	5.6	66.8	90.5	77.8	0.0
09.03.2023	28.1	32.4	29.9	1004	1010	1007	E	0.0	15.1	5.0	70.6	85.8	78.9	0.0
10.03.2023	25.9	32.5	29.4	1003	1009	1006	E	0.0	14.8	4.0	67.5	98.7	80.8	0.0
11.03.2023	28.5	33.0	30.2	1004	1009	1006	E	0.0	15.8	5.5	67.8	84.6	76.7	0.0
12.03.2023	25.2	32.9	29.6	1003	1009	1006	E	0.0	15.5	4.7	74.4	99.4	85.5	0.0
13.03.2023	25.8	32.6	29.4	1002	1008	1005	E	0.0	14.4	4.0	76.8	99.9	88.5	0.0
14.03.2023	25.3	32.0	28.8	1001	1007	1004	E	0.0	10.8	3.0	58.5	99.9	83.6	0.0
15.03.2023	26.4	33.5	30.1	1001	1006	1003	W	0.0	17.3	3.9	59.3	84.4	71.8	0.0
16.03.2023	29.1	34.3	31.0	1001	1007	1004	ESE	0.0	17.6	4.8	59.5	79.5	71.1	0.0
17.03.2023	25.4	33.6	29.7	1003	1009	1006	E	0.0	23.0	4.7	63.9	99.9	88.4	0.0
18.03.2023	29.0	34.3	30.9	1002	1008	1005	ESE	0.0	19.4	3.8	84.5	99.9	96	0.0
19.03.2023	26.9	33.4	29.7	1001	1008	1004	WNW	0.0	8.8	2.2	83.6	99.9	97.1	0.0
20.03.2023	26.1	34.1	29.7	1001	1007	1004	WSW	0.0	14.9	2.8	81.6	99.9	96.6	0.0
21.03.2023	27.6	34.6	30.7	1001	1006	1004	W	0.0	8.5	2.0	87.8	99.9	97.1	0.0
22.03.2023	29.1	34.9	31.4	1001	1008	1004	WSW	0.0	9.7	2.7	83.6	99.9	96.8	0.0
23.03.2023	28.2	33.9	30.9	1002	1007	1004	WSW	0.0	9.5	2.3	91.3	99.9	99.2	0.0
24.03.2023	27.3	34.9	30.9	1002	1007	1005	WSW	0.0	17.8	3.4	84.5	99.9	95.9	0.0
25.03.2023	29.7	34.5	31.5	1004	1008	1006	WSW	0.0	11.5	2.8	88.3	99.9	96.7	0.0
26.03.2023	28.6	34.8	31.4	1002	1008	1005	WSW	0.0	12.2	2.6	83.1	99.9	96.2	0.0
27.03.2023	29.2	34.7	31.6	1002	1007	1004	WSW	0.0	13.3	3.8	83.1	99.9	95.8	0.0
28.03.2023	29.5	34.6	31.5	1002	1007	1005	WSW	0.0	11.3	3.2	88.0	99.9	96.7	0.0
29.03.2023	29.2	35.0	31.5	1004	1009	1006	WSW	0.0	11.9	3.2	79.6	99.9	93.1	0.0
30.03.2023	28.1	34.6	31.2	1002	1008	1005	WSW	0.0	15.8	3.4	79.1	99.9	92.8	0.0
31.03.2023	27.9	34.8	31.2	1001	1007	1004	WSW	0.0	15.8	3.4	80.5	99.9	93.7	0.0

April 2023

Date	Ambient Temperature (oC)			Atmospheric Pressure (mbar)			Predominant Wind Direction (Blowing from)	Wind Speed (m/s)			Relative Humidity (%)			Rainfall (mm)
	Min	Max	Avg	Min	Max	Avg		Min	Max	Avg	Min	Max	Avg	
01.04.2023	29.0	35.2	31.6	1001	1007	1004	WSW	0.0	19.1	4.5	79.4	99.9	95.9	0.0
02.04.2023	30.3	34.9	32.1	1001	1007	1004	WSW	0.0	14.8	4.3	84.6	99.9	96.1	0.0
03.04.2023	30.3	35.5	32.1	1002	1006	1004	WSW	0.0	21.6	4.1	83.1	99.9	95.2	0.0
04.04.2023	30.2	35.7	32.1	1003	1008	1005	WSW	0.0	17.6	4.3	81.1	99.9	94.6	0.0
05.04.2023	29.7	35.4	32.0	1002	1007	1005	WSW	0.0	12.2	3.4	82.3	99.9	95.8	0.0
06.04.2023	29.6	35.8	32.1	1002	1008	1005	WSW	0.0	11.7	3.2	80.3	99.9	94.6	0.0
07.04.2023	28.3	35.1	31.7	1005	1010	1007	WSW	0.0	15.1	3.1	80.4	99.9	92.9	0.0
08.04.2023	27.8	34.3	31.4	1006	1011	1009	E	0.0	14.8	4.3	81.6	99.9	90.8	0.0
09.04.2023	30.2	33.8	31.7	1007	1012	1009	E	0.0	12.6	4.3	82.1	95.8	89.8	0.0
10.04.2023	29.9	34.1	31.6	1005	1010	1007	ESE	0.0	14.8	4.4	78.5	99.9	91.1	0.0
11.04.2023	26.5	33.9	30.7	1005	1009	1007	WSW	0.0	13.3	2.9	82.5	99.9	94.4	0.0
12.04.2023	26.4	36.5	31.2	1004	1009	1006	WSW	0.0	12.1	2.6	65.3	99.9	91.0	0.0
13.04.2023	26.4	36.2	31.4	1003	1008	1006	WSW	0.0	9.5	2.7	64.8	99.9	04:31	0.0
14.04.2023	26.9	36.8	31.6	1002	1008	1005	WSW	0.0	10.4	3.4	68.9	99.9	91.9	0.0
15.04.2023	26.6	36.7	31.6	1003	1008	1005	WSW	0.0	10.8	2.2	73.6	99.9	93.4	0.0
16.04.2023	27.3	36.8	31.7	1001	1006	1003	WSW	0.0	9.9	2.9	74.2	99.9	93.5	0.0
17.04.2023	27.2	37.2	31.8	1002	1006	1004	WSW	0.0	10.1	3.1	68.3	99.9	92.0	0.0
18.04.2023	27.1	35.5	31.4	1003	1008	1005	WSW	0.0	10.1	3.1	83.2	99.9	95.3	0.0
19.04.2023	27.6	36.8	31.9	999	1006	1003	WSW	0.0	14.8	3.3	78.1	99.9	94.6	0.0
20.04.2023	29.8	38.9	32.8	997	1003	1000	WSW	0.0	23.8	5.3	58.6	99.9	93.1	0.0
21.04.2023	30.5	37.4	33.0	998	1003	1000	SW	0.0	20.2	4.0	76.3	99.9	94.8	0.0
22.04.2023	30.5	36.4	32.6	999	1004	1001	WSW	0.0	9.7	2.6	85.4	99.9	97.6	0.0
23.04.2023	30.9	36.1	32.9	998	1005	1001	WSW	0.0	12.2	4.1	85.2	99.9	96.6	0.0
24.04.2023	28.0	36.1	31.7	1001	1006	1003	WSW	0.0	22.5	3.3	83.3	99.9	97.6	0.0
25.04.2023	30.9	36.2	32.7	1000	1006	1004	ESE	0.0	16.9	3.0	82.9	99.9	95.2	0.0
26.04.2023	29.8	34.6	31.8	1000	1006	1004	ESE	0.0	14.4	4.1	88.3	99.9	97.7	0.0
27.04.2023	28.8	35.7	32.2	1001	1006	1003	ESE	0.0	14.4	2.5	84.2	99.9	95.7	0.0
28.04.2023	29.2	36.0	32.4	1000	1007	1004	W	0.0	16.2	3.7	84.2	99.9	95.4	0.0
29.04.2023	29.2	36.2	32.3	1000	1006	1003	WSW	0.0	13.1	2.4	83.5	99.9	96.2	0.0
30.04.2023	28.8	36.3	32.2	998	1004	1002	WSW	0.0	14.8	3.7	75.9	99.9	93.9	0.0

May 2023

Date	Ambient Temperature (oC)			Atmospheric Pressure (mbar)			Predominant Wind Direction (Blowing from)	Wind Speed (m/s)			Relative Humidity (%)			Rainfall (mm)
	Min	Max	Avg	Min	Max	Avg		Min	Max	Avg	Min	Max	Avg	
01.05.2023	26.5	33.2	30.35	999	1005	1002	E	0	0.87	4.61	87.9	99.9	98.2	26.0
02.05.2023	26.3	32.9	29.11	1000	1006	1003	WSW	0	12.2	0.88	90.8	99.9	99.5	52 mm
03.05.2023	28	32.8	30.27	1000	1006	1003	West	0	18	0.79	90.8	99.9	98.9	0.0
04.05.2023	28.7	33.95	31.3	999	1004	1002	ESE	0	13.3	2.92	89.6	99.9	97.4	0.0
05.05.2023	27.9	35.2	30.91	999	1004	1001	WSW	0	14.6	3.39	80.4	99.9	96.7	0.0
06.05.2023	28.1	33.8	30.95	998	1003	1001	SW	0	12.2	2.43	95.3	99.9	85.3	0.0
07.05.2023	28.7	33.9	31.13	997	1003	1000	WSW	0	12.6	4.45	90.9	99.9	97.4	0.0
08.05.2023	27.4	34.8	31.12	997	1001	1000	ESE	0	15.5	4.23	82.2	99.9	96.3	0.0
09.05.2023	28.9	34.8	31.99	997	1002	1000	ESE	0	16.4	4.43	80.7	99.9	95.2	0.0
10.05.2023	29.5	35.1	32.21	997	1002	1000	WSW	0	12.2	3.44	79.7	99.9	94.9	0.0
11.05.2023	28.9	34.8	31.53	998	1002	1000	WSW	0	15.1	1.96	83.8	99.9	98	0.0
12.05.2023	29.8	38.6	33.22	996	1001	999	WSW	0	11.3	2.93	64.1	99.9	93.7	0.0
13.05.2023	31.3	39.75	34.85	996	1001	999	SW	0	20.2	7.71	63.9	99.9	84.8	0.0
14.05.2023	32.1	40.75	34.97	994	1000	997	WSW	0	21.6	6.18	57.9	99.9	83.2	0.0
15.05.2023	31.4	39.7	34.34	996	1001	999	SW	0	18	4.61	63.4	99.9	91.4	0.0
16.05.2023	31.7	40.6	34.66	998	1002	1000	SW	0	19.4	5.53	60.2	99.9	91.5	0.0
17.05.2023	31.35	36.5	33.7	999	1005	1002	SW	0	14.6	4.79	86.9	99.9	96	0.0
18.05.2023	31.1	36.9	32.96	1000	1005	1003	WSW	0	16.6	4.07	86.2	99.9	97	0.0
19.05.2023	31.15	36.5	33	999	1004	1002	WSW	0	20	4.03	83.1	99.9	94.4	0.0
20.05.2023	30.6	36.6	32.8	998	1003	1001	WSW	0	14.9	3.78	86.1	99.9	96.6	0.0
21.05.2023	29.2	35.3	32.09	999	1004	1002	WSW	0	18.7	3.77	85.8	99.9	98.2	0.0
22.05.2023	30.6	35.95	32.52	16.7	841	253	W	0	11.5	3.36	87	99.9	97.6	0.0
23.05.2023	30.4	36.25	32.8	1000	1006	1003	WSW	0	10.6	3.1	80.5	99.9	94.8	0.0
24.05.2023	31.2	37.3	33.19	999	1005	1002	SW	0	22	4.53	76	99.9	92.7	0.0
25.05.2023	31.4	38.1	32.97	999	1004	1002	SW	0	16.4	4.34	66.9	99.9	91.1	0.0
26.05.2023	31.5	39.25	33.45	1000	1004	1002	SW	0	30.2	6.97	61.6	99.9	88.1	0.0
27.05.2023	30.3	39.7	34.17	998	1002	1000	SW	0	17.6	4.86	62.2	99.9	86.2	0.0
28.05.2023	30.3	39.6	33.4	997	1002	1000	SW	0	18.7	4.03	61.2	99.9	92.2	0.0
29.05.2023	31.4	37.8	33.74	998	1004	1000	WSW	0	13.9	2.8	73.5	99.9	94	0.0
30.05.2023	28.2	36.85	32.23	999	1004	1002	WSW	0	23.2	3.56	82.4	99.9	95.3	0.0

June 2023

Date	Ambient Temperature (oC)			Atmospheric Pressure (mbar)			Predominant Wind Direction (Blowing from)	Wind Speed (m/s)			Relative Humidity (%)			Rainfall (mm)
	Min	Max	Avg	Min	Max	Avg		Min	Max	Avg	Min	Max	Avg	
01.06.2023	29.0	36.4	31.1	--	896	279	SW	0	14.2	3.6	74.0	99.9	0.3	0.0
02.06.2023	32.8	39.8	35.0	996	1001	998	SW	0	14.4	3.9	64.2	99.9	88.1	0.0
03.06.2023	32.3	39.3	34.9	996	1000	998	WSW	0	14.9	3.5	66.5	99.9	91.1	0.0
04.06.2023	31.5	40.6	34.3	996	1000	998	SW	0	20.5	5.0	60.9	99.9	88.6	0.0
05.06.2023	31.7	41.5	35.4	995	1001	998	WSW	0	19.1	4.8	54.3	99.9	83.4	0.0
06.06.2023	31.1	39.7	34.3	996	1000	998	SW	0	19.4	5.4	59.6	99.9	81.0	0.0
07.06.2023	30.1	42.7	34.7	994	999	997	WSW	0	21.1	7.9	52.2	99.9	80.9	0.0
08.06.2023	29.8	39.2	33.4	994	1001	998	SW	0	18.4	5.7	66.0	99.9	90.3	0.0
09.06.2023	32.0	40.4	34.3	995	999	997	WSW	0	15.7	5.5	54.7	99.9	84.6	0.0
10.06.2023	31.3	39.4	34.4	994	998	996	WSW	0	22.0	6.3	61.0	99.9	82.2	0.0
11.06.2023	31.2	39.7	33.9	994	999	996	SW	0	22.5	6.5	59.8	96.5	82.0	0.0
12.06.2023	30.5	40.0	33.6	994	999	996	WSW	0	31.5	6.0	57.3	96.9	81.6	0.0
13.06.2023	30.7	40.6	33.9	993	999	996	SW	0	23.0	6.5	59.8	99.9	88.5	0.0
14.06.2023	30.4	40.8	34.1	994	999	997	WSW	0	17.8	6.3	60.3	97.6	84.2	0.0
15.06.2023	29.9	39.8	33.5	996	1000	998	WSW	0	30.4	6.5	57.9	99.9	87.4	0.0
16.06.2023	30.9	40.8	34.4	995	1000	998	WSW	0	14.8	4.4	57.3	99.9	84.7	0.0
17.06.2023	31.5	39.1	34.6	994	999	997	WSW	0	15.1	5.0	62.0	99.9	87.1	0.0
18.06.2023	31.6	36.2	33.3	996	1000	998	WSW	0	14.8	5.2	69.7	99.9	88.3	0.5
19.06.2023	26.9	30.7	28.6	995	1001	997	SW	0	24.3	9.2	89.9	99.9	99.5	0.5
20.06.2023	27.1	34.4	30.8	994	998	996	SW	0	28.4	10.0	82.3	99.9	94.2	0.5
21.06.2023	26.6	33.7	30.1	996	1000	998	SW	0	16.7	4.2	85.2	99.9	98.0	0.0
22.06.2023	29.2	35.6	31.9	996	1000	998	SW	0	12.1	2.9	78.6	99.9	96.3	0.0
23.06.2023	29.9	35.4	32.0	996	1000	998	SW	0	17.6	4.0	80.5	99.9	95.2	0.0
24.06.2023	25.7	36.2	31.6	996	1000	998	WSW	0	28.3	3.8	76.9	99.9	94.5	0.0
25.06.2023	30.6	35.3	32.1	996	999	998	SW	0	15.5	5.3	77.6	99.9	92.6	0.0
26.06.2023	30.0	35.1	32.2	995	1000	998	WSW	0	16.6	3.9	79.1	99.9	93.6	0.0
27.06.2023	30.0	36.5	32.9	996	1001	998	SW	0	17.6	5.1	70.4	99.9	88.9	0.0
28.06.2023	30.1	37.3	32.8	997	1002	999	WSW	0	15.8	5.6	66.9	99.9	88.9	0.0
29.06.2023	30.0	37.5	33.0	997	1002	1000	WSW	0	23.4	6.3	68.8	99.9	90.5	0.0
30.06.2023	28.7	37.5	32.2	996	1002	1000	WSW	0	16.6	5.3	69.0	98.5	88.4	0.0

METEOROLOGICAL DATA

Meteorological data was collected on hourly basis by installing an auto weather monitoring station at Plant site. The report depicted hereunder presents the data for Mar - 2023.

The following parameters were recorded.

- Wind speed
- Wind direction
- Temperature
- Pressure
- Relative humidity
- Rainfall

WIND PATTERN Jan to Jun 2023

Marine Infrastructure Developer Pvt Ltd


Report Type: Wind Rose Report- Static Details and Interval: min | Time Range: 2023-01-01 00:00:00 to 2023-06-30 23:59:43 | Station Name: AQMS

Average Wind Speed :4.36 km/h | Average Wind Direction:181.99 Degree| Calm: 11.33 %| Blowing From: North

Report Created by Marine on 2023-07-06 11:19:08

Direction	0 - 5	5 - 10	10 - 15	15 - 20	20 - 25	25 - 30	30 - 35	Summary	Min	Max	Avg
N	0.47	0.38	0.15	0.02	0	0	0	1.02	0	0.47	0.15
NNE	1.38	2.23	0.89	0.12	0	0	0	4.62	0	2.23	0.66
NE	2.09	1.87	0.28	0.02	0	0	0	4.26	0	2.09	0.61
ENE	3.21	2.7	0.29	0.02	0	0	0	6.22	0	3.21	0.89
E	5.31	4.92	0.64	0.03	0	0	0	10.9	0	5.31	1.56
ESE	4.47	3.62	0.51	0.03	0	0	0	8.63	0	4.47	1.23
SE	2.04	1.01	0.16	0.01	0	0	0	3.22	0	2.04	0.46
SSE	1.69	0.51	0.03	0	0	0	0	2.23	0	1.69	0.32
S	1.84	0.88	0.22	0.02	0	0	0	2.96	0	1.84	0.42
SSW	2.1	1.17	0.24	0.03	0	0	0	3.54	0	2.1	0.51
SW	5.46	4.16	1.06	0.17	0.03	0	0	10.88	0	5.46	1.55
WSW	7.93	3.78	0.8	0.11	0.01	0	0	12.63	0	7.93	1.8
W	6.19	1.89	0.22	0.02	0	0	0	8.32	0	6.19	1.19
WNW	4.33	1.08	0.09	0.01	0	0	0	5.51	0	4.33	0.79
NW	2.03	0.52	0.05	0.01	0	0	0	2.61	0	2.03	0.37
NNW	0.84	0.25	0.03	0	0	0	0	1.12	0	0.84	0.16

Fig -1. Windrose diagram for Jan to Jun 2023.

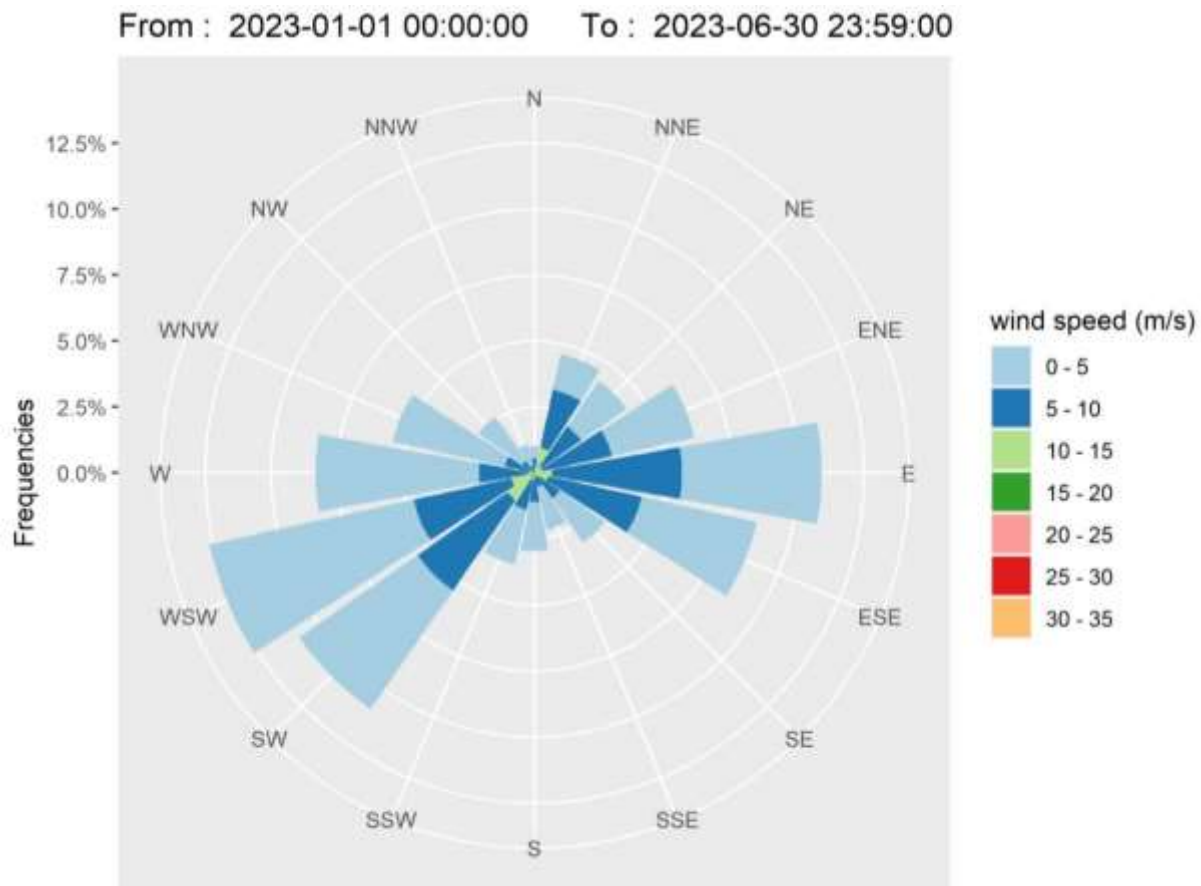

AMBIENT AIR QUALITY

Ambient air quality monitoring is required to determine the existing quality of air, evaluation of the effectiveness of control system and to identify areas in need of restoration and their prioritization. In order to generate background data, air quality monitoring is conducted to assess existing level of contamination and to assess possible effects of air contamination occurring in future.

Frequency of Monitoring

The frequency of monitoring that has been followed for sampling of ambient air quality is that one sample per weekly twice at three locations.

DETAILS OF AMBIENT AIR QUALITY MONITORING LOCATIONS

Station code	Location	Geographical location	Environmental setting
AAQ1	Port operating building	13° 16' 12" N 80° 20' 5" E	Industrial
AAQ2	RMU Building	13° 16' 25" N 80° 20' 16" E	Industrial
AAQ3	In Terminal Gate	13° 16' 25" N 80° 20' 0" E	Industrial

Fig - 6. AMBIENT AIR SAMPLING STATION LOCATION MAP



Fig.3.AMBIENT AIR SAMPLINGS STATIONS WITH RESPECT TO WIND



TECHNIQUES USED FOR AMBIENT AIR QUALITY MONITORING

S. No	Parameter	Technique	Unit	Minimum Detectable Limit
1	PM ₁₀	Respirable Dust Sampler (Gravimetric method)	µg/m ³	1.0
2	PM _{2.5}	Fine particle Sampler (Gravimetric method)	µg/m ³	5.0
3	Sulphur Dioxide	Modified West and Gaeke method	µg/m ³	4.0
4	Nitrogen Oxide	Jacob & Hochheiser method	µg/m ³	6.0
5	Lead	Atomic Absorption Spectrometry	µg/m ³	0.5
6	Carbon Monoxide	Draggers Tube	mg/m ³	0.1
7	Ozone	UV Photometric	µg/m ³	2.0
8	Ammonia	Indophenol blue method	µg/m ³	2.0
9	Benzene	Gas Chromatography	µg/m ³	1.0
10	Benzene (α) pyrene	Gas Chromatography	ng/m ³	0.1
11	Arsenic	Atomic Absorption Spectrometry	ng/m ³	1.0
12	Nickel	Atomic Absorption Spectrometry	ng/m ³	5.0

Results and Discussion

The results of the ambient air quality for the study period are presented and discussed. The minimum, maximum 98th percentile and average values have been computed from the observed raw data for all the AAQ monitoring stations. The summary of these results for all the locations is presented in the Table and the detailed analytical results are shown in Annexure - 2. These are compared with the standards prescribed by Central Pollution Control Board (CPCB) for “Industrial, Rural, Residential and other areas”.

Annexure 1 Summary of Ambient Air Quality Status

January - 2023

Parameters		AAQ-1	AAQ-2	AAQ-3	Std*
PM ₁₀	Minimum	42.0	43.0	53.0	100
	Maximum	61.0	58.0	53.0	
	98th percentile	60.4	57.9	61.9	
	Average	53.3	57.9	61.9	
PM _{2.5}	Minimum	15.0	14.0	19.0	60
	Maximum	28.0	28.0	27.0	
	98th percentile	27.7	27.7	26.9	
	Average	21.5	20.0	22.4	
SO ₂	Minimum	5.40	4.90	6.10	80
	Maximum	7.70	7.90	8.60	
	98th percentile	7.67	7.86	8.60	
	Average	6.58	6.55	7.71	
NO ₂	Minimum	14.50	14.10	15.70	80
	Maximum	17.8	18.0	18.6	
	98th percentile	17.7	17.94	18.57	
	Average	16.54	16.25	17.55	
CO mg/m3	Result	BDL (DL:1.0)	BDL (DL:1.0)	BDL (DL:1.0)	4.0
NH3	Result	BDL (DL: 2.0)	BDL (DL: 2.0)	BDL (DL: 2.0)	400
Ozone	Result	BDL (DL: 2.0)	BDL (DL: 2.0)	BDL (DL: 2.0)	180
Pb	Result	BDL (DL:0.5)	BDL (DL:0.5)	BDL (DL:0.5)	1.0
C6H6	Result	BDL (DL: 1.0)	BDL (DL: 1.0)	BDL (DL: 1.0)	5.0
All the values are expressed in ng/m3					
Benzene (a) pyrene	Result	BDL (DL: 0.1)	BDL (DL: 0.1)	BDL (DL: 0.1)	1
As	Result	BDL (DL: 1.0)	BDL (DL: 1.0)	BDL (DL: 1.0)	6
Ni	Result	BDL (DL: 5.0)	BDL (DL: 5.0)	BDL (DL: 5.0)	20
AAQ1: PORT OPERATING BUILDING, AAQ2: RMU BUILDING, AAQ3: IN TERMINAL GATE					

February -2023

Parameters		AAQ-1	AAQ-2	AAQ-3	Std*
PM ₁₀	Minimum	45	47	52	100
	Maximum	60	62	65	
	98th percentile	59.9	61.7	64.7	
	Average	54.4	54.0	58.9	
PM _{2.5}	Minimum	15	17	19	60
	Maximum	31	24.0	26.0	
	98th percentile	30.7	23.7	25.9	
	Average	22.6	20.1	23.1	
SO ₂	Minimum	4.50	5.40	6.90	80
	Maximum	7.50	7.40	8.20	
	98th percentile	7.44	7.36	8.17	
	Average	6.28	6.56	7.59	
NO ₂	Minimum	15.70	13.90	14.90	80
	Maximum	17.50	17.40	17.80	
	98th percentile	17.49	17.37	17.79	
	Average	16.46	16.33	16.54	
CO mg/m3	Result	BDL (DL:1.0)	BDL (DL:1.0)	BDL (DL:1.0)	4.0
NH3	Result	BDL (DL: 2.0)	BDL (DL: 2.0)	BDL (DL: 2.0)	400
Ozone	Result	BDL (DL: 2.0)	BDL (DL: 2.0)	BDL (DL: 2.0)	180
Pb	Result	BDL (DL:0.5)	BDL (DL:0.5)	BDL (DL:0.5)	1.0
C6H6	Result	BDL (DL: 1.0)	BDL (DL: 1.0)	BDL (DL: 1.0)	5.0
All the values are expressed in ng/m3					
Benzene (α) pyrene	Result	BDL (DL: 0.1)	BDL (DL: 0.1)	BDL (DL: 0.1)	1
As	Result	BDL (DL: 1.0)	BDL (DL: 1.0)	BDL (DL: 1.0)	6
Ni	Result	BDL (DL: 5.0)	BDL (DL: 5.0)	BDL (DL: 5.0)	20
AAQ1: PORT OPERATING BUILDING, AAQ2: RMU BUILDING, AAQ3: IN TERMINAL GATE					

March -2023

Parameters		AAQ-1	AAQ-2	AAQ-3	Std*
PM ₁₀	Minimum	43.0	50.0	47.0	100
	Maximum	61.0	65.0	63.0	
	98th percentile	60.6	64.9	62.7	
	Average	52.5	55.4	57.1	
PM _{2.5}	Minimum	17.0	18.0	21.0	60
	Maximum	30.0	27.0	28.0	
	98th percentile	29.6	26.7	27.6	
	Average	23.8	21.6	23.4	
SO ₂	Minimum	5.1	5.3	6.2	80
	Maximum	7.8	7.0	8.1	
	98th percentile	7.72	6.99	8.09	
	Average	6.39	6.21	7.20	
NO ₂	Minimum	15.0	13.7	13.1	80
	Maximum	17.9	17.2	17.5	
	98th percentile	17.84	17.14	17.43	
	Average	16.44	15.58	15.78	
CO mg/m3	Result	BDL (DL:1.0)	BDL (DL:1.0)	BDL (DL:1.0)	4.0
NH3	Result	BDL (DL: 2.0)	BDL (DL: 2.0)	BDL (DL: 2.0)	400
Ozone	Result	BDL (DL: 2.0)	BDL (DL: 2.0)	BDL (DL: 2.0)	180
Pb	Result	BDL (DL:0.5)	BDL (DL:0.5)	BDL (DL:0.5)	1.0
C6H6	Result	BDL (DL: 1.0)	BDL (DL: 1.0)	BDL (DL: 1.0)	5.0
All the values are expressed in ng/m3					
Benzene (α) pyrene	Result	BDL (DL: 0.1)	BDL (DL: 0.1)	BDL (DL: 0.1)	1
As	Result	BDL (DL: 1.0)	BDL (DL: 1.0)	BDL (DL: 1.0)	6
Ni	Result	BDL (DL: 5.0)	BDL (DL: 5.0)	BDL (DL: 5.0)	20
AAQ1: PORT OPERATING BUILDING, AAQ2: RMU BUILDING, AAQ3: IN TERMINAL GATE					

April -2023

Parameters		AAQ-1	AAQ-2	AAQ-3	Std*
PM ₁₀	Minimum	49.0	50.0	48.0	100
	Maximum	63.0	63.0	62.0	
	98th percentile	62.6	62.7	61.9	
	Average	55.0	57.0	56.8	
PM _{2.5}	Minimum	20.0	18.0	19.0	60
	Maximum	31.0	33.0	32.0	
	98th percentile	30.6	32.6	31.9	
	Average	25.1	26.1	26.1	
SO ₂	Minimum	5.1	5.2	5.3	80
	Maximum	7.5	7.1	7.0	
	98th percentile	7.47	7.07	6.97	
	Average	6.43	6.18	6.24	
NO ₂	Minimum	13.8	13.1	14.2	80
	Maximum	17.8	16.6	16.6	
	98th percentile	17.67	16.57	16.59	
	Average	15.95	15.13	15.68	
CO mg/m3	Result	BDL (DL:1.0)	BDL (DL:1.0)	BDL (DL:1.0)	4.0
NH3	Result	BDL (DL: 2.0)	BDL (DL: 2.0)	BDL (DL: 2.0)	400
Ozone	Result	BDL (DL: 2.0)	BDL (DL: 2.0)	BDL (DL: 2.0)	180
Pb	Result	BDL (DL:0.5)	BDL (DL:0.5)	BDL (DL:0.5)	1.0
C6H6	Result	BDL (DL: 1.0)	BDL (DL: 1.0)	BDL (DL: 1.0)	5.0
All the values are expressed in ng/m3					
Benzene (α) pyrene	Result	BDL (DL: 0.1)	BDL (DL: 0.1)	BDL (DL: 0.1)	1
As	Result	BDL (DL: 1.0)	BDL (DL: 1.0)	BDL (DL: 1.0)	6
Ni	Result	BDL (DL: 5.0)	BDL (DL: 5.0)	BDL (DL: 5.0)	20
AAQ1: PORT OPERATING BUILDING, AAQ2: RMU BUILDING, AAQ3: IN TERMINAL GATE					

May -2023

Continuous Ambient Air Quality Monitoring system data

Parameter	AQMS PM10 (ug/m3)	AQMS PM2.5 (ug/m3)	AQMS SO2 (ug/m3)	AQMS NO2 (ug/m3)	AQMS Benzene (ug/m3)
Prescribed Standard	100	60	80	80	5
Avg	30.85	13.86	4.88	12.46	0.2
Min	4.32	1.78	3.04	7.17	0
Max	53.95	29.45	5.81	19.74	5.78

June - 2023

Parameters		AAQ-1	AAQ-2	AAQ-3	Std*
PM ₁₀	Minimum	45.8	43.6	47.5	100
	Maximum	59.2	65.8	64.8	
	98th percentile	59.0	64.8	64.7	
	Average	52.6	53.6	56.6	
PM _{2.5}	Minimum	21.1	19.7	21.6	60
	Maximum	30.3	28.1	32.6	
	98th percentile	30.1	27.8	32.2	
	Average	25.3	23.3	26.0	
SO ₂	Minimum	5.5	4.8	5.1	80
	Maximum	8.1	7.8	6.6	
	98th percentile	8.0	7.7	6.6	
	Average	6.5	6.4	5.9	
NO ₂	Minimum	14.3	13.6	14.7	80
	Maximum	18.3	16.2	17.5	
	98th percentile	18.2	16.1	17.4	
	Average	15.9	15.0	16.0	
CO mg/m3	Result	BDL (DL:1.0)	BDL (DL:1.0)	BDL (DL:1.0)	4.0
NH3	Result	BDL (DL: 2.0)	BDL (DL: 2.0)	BDL (DL: 2.0)	400
Ozone	Result	BDL (DL: 2.0)	BDL (DL: 2.0)	BDL (DL: 2.0)	180
Pb	Result	BDL (DL:0.5)	BDL (DL:0.5)	BDL (DL:0.5)	1.0
C6H6	Result	BDL (DL: 1.0)	BDL (DL: 1.0)	BDL (DL: 1.0)	5.0
All the values are expressed in ng/m3					
Benzene (α) pyrene	Result	BDL (DL: 0.1)	BDL (DL: 0.1)	BDL (DL: 0.1)	1
As	Result	BDL (DL: 1.0)	BDL (DL: 1.0)	BDL (DL: 1.0)	6
Ni	Result	BDL (DL: 5.0)	BDL (DL: 5.0)	BDL (DL: 5.0)	20
AAQ1: PORT OPERATING BUILDING, AAQ2: RMU BUILDING, AAQ3: IN TERMINAL GATE					

**NATIONAL AMBIENT AIR QUALITY STANDARDS
CENTRAL POLLUTION CONTROL BOARD
NOTIFICATION**

New Delhi, the 18th November, 2009

No.B-29016/20/90/PCI-L—In exercise of the powers conferred by Sub-section (2) (h) of section 16 of the Air (Prevention and Control of Pollution) Act, 1981 (Act No. 14 of 1981), and in super session of the Notification No(s). S.O. 384(E), dated 11th April, 1994 and S.O. 935(E), dated 14th October, 1998, the Central Pollution Control Board hereby notify the National Ambient Air Quality Standards with immediate effect, namely:-

NATIONAL AMBIENT AIR QUALITY STANDARDS

S. No.	Pollutant	Time Weighted average	Concentration in Ambient Air		Methods of Measurement
			Industrial, Residential, Rural and Other Area	Ecologically sensitive area (notified by Central Govt.)	
(1)	(2)	(3)	(4)	(5)	(6)
1	Sulphur Dioxide (SO ₂), µg/m ³	Annual*	50	20	<ul style="list-style-type: none"> Improved West and Geake Ultraviolet fluorescence
		24 hours**	80	80	
2	Nitrogen Dioxide (NO ₂), µg/m ³	Annual*	40	30	<ul style="list-style-type: none"> Modified Jacob & Hochheiser (Na-Arsenite) Chemiluminescence
		24 hours**	80	80	
3	Particulate Matter (size less than 10 µm) or PM ₁₀ µg/m ³	Annual*	60	60	<ul style="list-style-type: none"> Gravimetric TOEM Beta attenuation
		24 hours**	100	100	
4	Particulate Matter (size less than 2.5 microns) or PM _{2.5} µg/m ³	Annual*	40	40	<ul style="list-style-type: none"> Gravimetric TOEM Beta attenuation
		24 hours**	60	60	
5	Ozone (O ₃) µg/m ³	8 hours **	100	100	<ul style="list-style-type: none"> UV photometric Chemiluminescence Chemical method
		1 hour **	180	180	
6	Lead (Pb) µg/m ³	Annual*	0.5	0.5	<ul style="list-style-type: none"> ASS / ICP method after sampling on EPM 2000 or equivalent filter paper ED – XRF using Teflon filter
		24 hours**	1.0	1.0	
7	Carbon Monoxide (CO) mg/m ³	8 hours**	2	2	Non Dispersive Infra RED (NDIR) Spectroscopy
		1 hour**	4	4	
8	Ammonia (NH ₃) µg/m ³	Annual*	100	100	<ul style="list-style-type: none"> Chemiluminescence Indophenol blue method
		24 hours**	400	400	
9	Benzene (C ₆ H ₆) µg/m ³	Annual*	5	5	<ul style="list-style-type: none"> Gas chromatography based continuous analyser Adsorption and desorption followed by GC analysis
10	Benzo (a) Pyrene (BaP) – particulate phase only ng/m ³	Annual*	1	1	Solvent extraction followed by HPLC / GC analysis
11	Arsenic (As) ng/m ³	Annual*	6	6	AAS / ICP method after sampling on EPM 2000 or equivalent filter paper
12	Nickel (Ni) ng/m ³	Annual*	20	20	AAS / ICP method after sampling on EPM 2000 or equivalent filter paper

* Annual arithmetic mean of minimum 104 measurements in a year at a particular site taken twice a week 24 hourly at uniform intervals.

** 24 hourly or 8 hourly or 1 hourly monitored values, as applicable, shall be complied with 98% of the time in a year. 2% of the time, they may exceed the limits but not on two consecutive days of monitoring.

Note: Whenever and wherever monitoring results on two consecutive days of monitoring exceed the limits specified above for the respective category, it shall be considered adequate reason to institute regular or continuous monitoring and further investigation.

i. **AMBIENT NOISE LEVEL INTENSITY**

Collection of ambient noise levels at four locations. Spot noise levels were measured with a pre-calibrated Noise Level Meter - SL- 4023 SD for day and night periods.

DETAILS OF NOISE MONITORING LOCATIONS

STATION CODE	LOCATIONS	GEOGRAPHICAL LOCATION	Environmental setting
N1	In Terminal Gate	13° 16' 25" N 80° 20' 0" E	Industrial
N2	RMU Building	13° 16' 25" N 80° 20' 16" E	Industrial
N3	Port operating building	13° 16' 12" N 80° 20' 5" E	Industrial

Fig - 9. Ambient Noise Level Monitoring Locations



The ambient noise levels monitored during the study period are given hereunder in form of Leq day, Leq night compared with CPCB Standards.

Annexure 2 Ambient Noise Level Monitoring Report Jan- Jun 2023

Location: 1 - In Terminal Gate

Location	In Terminal Gate					
Month	Jan	Feb	Mar	Apr	May	Jun
Unit	Leq dB(A)	Leq dB(A)	Leq dB(A)	Leq dB(A)	Leq dB(A)	Leq dB(A)
06.00 - 07.00 (Day)	64	65.2	62.4	60.7	-	60.1
07.00 -08.00	63.4	64.2	61.4	61.5	-	60.9
08.00 - 09.00	65.6	65.8	61.8	62	-	61.2
09.00 - 10.00	63.3	64.6	64.6	64.1	-	62.4
10.00 - 11.00	61.9	63.7	62.5	63.2	-	62.8
11.00 - 12.00	62.5	65.5	65.7	64.8	-	63.5
12.00 - 13.00	63	62	66.2	65.9	-	62.1
13.00 - 14.00	65	64.2	66	65.3	-	61.5
14.00 - 15.00	64.1	65.4	66.2	66.1	-	62.9
15.00 - 16.00	65.6	63.3	64	65.1	-	63.1
16.00 - 17.00	66.4	65.7	63.5	64.9	-	64.3
17.00 - 18.00	63.7	64.4	60.7	61.5	-	61.6
18.00 - 19.00	60.9	62.6	60.5	62.6	-	60.8
19.00 -20.00	63.8	63.4	64.9	61.4	-	61.4
20.00 - 21.00	62.4	65.2	65.2	64.4	-	62.3
21.00 - 22.00	61.2	63.5	62.3	63.8	-	60.7
22.00 - 23.00 (Night)	61.9	62.4	61.2	61.9	-	59.1
23.00 - 00.00	62.7	63.3	63.6	62.7	-	61.2
00.00 - 01.00	59.4	60.1	63.3	59.9	-	58.4
01.00 - 02.00	58.6	59.9	61.7	62.5	-	60.9
02.00 - 03.00	60.5	60.9	62.1	60.7	-	59.1
03.00 - 04.00	62	61.3	60.8	61.2	-	60.3
04.00 - 05.00	60.8	62.4	59.7	60.3	-	59.4
05.00 - 06.00	63.5	61.9	61.5	59.9	-	58.6

Location: 2 - RMU Building

Location	RMU Building					
Month	Jan	Feb	Mar	Apr	May	Jun
Unit	Leq dB(A)	Leq dB(A)	Leq dB(A)	Leq dB(A)	Leq dB(A)	Leq dB(A)
06.00 - 07.00 (Day)	56.8	60.4	62.6	63.1	-	61.2
07.00 - 08.00	60.7	61.6	60.7	61.4	-	60.1
08.00 - 09.00	56.7	59.8	61.9	61.8	-	60.9
09.00 - 10.00	60.4	61.7	63	62.9	-	61.8
10.00 - 11.00	60.4	62	64.2	64	-	62.5
11.00 - 12.00	58.3	60.8	61.1	63.5	-	61.9
12.00 - 13.00	59.5	58.7	59	62.2	-	63.6
13.00 - 14.00	56.6	59.4	59.5	61.3	-	62.4
14.00 - 15.00	55.8	57.8	57.8	63.8	-	61
15.00 - 16.00	57.7	59.4	60.2	62.6	-	63.1
16.00 - 17.00	56.6	60.4	61.3	61.3	-	62.7
17.00 - 18.00	55.8	62.1	63.1	62.4	-	61.3
18.00 - 19.00	55.5	59.9	62	63.1	-	62
19.00 - 20.00	56.7	58.5	59.6	61	-	60.3
20.00 - 21.00	56.9	59.7	59.3	2.8	-	61.1
21.00 - 22.00	58.2	60.8	61.2	62.4	-	60.5
22.00 - 23.00 (Night)	53.1	59.2	60.4	61.6	-	60.2
23.00 - 00.00	54	58.9	59.9	60.7	-	59.5
00.00 - 01.00	54.2	59.7	59.5	61.9	-	58.6
01.00 - 02.00	53.3	61.1	60.8	61.1	-	59.1
02.00 - 03.00	50.4	59.8	59.5	61	-	58.3
03.00 - 04.00	53.2	62	59.2	59.8	-	58.9
04.00 - 05.00	53.5	60.6	59.4	60.1	-	59.7
05.00 - 06.00	53	62	59.6	63.5	-	60.8

Location: 3 - RMU Building

Location	Port operating building					
Month	Jan	Feb	Mar	Apr	May	Jun
Unit	Leq dB(A)	Leq dB(A)	Leq dB(A)	Leq dB(A)	Leq dB(A)	Leq dB(A)
06.00 - 07.00 (Day)	57.7	62.4	60.5	60.6	-	61.8
07.00 -08.00	57.1	60.1	61.7	61.1	-	62.4
08.00 - 09.00	56.7	59.4	62.9	63	-	62.9
09.00 - 10.00	55.4	60.3	60.8	63.8	-	64.3
10.00 - 11.00	61.5	63.6	65.5	63.5	-	65.1
11.00 - 12.00	59.2	60.6	62.7	65.3	-	65.9
12.00 - 13.00	58.8	63.4	65.1	64.7	-	66.3
13.00 - 14.00	62.1	60.7	63.6	63.1	-	64.8
14.00 - 15.00	62.5	61.1	61.3	64.3	-	65.7
15.00 - 16.00	60.3	58.7	60.9	64.7	-	66.4
16.00 - 17.00	58.4	59.6	60.6	65.2	-	65.5
17.00 - 18.00	59.8	61.7	65.7	63.9	-	62.4
18.00 - 19.00	60.8	62.3	63.4	62.7	-	64.6
19.00 -20.00	58.1	60.6	62.1	62.1	-	63.1
20.00 - 21.00	61.6	59.7	60.8	63.8	-	65.3
21.00 - 22.00	57.6	60.1	60.4	62.9	-	64.6
22.00 - 23.00 (Night)	56.7	58.4	60.7	62.4	-	59.2
23.00 - 00.00	56.3	57.2	58.3	61.9	-	58.8
00.00 - 01.00	57.6	59.3	59.6	60.2	-	59.6
01.00 - 02.00	57.8	60.2	61.5	61.7	-	60.2
02.00 - 03.00	55.2	59.4	61	60.5	-	59.8
03.00 - 04.00	55.7	61.1	59.5	59.5	-	60.4
04.00 - 05.00	53.5	59.9	59.1	60.6	-	60.9
05.00 - 06.00	58	60.4	59.3	60	-	61.7

Ambient Air Quality Standards in respect of Noise

Area Code	Category of Area / Zone	Limits in dB(A) Leq*	
		Day Time	Night Time
(A)	Industrial area	75	70
(B)	Commercial area	65	55
(C)	Residential area	55	45
(D)	Silence Zone	50	40

- Note:-
1. Day time shall mean from 6.00 a.m. to 10.00 p.m.
 2. Night time shall mean from 10.00 p.m. to 6.00 a.m.
 3. Silence zone is an area comprising not less than 100 metres around hospitals, educational institutions, courts, religious places or any other area which is declared as such by the competent authority
 4. Mixed categories of areas may be declared as one of the four above mentioned categories by the competent authority.

* dB(A) Leq denotes the time weighted average of the level of sound in decibels on scale A which is relatable to human hearing.

A "decibel" is a unit in which noise is measured.

"A", in dB(A) Leq, denotes the frequency weighting in the measurement of noise and corresponds to frequency response characteristics of the human ear.

Leq: It is an energy mean of the noise level over a specified period.

DG SET EMISSIONS

Sampling of Flue gas emission level at 4 no's of DG Sets were carried out and its emissions were determined along with its noise intensity. The Detailed report has been enclosed as Annexure - 4.

DETAILS OF EMISSION MONITORING LOCATIONS

STATION CODE	LOCATIONS	Geographical Location
SM-01	DG - 1 1500 KVA (Near MRSS)	13° 16'13.40"N 80° 20'8.15"E
SM-02	DG - 2 1500 KVA (Near MRSS)	13° 16'13.40"N 80° 20'8.15"E
SM-03	DG - 3 1500 KVA (Near MRSS)	13° 16'13.40"N 80° 20'8.15"E
SM-04	DG - 4 125 KVA (Near MRSS)	13° 16'13.16"N 80° 20'7.19"E

Annexure 4 Source Emission Monitoring Report Jan to Jun 2023

S. No	Capacity	1500 KVA - 1					
	Month	Jan	Feb	Mar	Apr	May	Jun
	Parameters						
1	Stack Temperature, °C	-	210	-	219	-	215
2	Flue Gas Velocity, m/s	-	22.78	-	21.37	-	19.68
3	Sulphur Dioxide, mg/Nm3	-	6.4	-	6.9	-	6.4
4	NOX (as NO2) in ppmv	-	92	-	83	-	79
5	Particular matter, mg/Nm3	-	8.5	-	9.6	-	13.8
6	Carbon Monoxide, mg/Nm3	-	30	-	34	-	37
7	Gas Discharge, Nm3/hr	-	6346	-	5844	-	17191

S. No	Capacity	1500 KVA - 2					
	Month	Jan	Feb	Mar	Apr	May	Jun
	Parameters						
1	Stack Temperature, °C	-	231	-	226	-	10
2	Flue Gas Velocity, m/s	-	20.96	-	22.15	-	20.92
3	Sulphur Dioxide, mg/Nm3	-	7.8	-	7.2	-	6.9
4	NOX (as NO2) in ppmv	-	96	-	95	-	91
5	Particular matter, mg/Nm3	-	7	-	10.8	-	16.1
6	Carbon Monoxide, mg/Nm3	-	36	-	37	-	40
7	Gas Discharge, Nm3/hr	-	5595	-	5972	-	18052

S. No	Capacity	1500 KVA - 3					
	Month	Jan	Feb	Mar	Apr	May	Jun
	Parameters						
1	Stack Temperature, °C	214	-	207	-	-	-
2	Flue Gas Velocity, m/s	20.72	-	22.62	-	-	-
3	Sulphur Dioxide, mg/Nm3	7.3	-	6.3	-	-	-
4	NOX (as NO2) in ppmv	93	-	87	-	-	-
5	Particular matter, mg/Nm3	8.6	-	11.3	-	-	-
6	Carbon Monoxide, mg/Nm3	31	-	41	-	-	-
7	Gas Discharge, Nm3/hr	5720	-	6340	-	-	-

S. No	Capacity	125 KVA - 4					
	Month	Jan	Feb	Mar	Apr	May	Jun
	Parameters						
1	Stack Temperature, °C	129	-	125	-	-	-
2	Flue Gas Velocity, m/s	12.91	-	13.17	-	-	-
3	Sulphur Dioxide, mg/Nm ³	5.3	-	6.1	-	-	-
4	NO _x (as NO ₂) in ppmv	65	-	76	-	-	-
5	Particular matter, mg/Nm ³	5.8	-	9.7	-	-	-
6	Carbon Monoxide, mg/Nm ³	21	-	32	-	-	-
7	Gas Discharge, Nm ³ /hr	608	-	626	-	-	-

Parameter		Area Category	Total engine rating of the plant (includes existing as well as new generator sets)	Generator sets commissioning date		
				Before 1.7.2003	Between 1.7.2003 and 1.7.2005	On or after 1.7.2005
NO _x (as NO ₂) (At 15% O ₂ , dry basis, in ppmv)		A	Up to 75 MW	1100	970	710
		B	Up to 150 MW			
		A	More than 75 MW	1100	710	360
		B	More than 150 MW			
NMHC (as C) (at 15% O ₂), mg/Nm ³		Both A and B		150	100	
PM (at 15% O ₂), mg/Nm ³	Diesel Fuels- HSD & LDO	Both A and B		75	75	
	Furnace Oils- LSHS & FO	Both A and B		150	100	
CO (at 15% O ₂), mg/Nm ³		Both A and B		150	150	

¹ Inserted by Rule 2(b) of the Environment (Protection) Second Amendment Rules, 2008 notified by G.S.R.280(E), dated 11.4.2008.

² Serial No.96 and entries relating thereto inserted by Rule 2 of the Environment (Protection) Third Amendment Rules, 2002 notified vide Notification G.S.R.489(E), dated 9.7.2002.

STP WATER SAMPLE ANALYSIS

Water samples were collected at the following points.

- 25 KLD Treated Water Outlet

DETAILS OF STP WATER LOCATIONS

STATION CODE	LOCATIONS	GEOGRAPHICAL LOCATION
STP-1	25 KLD	130 16' 12" N 800 20' 8" E

Analysis results of the water sample collected from the above location are enclosed as Annexure - 5.

STP - INLET WATER							
Capacity		STP 25KLD					
Month		Jan	Feb	Mar	Apr	May	Jun
S.No.	Parameters					-	
1	pH @ 25 °C	7.31	7.56	7.19	7.05	-	7.12
2	Total Suspended Solids	145	128	121	103	-	110
3	BOD at 27 °C for 3 days	131	110	135	124	-	132
4	Fecal Coliform	840	840	920	940	-	1100
5	COD	378	332	363	325	-	356
6	Oil & Grease	8.4	7.5	7.9	6.6	-	6.9
7	Total Dissolved Solids	1316	1518	906	837	-	870
8	Chlorides (as Cl)	530	634	421	398	-	410
9	Sulphates (as SO4)	43	47	53	52	-	60

STP - OUTLET WATER							
Capacity		STP 25KLD					
Month		Jan	Feb	Mar	Apr	May	Jun
S.No.	Parameters					-	
1	pH @ 25 °C	7.88	7.92	7.34	7.08	-	7.18
2	Total Suspended Solids	24	21	26	23	-	26.0
3	BOD at 27 °C for 3 days	16	14	17	15	-	18
4	Fecal Coliform	120	110	130	110	-	130
5	COD	88	58	82	59	-	65.0
6	Oil & Grease	BDL	BDL	BDL	BDL	-	<1.0
7	Total Dissolved Solids	1028	1142	742	751	-	768
8	Chlorides (as Cl)	588	618	386	346	-	355
9	Sulphates (as SO4)	44	41	45	40	-	45

MINISTRY OF ENVIRONMENT, FOREST AND CLIMATE CHANGE

NOTIFICATION

New Delhi, the 13th October, 2017

G.S.R. 1265(E).—In exercise of the powers conferred by sections 6 and 25 of the Environment (Protection) Act, 1986 (29 of 1986), the Central Government hereby makes the following rules further to amend the Environment (Protection) Rules, 1986, namely:-

1. **Short title and commencement.**—(1) These rules may be called the Environment (Protection) Amendment Rules, 2017.

(2) They shall come into force on the date of their publication in the Official Gazette.

2. In the Environment (Protection) Rules, 1986, in Schedule – I, after serial number 104 and the entries relating thereto, the following serial number and entries shall be inserted, namely:—

Sl. No.	Industry	Parameters	Standards	
1	2	3	4	
		Effluent discharge standards (applicable to all mode of disposal)		
“105	Sewage Treatment Plants (STPs)		Location	Concentration not to exceed
			(a)	(b)
		pH	Anywhere in the country	6.5-9.0
		Bio-Chemical Oxygen Demand (BOD)	Metro Cities*, all State Capitals except in the State of Arunachal Pradesh, Assam, Manipur, Meghalaya Mizoram, Nagaland, Tripura Sikkim, Himachal Pradesh, Uttarakhand, Jammu and Kashmir, and Union territory of	20
			Andaman and Nicobar Islands, Dadar and Nagar Haveli Daman and Diu and Lakshadweep	
			Areas/regions other than mentioned above	30
		Total Suspended Solids (TSS)	Metro Cities*, all State Capitals except in the State of Arunachal Pradesh, Assam, Manipur, Meghalaya Mizoram, Nagaland, Tripura Sikkim, Himachal Pradesh, Uttarakhand, Jammu and Kashmir and Union territory of Andaman and Nicobar Islands, Dadar and Nagar Haveli Daman and Diu and Lakshadweep	<50
			Areas/regions other than mentioned above	<100
		Fecal Coliform (FC) (Most Probable Number per 100 milliliter, MPN/100ml	Anywhere in the country	<1000
*Metro Cities are Mumbai, Delhi, Kolkata, Chennai, Bengaluru, Hyderabad, Ahmedabad and Pune.				

vi. DRINKING WATER SAMPLE ANALYSIS

Drinking Water samples were collected at the Canteen or Office Building. Analysis results of the water sample collected from the above location are enclosed as Annexure - 6.

Annexure 6 Drinking Water test report Jan to Jun 2022


S.No.	Parameters	Unit	Jan	Feb	Mar	Apr	May	Jun
1	Color	Hazen	BDL (DL :1.0)	BDL (DL :1.0)	-	BDL (DL :1.0)	-	0
2	Odour	-	Unobjectionable	Unobjectionable	-	Unobjectionable	-	Unobjectionable
3	Taste	-	Agreeable	Agreeable	-	Agreeable	-	Agreeable
4	Turbidity	N.T.U	BDL(DL 0.5)	BDL(DL 0.5)	-	BDL(DL 0.5)	-	<0.01
5	pH @ 25 °C	-	6.96	7.08	-	6.52	-	6.66
6	Total Hardness as CaCo3	mg/L	8.0	12.0	-	11.0	-	12.9
7	Iron as Fe	mg/L	BDL(DL 0.05)	BDL(DL 0.05)	-	BDL(DL 0.05)	-	BDL(DL 0.05)
8	Chloride as Cl	mg/L	6.3	14	-	9	-	11.3
9	Total Residual Chlorine	mg/L	BDL (DL : 0.1)	BDL (DL : 0.1)	-	BDL (DL : 0.1)	-	<0.1
10	Total Dissolved Solids	mg/L	38	52	-	32	-	40
11	Calcium as Ca	mg/L	2.0	3.2	-	2.7	-	3.26
12	Copper as Cu	mg/L	BDL(DL 0.05)	BDL(DL 0.05)	-	BDL(DL 0.05)	-	BDL(DL 0.05)
13	Manganese as Mn	mg/L	BDL(DL 0.05)	BDL(DL 0.05)	-	BDL(DL 0.05)	-	BDL(DL 0.05)
14	Sulphate as SO4	mg/L	BDL (DL :1.0)	BDL (DL :1.0)	-	BDL (DL :1.0)	-	BDL (DL :1.0)
15	Nitrate as No3	mg/L	BDL (DL :1.0)	BDL (DL :1.0)	-	BDL (DL :1.0)	-	BDL (DL :1.0)
16	Fluoride as F	mg/L	BDL (DL :0.1)	BDL (DL :0.1)	-	BDL (DL :0.1)	-	BDL (DL :0.1)
17	Phenolic compounds as C6H5OH	mg/L	BDL(DL 0.001)	BDL(DL 0.001)	-	BDL(DL 0.001)	-	BDL(DL 0.001)
18	Mercury as Hg	mg/L	BDL (DL : 0.001)	BDL (DL : 0.001)	-	BDL (DL : 0.001)	-	BDL (DL : 0.001)
19	Cadmium as Cd	mg/L	BDL (DL : 0.003)	BDL (DL : 0.003)	-	BDL (DL : 0.003)	-	BDL (DL : 0.003)
20	Selenium as Se	mg/L	BDL (DL : 0.01)	BDL (DL : 0.01)	-	BDL (DL : 0.01)	-	BDL (DL : 0.01)
21	Arsenic as As	mg/L	BDL (DL : 0.01)	BDL (DL : 0.01)	-	BDL (DL : 0.01)	-	BDL (DL : 0.01)
22	Lead as Pb	mg/L	BDL (DL : 0.01)	BDL (DL : 0.01)	-	BDL (DL : 0.01)	-	BDL (DL : 0.01)
23	Zinc as Zn	mg/L	BDL (DL : 0.05)	BDL (DL : 0.05)	-	BDL (DL : 0.05)	-	BDL (DL : 0.05)
24	Anionic Detergents	mg/L	Nil	Nil	-	Nil	-	Nil
25	Total Chromium as Cr	mg/L	BDL (DL : 0.05)	BDL (DL : 0.05)	-	BDL (DL : 0.05)	-	BDL (DL : 0.05)
26	Phenolphthalein Alkalinity as CaCo3	mg/L	Nil	Nil	-	Nil	-	Nil
27	Total Alkalinity as CaCo3	mg/L	22	27	-	24	-	19
28	Aluminium as Al	mg/L	BDL (DL : 0.03)	BDL (DL : 0.03)	-	BDL (DL : 0.03)	-	BDL (DL : 0.03)
29	Boron as B	mg/L	BDL (DL :0.1)	BDL (DL :0.1)	-	BDL (DL :0.1)	-	BDL (DL :0.1)
30	Magnesium as Mg	mg/L		0.97	-	9.93	-	1.15
31	Mineral Oil	mg/L	Nil	Nil	-	Nil	-	Nil
32	Polynuclear Aromatic Hydrocarbons	mg/L	Nil	Nil	-	Nil	-	Nil
33	Pesticides	mg/L	Nil	Nil	-	Nil	-	Nil
34	Cyanide as CN	mg/L	BDL (DL: 0.01)	BDL (DL: 0.01)	-	BDL (DL: 0.01)	-	BDL (DL: 0.01)
35	E. coli	MPN/100ml	Absent	Absent	-	Absent	-	Absent
36	Total Coliform	MPN/100ml	Absent	Absent	-	Absent	-	Absent

VII. MARINE SAMPLING:

Marine Water samples and sediment samples were collected at locations South side berth and North side berth. Analysis data of Marine and sediments as represented in Annexure - 7 & 8.

STATION CODE	LOCATIONS	Geographical Location
MW – 1 / MS – 1	Bollard / Berth area	130 16' 25" N 800 20' 16" E

Water and Marine Sampling Locations

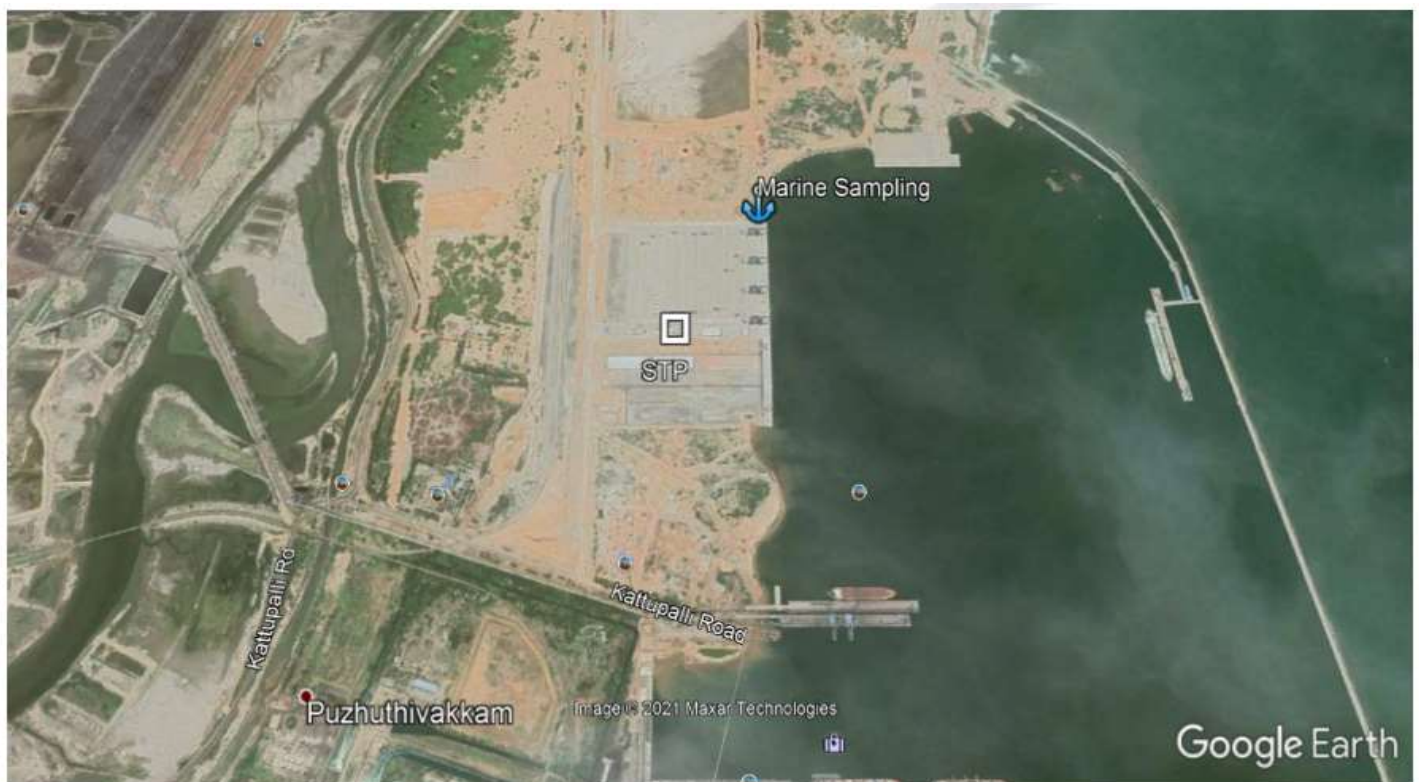

Annexure 7 Marine Water sample test report Jan to Jun 2023

[illegible]

Month & Year			Jan		Feb		Mar		Apr		May		Jun	
S.No.	Parameters	Unit	Surface	Bottom	Surface	Bottom	Surface	Bottom	Surface	Bottom	Surface	Bottom	Surface	Bottom
38	Primary Productivity	mg C/m ³ /hr	9.47	10.58	8.89	9.87	8.95	9.76	8.76	9.14	-	-	8.72	9.11
39	Chlorophyll a	mg /m ³	7.03	6.45	6.04	7.11	7.04	6.43	6.12	6.74	-	-	6.1	6.72
40	Phaeopigment	mg /m ³	3.56	3.92	2.78	3.79	3.26	3.87	2.91	3.56	-	-	2.89	3.53
41	Total Biomass	ml /100 m ³	2.05	1.97	1.86	2.21	2.01	1.94	1.89	2.17	-	-	1.86	2.15
PHYTOPLANKTON														
42	Bacteriastrum hyalinum	nos/ml	16	20	19	17	15	19	17	16		-	15	13
43	Bacteriastrum varians	nos/ml	18	17	21	19	19	16	20	17	-	-	17	20
44	Chaetoceros didymus	nos/ml	15	12	17	13	17	13	16	14	-	-	13	11
45	Chaetoceros decipiens	nos/ml	14	16	15	18	12	16	14	18	-	-	11	15
46	Biddulphia mobiliensis	nos/ml	17	19	19	16	15	18	17	14	-	-	20	17
47	Ditylum brightwellii	nos/ml	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	-	-	Nil	Nil
48	Gyrosigma sp	nos/ml	7	8	9	6	8	8	9	7			5	3
49	Cladophysis sps	nos/ml	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	-	-	Nil	Nil
50	Coscinodiscus centralis	nos/ml	14	13	16	11	12	14	15	12	-	-	17	15
51	Coscinodiscus granii	nos/ml	12	10	15	12	10	11	14	11	-	-	10	7
52	Cylotella sps	nos/ml	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	-	-	Nil	Nil
53	Hemidiscus hardmanianus	nos/ml	18	15	20	14	16	13	19	16	-	-	17	13
54	Laudaria annulata	nos/ml	14	18	16	11	12	17	16	13	-	-	19	15
55	Pyropacus horologicum	nos/ml	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	-	-	Nil	Nil
56	Pleurosigma angulatum	nos/ml	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	-	-	Nil	Nil
57	Leptocylindrus danicus	nos/ml	22	21	21	19	24	22	22	18	-	-	19	16
58	Guinardia flaccida	nos/ml	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	-	-	Nil	Nil
59	Rhizosolenia alata	nos/ml	6	7	8	5	5	8	7	6	-	-	10	8
60	Rhizosolenia imbricata	nos/ml	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	-	-	Nil	Nil
61	Rhizosolenia semispina	nos/ml	20	17	19	16	21	19	20	15	-	-	18	17
62	Thalassionema nitzschioides	nos/ml	20	24	21	20	18	22	20	20	-	-	22	19
63	Triceratium reticulatum	nos/ml	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	-	-	Nil	Nil
64	Ceratium trichoceros	nos/ml	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	-	-	Nil	Nil
65	Ceratium furca	nos/ml	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	-	-	Nil	Nil
66	Ceratium macroceros	nos/ml	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	-	-	Nil	Nil
67	Ceracium longipes	nos/ml	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	-	-	Nil	Nil
ZOOPLANKTONS														
68	Acrocalanus gracilis	nos/ml	14	18	16	20	11	15	17	19	-	-	15	16
69	Acrocalanus sp	nos/ml	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	-	-	Nil	Nil
70	Paracalanus parvus	nos/ml	9	12	7	10	7	10	6	8	-	-	8	11
71	Eutimninus sps	nos/ml	10	8	9	6	8	6	8	5	-	-	6	3
72	Centropages furcatus	nos/ml	8	14	10	13	7	12	10	11	-	-	12	10
73	Corycaeus dana	nos/ml	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	-	-	Nil	Nil
74	Oithona brevicornis	nos/ml	11	15	12	18	10	14	11	16	-	-	13	19
75	Euterpina acutifrons	nos/ml	15	14	11	16	14	15	10	15	-	-	9	14
76	Metacalanus aurivilli	nos/ml	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	-	-	Nil	Nil
77	Copepod nauplii	nos/ml	11	10	10	12	12	11	10	13	-	-	12	12
78	Cirripede nauplii	nos/ml	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	-	-	Nil	Nil
79	Bivalve veliger	nos/ml	17	14	19	16	18	15	17	13	-	-	15	12
80	Gastropod veliger	nos/ml	13	17	11	19	14	18	15	17	-	-	13	15

Annexure 8 MARINE SEDIMENT QUALITY ANALYSIS REPORT Jan to Jun 2023

S.NO	PARAMETER	UNITS	Jan	Feb	Mar	Apr	May	Jun
1	Total organic matter	%	0.68	0.63	0.79	0.71	-	0.66
2	% Sand	%	20	20	20	15	-	19
3	% Silt	%	30	30	30	30	-	34
4	% Clay	%	50	50	50	55	-	47
5	Iron (as Fe)	mg/kg	17.1	15.9	18.2	19.4	-	21.2
6	Aluminium (as Al)	mg/kg	9608	9314	9472	8936	-	9010
7	Chromium (as Cr)	mg/kg	19	15	17	51	-	54
8	Copper (as Cu)	mg/kg	41	47	40	46	-	49
9	Manganese (as Mn)	mg/kg	52	40	49	53	-	55
10	Nickel (as Ni)	mg/kg	20	18	25	48	-	51
11	Lead (as Pb)	mg/kg	25	23	26	18	-	21
12	Zinc (as Zn)	mg/kg	183	171	181	232	-	239
13	Mercury(as Hg)	mg/kg	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	-	BDL (DL : 0.1)
14	Total phosphorus as P	mg/kg	104	101	109	135	-	141
15	Octane	mg/kg	BDL	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	-	BDL (DL : 0.1)
16	Nonane	mg/kg	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	-	BDL (DL : 0.1)
17	Decane	mg/kg	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	-	BDL (DL : 0.1)
18	Undecane	mg/kg	0.55	0.63	0.53	0.61	-	0.63
19	Dodecane	mg/kg	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	-	BDL (DL : 0.1)
20	Tridecane	mg/kg	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	-	BDL (DL : 0.1)
21	Tetradecane	mg/kg	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	-	BDL (DL : 0.1)
22	Pentadecane	mg/kg	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	-	BDL (DL : 0.1)
23	Hexadecane	mg/kg	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	-	BDL (DL : 0.1)
24	Heptadecane	mg/kg	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	-	BDL (DL : 0.1)
25	Octadecane	mg/kg	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	-	BDL (DL : 0.1)
26	Nonadecane	mg/kg	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	-	BDL (DL : 0.1)
27	Elcosane	mg/kg	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	BDL (DL : 0.1)	-	BDL (DL : 0.1)

S.NO	BENTHOS SPECIES	UNITS	Jan	Feb	Marc	Apr	May	June
I.Nematoda								
1	Oncholaimus sp	nos/m ²	13	16	14	15	-	17
2	Tricoma sp	nos/m ²	15	12	13	23	-	21
II.Foraminifera								
1	Ammonia beccarii	nos/m ²	9	8	7	18	-	20
2	Quinulina sp	nos/m ²	14	16	15	23	-	25
3	Discorbinella sp.,	nos/m ²	11	13	12	20	-	18
4	Bolivinaspathulata	nos/m ²	12	15	11	9	-	11
5	Elphidium sp	nos/m ²	24	21	22	17	-	14
6	Nonion depressula	nos/m ²	18	20	19	19	-	21
III.Molluscs-Bivalvia								
1	Meretrix veligers	nos/m ²	22	21	20	22	-	19
2	Anadora veligers	nos/m ²	10	9	13	23	-	21
3	Total No. of individuals	nos/m ²	148	151	146	189	-	212
4	Shanon Weaver Diversity Index (SWDI)		2.25	2.26	2.26	2.27	-	2.28

PHOTOGRAPHS

PORT OPERATING BUILDING – AAQ 1



RMU BUILDING – AAQ 2



IN TERMINAL GATE – AAQ 3



PORT OPERATING BUILDING




IN TERMINAL GATE




RMU BUILDING



MARINE WATER BOTTOM

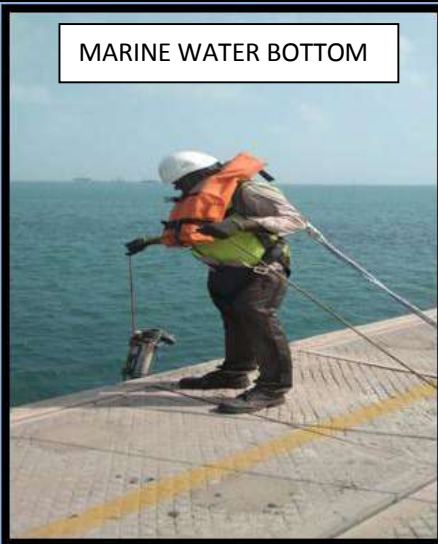

MARINE SEDIMENT

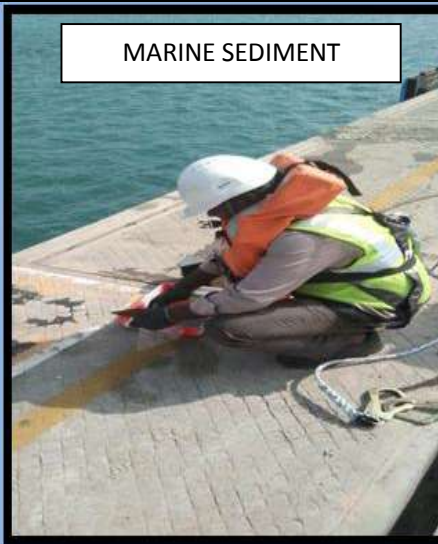

DG 1500 KVA-3



DG 1500 KVA -2



Drinking Water



STP Outlet Water



ANNEXURE – 2
(Annual Environment Statement in Form-V)

Subramanian A

From: Sathish Kumar R
Sent: Thursday, September 22, 2022 4:39 PM
To: eccompliance-tn@gov.in; DEE GMP TNPCB
Cc: Ramde Karangiya; Subramanian A
Subject: Submission of Environmental Statement (Form V) for the financial year ending 31st March, 2022 of Adani Ennore Container Terminal Private Limited, Chennai
Attachments: AECTPL _Form V (2021-22).pdf

Dear Sir,

With reference to the captioned subject, we submit herewith the **Environmental Statement** of **M/s Adani Ennore Container Terminal Private Limited**, in **Form-V** prescribed under Rule 14 of the Environment (Protection) Rules 1986 for the financial year ending 31st March 2022.

Submitted for your kind information and records.

Thanks and Regards

R. Sathish Kumar

Deputy General Manager - Environment | Adani Ports and SEZ Limited |

Mob +91 91760 00959 | Direct: +91 44 2796 8177 | Extn. 69177 |

sathish.r@adani.com | www.adaniports.com |



Growth
with
Goodness

Our Values: Courage | Trust | Commitment



AECTPL/TNPCB/2022-23/128

Date:22.09.2022

To,

The Member Secretary,
Tamil Nadu Pollution Control Board,
76, Mount Salai,
Guindy,
Chennai - 600 032

Dear Sir,

Sub: Submission of Environmental Statement (Form V) for the financial year ending 31st March, 2022 of Adani Ennore Container Terminal Private Limited (AECTPL) - Reg.

Ref: 1. Consent to Operate Order No. 2108136876855 dated 24.08.2021 under Water Act
2. Consent to Operate Order No. 2108236876855 dated 24.08.2021 under Air Act

With reference to the captioned subject and cited references above, we submit herewith the Environmental Statement of **M/s Adani Ennore Container Terminal Private Limited**, in **Form-V** prescribed under Rule 14 of the Environment (Protection) Rules 1986 for the financial year ending 31st March 2022.

Submitted for your kind information and records.

Thanking you,

For, **M/s. ADANI ENNORE CONTAINER TERMINAL PRIVATE LIMITED.**

R. Sathish Kumar
Head - Environment



Enclosure: as above

Copy To:

- 1) The Joint Chief Environmental Engineer, Tamilnadu Pollution Control Board, First Floor, 950/1, Poonamallee High Road, Arumbakkam, Chennai-600 106
- 2) The District Environmental Engineer, Tamil Nadu Pollution Control Board, Gummidipoondi - 601201.

Adani Ennore Container Terminal Pvt Ltd
Adani House
C/o. Kamarajar Port Limited
Ponneri Taluk, Tiruvallur District
Tamil Nadu- 600 120.

Tel +91 44 2824 3062

info@adani.com
www.adani.com

CIN: U61200GJ2014PTC078795

Form-V

(See rule 14 of Environment (Protection) Rules, 1986)

Environmental Statement for the financial year ending 31st March 2022

PART - A

i) Name and Address of the owner / occupier of the industry operation or process	:	Mr. G.J. Rao Chief Executive Officer Adani Ennore Container Terminal Private Limited C/O Kamarajar Port Limited Vallur Post, Ennore Thiruvallur District- 600 120 Tamil Nadu, India
ii) Industry Category	:	Primary : Red Secondary : 1065 – Ports and Harbour, Jetties and Dredging Operations.
iii) Production Capacity	:	Cargo Handling Capacity : 11.68 MMTPA of Container cargo
iv) Year of establishment	:	2016
v) Date of the last environmental statement submitted	:	Vide our Letter No. AECTPL/TNPCB/2021-22/79 dated 23.09.2021



PART - B

WATER AND RAW MATERIAL CONSUMPTION

(i) Water Consumption

S. No	Water Consumption (m ³ /Calendar Day)	2020-2021	2021-2022
1.	Process	NIL	NIL
2.	Cooling	NIL	NIL
3.	Domestic	13.8	12.6

(ii) Raw Material Consumption

S. No.	Name of Raw Material	Name of Products	Consumption of Raw Material per Unit of output	
			During the previous financial year (2020-21)	During the current financial year (2021-22)
1	Not Applicable	Not Applicable	NIL	NIL

The unit does not undergo any manufacturing process. Hence, there is no raw material consumption.



PART - C

POLLUTION DISCHARGE TO ENVIRONEMENT/ UNIT OF OUTPUT (Parameters as specified in the consent issued)

Pollutants	Quality of Pollutants Discharged (Mass/day)	Concentration of Pollutants discharges (mass/volume)	Percentage of variation from prescribed standards with reason	
a) Water	STP Treated Water Characteristics: -			
	Parameter	Consent Limit	Actual	% Variation with prescribed standard
	pH	5.5-9	7.44	-Nil-
	Total Suspended Solids (mg/l)	30	18.62	-Nil-
	BOD (3 days at 27°C) (mg/l)	20	12.59	-Nil-
	Fecal Coliform (MPN/100ml)	1000	177.08	-Nil-
b) Air	DG sets are provided as standby power source and are used during power failure only. The Height of DG stacks as per CPCB/ TNPCC Standards. All the monitored parameters are within standards.			
	All the DG Sets are retrofitted to reduce the Particulate Matter emission level. Efficiency of the retrofitting equipment is observed above 90% against the TNPCC requirement of >70%.			
	All the monitored parameters are well within the prescribed standards.			
Particulate Matter (mg/Nm ³)	DG stack emission report is enclosed as Annexure 1			
Sulphur Dioxide (mg/Nm ³)				
Nitrogen Oxide (ppm)				



PART-D

HAZARDOUS WASTES

(As specified under Hazardous Waste Management and Handling Rules 1989)

Hazardous Wastes	Total Quantity (Kg)	
	During the previous Financial Year (2020-21)	During the current Financial Year (2021-22)
(a) From Process	-Nil-	<ul style="list-style-type: none">• Used/Spent Oil (5.1) – 2500 Liters (2.268 Tons)• Wastes or residue containing oil (5.2) - 800 Liters (0.72 Tons)
(b) From Pollution control facilities	NA	NA

PART-E

SOLID WASTES

TOTAL QUANTITY GENERATED			
Solid Waste		During the previous Financial Year (2020-21)	During the current Financial Year (2021-22)
a)	From process	NIL	NIL
b)	From pollution control facilities- STP	63.42 kgs	99.3 kgs
c)	1. Quantity recycled or reutilized within the Unit	63.42 kgs	99.3 kgs
	2. Sold	NIL	NIL
	3. Disposed	NIL	NIL



PART-F

Please specify the characterization (in terms of Composition and quantum) of Hazardous as well as solid wastes and indicate disposal practice adopted for both these categories of wastes:


- **"Zero Waste to Landfill" Initiative** – No waste is being sent to landfill or incineration facility. AECTPL is having Integrated Waste Management System (IWMS) to proper segregate & recover the materials and are handled as per 5R (Reduce, Reuse, Recycle, Recover and Reprocess) principle.
- AECTPL has awarded with Zero Waste to Landfill Management System (ZWTL MS 2020) from TÜV Rheinland India Pvt. Ltd (Annexure – 2).
- Hazardous wastes include Used oil, Filters contaminated with Oil and Empty barrels / containers contaminated with hazardous wastes. All the hazardous wastes are collected and stored properly in Integrated Waste Management Shed & are being disposed to TNPCB authorized /registered recyclers in line with Hazardous and other Wastes (Management and Transboundary Movement) Rules, 2016 (As amended).
- The used batteries and E –wastes are also stored in Integrated Waste Management Shed and disposed off through approved vendor in line to E-Waste Management Rules 2016 (as amended).
- Hazardous waste Annual returns in Form 4 was submitted in line with the Hazardous and Other Wastes (Management & Trans boundary Movement) Rules, 2016.
- E-waste returns in Form 3 was submitted in line with the E-waste Management Rules, 2016.
- 100% utilization of STP sludge for greenbelt maintenance as manure.
- AECTPL certified as "Single Use Plastic (SUP) Free" site from CII –ITC Centre of Excellence for Sustainable Development.



PART-G

Impact of the pollution abatement measures taken on conservation of natural resources and on the cost of production

- Adani Ennore Container Terminal Private Limited is having electrified cranes only and hence the diesel consumption by the cranes is eliminated completely.
- All the DG Sets are retrofitted to reduce the Particulate Matter emission level. Efficiency of the retrofitting equipment is observed above 90% against the TNPCB requirement of >70%.
- All the domestic wastewaters being generated at port is treated at existing sewage treatment plant and the treated water is being reused within port premises for gardening/horticulture purpose.
- Sewage Treatment Plant (STP) is in continuous operation and the treated effluent water quality is meeting the TNPCB norms. The total cost spent on STP operation during the year 2021-22 is Rs. 4.56 Lakhs.
- Regular Environmental monitoring is being carried out through NABL accredited laboratory. All the monitored environmental parameters are well within the prescribed norms & the details of monitored data is being submitted regularly to TNPCB, CPCB, MoEF&CC and other concerned authorities.
- Unit is continuously developing and maintaining Greenbelt within the port premises.
- Implemented Integrated Waste Management System (IWMS) for managing all types of wastes in line with 5R (Reduce, Reuse, Recycle, Recover and Reprocess) principle.



PART-H


Additional measures/investment proposal for Environmental protection including abatement of pollution, prevention of pollution.

<u>Regular Expenditure (Cost in INR lakhs/year)</u>		
S. No.	Description	Cost
1	Environmental monitoring & Environment Studies	7.86
2	Green belt & Horticulture development	4.87
3	Annual maintenance contractor of STP operation	4.56
4	Operation & Maintenance of Integrated Waste Management System	2.89
5	Housekeeping	37.20

PART-I

ANY OTHER PARTICULARS IN RESPECT TO ENVIRONMENT

- Handling of all types of wastes in line with 5R (Reduce, Reuse, Recycle, Recover and Reprocess) Principle.
- Paperless Operation is in place (Except for Statutory requirements) using application tools and Software – Terminal Info Gateway (TIG).
- Energy Conservation Committee to measure the amount of energy consumed and take actions to reduce the energy consumed through port operations
- Water Warriors committee to identify and reduce the water consumption. The committee would propose innovative water solutions.
- Integrated Management System (ISO 9001:2015, 14001:2015, 45001:2018 and 50001:2018) certified Port.
- Obtained "5S" Certification at MIDPL
- AECTPL is bestowed with the top honors and the details of accolades received during the year 2021-22 are mentioned here under (photos attached at Annexure-3);
 - "21st Annual Greentech Environment & Sustainability" Award 2021' organized by Greentech Foundation, New Delhi for outstanding achievements in **"Environment Protection"** category



- "Platinum Award" under Apex India Green Leaf Award 2021 for Energy Efficiency category


- **Community Development:**

Kattupalli Port has been propagating the community development through a broad based Corporate Social Responsibility (CSR) program in the project area through Adani Foundation since 2018 to ensure inclusive growth and catering to the developmental needs of the community at the grassroots level. The *project area encompasses 11 panchayats covering about 46 villages within 10 Km radius of the Kattupalli Port*. The key interventions introduced in the project area are as under:

- Education
- Community Health
- community Infrastructure facility
- Sustainable Livelihood development
- Tree Plantation & Bio-Diversity development program
- Special Focus Groups
- COVID / Cyclone relief measures

Date: 22.09.2022


(Signature of a person carrying out an industry operation or process)



Name : **G.J. Rao**

Designation: **Chief Executive Officer**

Address : Adani Ennore Container Terminal Pvt Ltd
C/O Kamarajar Port Limited
Vallur post, Ennore
Thiruvallur District- 600 120.



ANNEXURE - 1

ANNEXURE - 1

AECTPL- STACK MONITORING (April'2021 to March'2022)													
Location		DG - 1 1500KVA											
Month & Year		Apr-21	May-21	Jun-21	Jul-21	Aug-21	Sep-21	Oct-21	Nov-21	Dec-21	Jan-22	Feb-22	Mar-22
S.No.	Parameters	20.04.21	21.05.21	19.06.21	21.07.21	19.08.21	16.09.21	22.10.21	16.11.21	27.12.21	24.01.22	17.02.22	24.03.22
1	Stack Temperature, °C	230.0	237.0	-	237.0	223.0	213.0	218.0	226.0	234.0	229.0	-	230.0
2	Flue Gas Velocity, m/s	22.6	21.3	-	20.2	21.4	22.1	21.5	22.0	21.0	22.9	-	22.6
3	Gas Discharge, Nm3/hr	6053.0	5606.0	-	5316.0	5794.0	6107.0	5877.0	5926.0	5581.0	6143.0	-	5606.0
4	Sulphur Dioxide, mg/Nm3	8.9	8.2	-	7.9	8.1	8.9	7.3	7.9	8.2	7.6	-	8.2
5	NOX (as NO2) in ppmv	126.0	129.0	-	152.0	140.0	152.0	128.0	135.0	140.0	134.0	-	131.0
6	Particular matter, mg/Nm3	34.8	32.8	-	32.0	34.1	37.3	11.0	10.0	9.4	11.0	-	9.2
7	Carbon Monoxide, mg/Nm3	81.0	84.0	-	87.0	83.0	80.0	65.0	69.0	75.0	40.0	-	40.0

Location		DG-2 1500KVA											
Month & Year		Apr-21	May-21	Jun-21	Jul-21	Aug-21	Sep-21	Oct-21	Nov-21	Dec-21	Jan-22	Feb-22	Mar-22
S.No.	Parameters	20.04.21	21.05.21	19.06.21	21.07.21	19.08.21	16.09.21	22.10.21	16.11.21	27.12.21	24.01.22	17.02.22	24.03.22
1	Stack Temperature, °C	221.0	228.0	220.0	242.0	235.0	228.0	235.0	-	218.0	223.0	-	235.0
2	Flue Gas Velocity, m/s	21.0	21.4	19.5	21.6	23.0	21.0	21.6	-	22.5	21.5	-	23.1
3	Gas Discharge, Nm3/hr	5714.0	5755.0	5327.0	5632.0	6094.0	5634.0	5728.0	-	6154.0	5830.0	-	5755.0
4	Sulphur Dioxide, mg/Nm3	8.0	7.8	8.3	8.9	8.1	7.5	6.7	-	7.8	7.2	-	7.8
5	NOX (as NO2) in ppmv	115.0	122.0	118.0	164.0	155.0	139.0	120.0	-	129.0	131.0	-	127.0
6	Particular matter, mg/Nm3	33.1	35.4	32.1	34.7	32.0	34.4	8.2	-	9.5	10.0	-	8.8
7	Carbon Monoxide, mg/Nm3	75.0	80.0	74.0	85.0	88.0	85.0	61.0	-	68.0	42.0	-	36.0

Location		DG-3 1500KVA											
Month & Year		Apr-21	May-21	Jun-21	Jul-21	Aug-21	Sep-21	Oct-21	Nov-21	Dec-21	Jan-22	Feb-22	Mar-22
S.No.	Parameters	20.04.21	21.05.21	19.06.21	21.07.21	19.08.21	16.09.21	22.10.21	16.11.21	27.12.21	24.01.22	17.02.22	24.03.22
1	Stack Temperature, °C	225.0	214.0	-	-	218.0	224.0	217.0	205.0	223.0	-	220.0	214.0
2	Flue Gas Velocity, m/s	22.0	21.0	-	-	22.5	21.4	22.1	20.7	22.4	-	22.2	21.2
3	Gas Discharge, Nm3/hr	5951.0	5796.0	-	-	6151.0	5785.0	6057.0	5835.0	6068.0	-	6050.0	5796.0
4	Sulphur Dioxide, mg/Nm3	8.4	7.1	-	-	7.4	7.9	6.5	6.1	7.5	-	8.1	7.1
5	NOX (as NO2) in ppmv	120.0	110.0	-	-	130.0	135.0	124.0	120.0	136.0	-	127.0	120.0
6	Particular matter, mg/Nm3	32.3	30.6	-	-	30.6	33.1	4.1	6.8	11.0	-	9.6	10.4
7	Carbon Monoxide, mg/Nm3	79.0	73.0	-	-	79.0	83.0	64.0	56.0	64.0	-	35.0	33.0

Location		DG-4 125KVA											
Month & Year		Apr-21	May-21	Jun-21	Jul-21	Aug-21	Sep-21	Oct-21	Nov-21	Dec-21	Jan-22	Feb-22	Mar-22
S.No.	Parameters	20.04.21	21.05.21	19.06.21	21.07.21	19.08.21	16.09.21	22.10.21	16.11.21	27.12.21	24.01.22	17.02.22	24.03.22
1	Stack Temperature, °C	127.0	122.0	125.0	-	121.0	125.0	130.0	126.0	121.0	-	126.0	122.0
2	Flue Gas Velocity, m/s	12.1	11.4	12.2	-	11.8	12.5	12.9	12.1	11.7	-	12.1	12.9
3	Gas Discharge, Nm3/hr	568.0	547.0	580.0	-	568.0	592.0	606.0	606.0	563.0	-	571.0	571.0
4	Sulphur Dioxide, mg/Nm3	4.6	4.4	4.7	-	5.0	5.4	4.2	4.0	4.5	-	4.9	5.3
5	NOX (as NO2) in ppmv	87.0	80.0	86.0	-	81.0	87.0	73.0	68.0	61.0	-	67.0	60.0
6	Particular matter, mg/Nm3	13.9	14.5	13.0	-	14.3	16.0	9.4	8.5	5.3	-	4.6	5.3
7	Carbon Monoxide, mg/Nm3	30.0	33.0	36.0	-	29.0	33.0	26.0	29.0	25.0	-	23.0	21.0



Certificate

Standard: **Zero Waste to Landfill Management System
(ZWTL MS 2020)**

Certificate Holder: **Adani Ennore Container Terminal Private Limited**
Ennore Terminal, C/O Kamarajar Port Ltd,
Tiruvallur - 600120, Tamil Nadu, India

Scope: **Providing Port facilities for Handling and
Storage of Containerized Cargo**

Proof has been furnished by means of an audit that the
Requirements of ZWTL MS 2020 are met, with the
achievement of waste diversion rate of above 99%

Validity: This certificate is valid from 01-06-2021 until 31-05-2024
Subject to satisfactory annual surveillance audits.

Certificate No. TUV/ZWLMS/2021/Adani Ports/0503

A handwritten signature in green ink, appearing to be 'Gang'.

New Delhi, 01-06-2021

TÜV Rheinland India Pvt. Ltd.
Office 610, 6th Floor, iThum
Tower, A-40, Sector-62,
Noida- 201301, India

Accolades

Annexure - 3



Greentech Foundation Winner Awards –2021



APEX India Green Leaf Platinum Award - 2021
