adani

Ports and Logistics

Ref: GPL/ENV/ 2026-27/10 **Date: 08.05.2026**

To,

The Director,
Ministry Of Environment, Forest & Climate Change
Indira Paryavaran, Jor Bagh Road, New Delhi -110003

Sub: Development of Gopalpur Ports Ltd. Env. Compliance.

Ref No: 10-12/2009-IA.III dated:30th March 2011, 14th August 2018

Dear Sir,

With reference to the above, we are submitting our compliance with the conditions as laid down in different permission and clearances. The Compliance report till end of March'2026 is enclosed for your kind consideration.

Thanking You,

Yours Sincerely

For **Gopalpur Ports Limited**

(Ranjan Sahu)

Authorized Signatory

Copy to:

1. Additional Chief Secretary, Department of Forest & Wildlife, Govt. of Odisha, Secretariat, Bhubaneswar-751001.
2. The Chairmen, Central Pollution Control Board, Parivesh Bhavan, CBD-cum-office Complex East, Arjune Nagar, Delhi-110032.
3. Addl.Principal Chief Conservator of Forest (Central), Ministry of Environment, Forest and Climate Change, Regional office (EZ), A/3, Chandrasekharpur, Bhubaneswar-751023.
4. The Member Secretary, Odisha State Pollution Control Borad, Parivesh Bhavan, A/118, Nilakantha Nagar, Unit-VIII, Bhubaneswar-751012, Odisha.
5. Regional Officer, Odisha State Pollution Control Board, Berhampur, Ganjam,-760008,Odisha.

Gopalpur Ports Limited
Adani Corporate House, Shantigram,
Nr. Vaishno Devi Circle, S. G. Highway,
Khodiyar, Ahmedabad - 382421

Tel +91 79 2555 4444
Fax +91 79 2555 7177
Investor.apsezl@adani.com
www.adaniports.com
CIN: U63032OR2006PLC008831

Registered Office: Gopalpur Port Arjeepalli, Via Chatrapur, Ganjam, Chatrapur, Odisha, India, 761020

Sl. No.	Conditions	Compliance Status
6.		
(i)	"Consent for Establishment" shall be obtained from State Pollution Control Board under Air and Water Act and a copy shall be submitted to the Ministry before start of any construction work at the site.	Complied. Consent for Establishment obtained for 10 MTPA from SPCB Vide CTE No: 24195/Ind-II-NOC-5022dated:06.11.2008 & vide CTE No: 13982/Ind-IINOC-5022 (pt) dated:27-11-2018 for 20MTPA.
(ii)	No construction works other than those permitted in Coastal Regulation Zone Notification, 2011 shall be carried out in Coastal Regulation Zone area.	Noted and Being Complied Construction activities are being carried out in line with the approvals accorded and in compliance with the provisions of CRZ notification 2011, as amended till date.
(iii)	The shoreline map prepared by Institute for Ocean Management, Chennai with regard to the stretch at Gopalpur Port has been examined and it is observed that on the southern side of the port, the area is shown as high to medium accretion while, on the northern side the area is shown as low to medium erosion. This is because the net littoral drift is towards the northern side and due to the break water at the southern port there seems to be accretion at the southern breakwater and low to medium erosion on the northern side. This has to be ratified by adopting suitable sand bypass system from south break water to the northern side of the north break water.	Being Complied Beach nourishment is undertaken for 5.6 MCM in the North side of the Port to address the erosional aspect. Environmental monitoring report (From Oct' 2025 to March 2026) attached.
(iv)	Controlled and proper methods of dredging including state of the art equipment and planning the dredging operation and disposal shall be employed.	Being Complied Dredging is carried out by use of controlled cutter suction Dredge (CDS). Other mitigation measures are implemented to curtail the turbidity. As a part of existing

		operation, periodic marine water quality monitoring including turbidity is carried out by engaging MOEF&CC approved laboratory. The details of marine water quality monitoring reports for the period from October'2025 to March'2026 are enclosed.
(v)	Technically qualified institutions shall be engaged to monitor the impact right from the beginning to suggest scientifically accepted mitigation measures such as and when required on annual basis at least for first 3 years, shall be obtained.	Being Complied Department of Marine Sciences, Berhampur University engaged to carry out the environmental monitoring of project work of Gopalpur port.
(vi)	A high-level expert committee shall be constituted including the experts for Monitoring the population of benthic life during and after the construction phase and also to ensure compliance of other conditions stipulated in the clearance.	Being complied High level expert committee has been constituted and periodically reviews the compliance conditions stipulated in the clearance.
(vii)	An additional substratum shall be provided with the breakwaters, thereby adding to the habitat of benthic community, especially flora which is very low due to the present geo physical characteristics of the area.	Additional substratum provided during construction of break water and from the studies being carried out by department of Marine Science dept., Berhampur University there is increase in habitat of benthic community.
(viii)	Oil spills if any shall be properly collected and disposed as per the Rules.	Being Complied Oil Spill Contingency Plan (OSCP) is in place. Utmost care is being taken to avoid spillage of fuel/engine oil and lubricants from site. In case of any accidental spillage, saw dust or sand is being used along with absorbent to arrest the spillage. Used oil/waste oil/waste containing oils are handed over to SPCB approved authorized recyclers. Marine water quality & productivity is monitored by MoEF&CC accredited laboratory, M/s- My

		World Consultancy Services Pvt. Ltd There is no adverse impact on water quality and marine productivity in the vicinity
(ix)	There shall be no drawl of ground water in CRZ area.	Complied with. There is no withdrawal of ground water from the CRZ area. We have received permission for 02 nos. of bore wells & 01 no's of Piezometers from CGWA for drawl of ground water. NOC No: CGWA/NOC/INF/ORIG/ 2021/ 11458, valid up to 25.03.2026 for 100 m3/ day.
(x)	Environment Management Plan as suggested shall be strictly complied with.	Complied. As per the EMP the Environmental monitoring and mitigation measures are strictly followed. As a part of existing operation periodic monitoring program covering all seasons on various aspects of the marine ecology monitoring is carried out by NABL & MoEF&CC accredited laboratory, M/s- My World Consultancy services Pvt.Ltd The monitoring results for the period October'25 to March '2026 are enclosed.
(xi)	There shall be no disposal of solid and liquid wastes into the Coastal areas.	Being complied. the generated solid waste segregated and disposed of to Authorized Recycler. Similarly, the secondary containment facility provision is implemented at site and further disposal adopted through Authorized recycler for liquid waste.
(xii)	Sewage Treatment facility should be provided in accordance with the CRZ notification, 2011. Treated sewage shall be reused for flushing of toilets and horticulture purposes.	Being Complied. As a part of existing operation, one STP of capacity 15 KLD, is functioning for treatment of sewage from township area. 3 nos. of Settling ponds have been constructed for

		treatment of runoff water. The treated water is being used for dust suppression of internal roads. Periodic testing of water quality is being carried out by MoEF&CC approved laboratory, and the results are being submitted to SPCB/MOEF&CC. All results are well within the prescribed standards. The water treated is being used for horticulture purpose.
(xiii)	The solid waste shall be properly collected, segregated, and disposed as per the provision of solid Waste (Management and Handling) Rules, 2000.	Being Complied Waste management Plan is in place. GPL has developed a vision for making itself – "A Zero Waste to Landfill Port" by adoption of 5R principle of waste management i.e., Reduce, Reuse, Reprocess, Recycle & Recover. Biodegradable waste is being used for compost preparation. Recyclable waste is handed over to authorized recyclers.
(xiv)	Installation and operation of DG set if any shall comply with the guidelines of CPCB.	Being Complied CPCB approved DG sets are installed. As a part of existing operation 6 nos. of standby DG Sets of capacity ranging from 100 KVA to 250 KVA are in position for emergency backups & uninterrupted power supply to the water supply system and Port operation system. DG sets monitoring carried out by NABL and MOEF&CC accredited laboratory, M/s- My World Consultancy services Pvt._Ltd with frequency monthly basis.
(xv)	The approach channel shall be properly demarcated with lighted buoys for safe navigation and adequate traffic control guidelines shall be framed. The fishermen	Being Complied Channel Marker Buoys have been installed for safe navigation. Fishermen Sensitization

	shall be suitably educated and informed about the traffic guidelines.	is being done regularly for harmony with port operation.
(xvi)	The project proponent shall set up separate environmental management cells for effective implementation of the stipulated environmental safeguards under the supervision of a Senior Executive.	Being Complied Environment Management Cell has been created Headed by Senior Environment personnel.
(xvii)	The project proponent shall take up mangrove plantation/green belt in the project area, wherever possible. Adequate budget shall be provided in the Environment Management Plan for such mangrove development.	Being Complied Greenbelt development has been carried out in and around the port with the selection of native species.
(xviii)	The funds earmarked for environment management plan shall be included in the budget and this shall not be diverted for any other purposes.	Being Complied Adequate funds are ear-marked and available.
(xix)	Under the provisions of Environment (Protection) Act, 1986, legal action shall be initiated against the project proponent if it was found that the construction of the project has been started without obtaining environmental clearance.	Noted and complied Construction of the project commenced after obtaining Environmental Clearance. Date of project commencement is 10th Nov. 2011.
7.		
(I)	Adequate provision for infrastructure facilities including water supply, fuel and sanitation must be ensured for construction workers during the construction phase of the project to avoid any damage to the environment.	Complied
(ii)	Appropriate measures must be taken while undertaking digging activities to avoid any likely degradation of water quality.	Being complied with. GPL ensuring digging activities & further regular marine monitoring is carried out to check the level of turbidity.

(iii)	Borrow sites for each quarry sites for road construction material and dump sites must be identified keeping in view the following: a) No excavation or dumping on private property is carried out without written consent of the owner. b) No excavation or dumping shall be allowed on wetlands, forest areas or other ecologically valuable or sensitive locations. c) Excavation work shall be done in close consultation with the soil Conservation and Watershed Development Agencies working in the area, and d) Construction spoils including bituminous material and other hazardous materials must not be allowed to contaminate water courses and the dump sites for such materials must be secured so that they shall not leach into the ground water.	Being complied. a). No excavation or dumping is carried out on private property. b). No excavation or dumping is carried out in forest areas, wetlands or other ecological valuable or sensitive areas. c). No excavation work is being undertaken. d). Hazardous Waste Management Rules are being followed at site strictly. Utmost care is being taken to prevent contamination by spillage.
(iv)	The construction material shall be obtained only from approved quarries. In case new quarries are to be opened, specific approvals from the competent authority shall be obtained in this regard.	Noted and being Complied Construction materials are being procured only from approved quarries. GPL has obtained the CTO of Pallur Hill stone quarry :1404/2025-26 dated: 31.03.2026 for 48000 CUM/ Annum.
(v)	Adequate precautions shall be taken during transportation of the construction material so that it does not affect the environment adversely.	Being complied . All vehicles coming into the site will be under a speed restriction of 20 km/hr. • Regular Water sprinkling will be done on the approach road by mobile water tankers.

		• It will ensure that all vehicles entering the Port have a valid PUC certification.
(vi)	Full support shall be extended to the officers of this Ministry/Regional Office at Bhubaneswar by the project proponent during inspection of the project for monitoring purposes by furnishing full details and action plan including action taken reports in respect of mitigation measures and other environmental protection activities.	Noted GPL is committed to providing necessary support.
(vii)	A Six-monthly monitoring report shall need to be submitted by the project proponents to the Regional Office of this Ministry at Bhubaneswar regarding the implementation of the stipulated conditions.	Complied. Six – Monthly report submitted to the Regional Office of this Ministry at Bhubaneswar regarding the implementation of the stipulated conditions vide letter no: GPL/ENV/2025-26/33 dated:25.11.2025.
(viii)	Ministry of Environment and Forests or any other competent authority may stipulate any additional conditions or modify the existing ones, if necessary, in the interest of environment and the same shall be complied with.	Noted and Being Complied
(ix)	The Ministry reserves the right to revoke this clearance if any of the conditions stipulated are not complied with the satisfaction of the Ministry.	Noted
(x)	In the event of a change in project profile or change in the implementation agency, a fresh reference shall be made to the Ministry of Environment and Forests.	Noted
(xi)	The project proponents shall inform the Regional Office as well as the Ministry, the date of financial closure and final approval of	Complied

	the project by the concerned authorities and the date of start of land development work.	The Land development work commenced on 10th November 2011 after approval of the project.
(xii)	A copy of the clearance letter shall be marked to concern Panchayat / local NGO, if any, from whom any suggestion / representation have been made, received while processing the proposal.	Noted and complied.
(xiii)	Orissa Pollution control Board shall display a copy of the clearance letter at the Regional Office, District Industries Centre and Collector's Office/Tahsildar's office for 30 days.	Complied
8.	These stipulations would be enforced among others under the provisions of Water (Prevention and Control of Pollution) Act 1974, the Air (Prevention and Control of Pollution) Act 1981, the Environment (Protection) Act, 1986, the Public Liability (Insurance) Act, 1991 and EIA Notification 1994, including the amendments and rules made thereafter.	Noted
9.	All other statutory clearances such as the approvals for storage of diesel from Chief Controller of Explosives, Fire Department, Civil Aviation Department, Forest Conservation act, 1980 and Wildlife (Protection) Act, 1972 etc. shall be obtained, as applicable by project proponents from the respective competent authorities.	Being Complied The PESSO License No. P/EC/OR/14/2531(P420098), dated; 10/01/2024 obtained from Dy. Chief Controller of Explosives, Bhubaneswar having 3 number(s) underground gas tight tanks of capacity 70.00+ 20.00+ 20.00 kiloliters respectively of petroleum Class B connected with 2 number(s) electrically/manually operated dispensing pump(s).
10.	The project proponent shall advertise in at least two local Newspapers widely circulated	Complied, vide letter No. GPL/2011/59, dated 11/04/2011

	in the region, one of which shall be in the vernacular language informing that the project has been accorded Environmental Clearance and copies of clearance are available with the State Pollution Control Board and may also be seen on the website of the Ministry of Environment and forests at http://www.envfor.nic.in. The advertisement should be made within 10 days from the date of receipt of the Clearance letter and a copy of the same should be forwarded to the Regional Office of this Ministry at Bhubaneswar.	
11.	Environmental clearance is subject to final order of the Hon'ble Supreme court of India in the matter of Goa Foundation vs. Union of India in Writ Petition (Civil) No.460 of 2004 as may be applicable to this Project.	Agreed
12.	Status of compliance to the various stipulated environmental conditions and environmental safeguards will be uploaded by the project proponent in its website.	Being Complied. The status of compliance to the various stipulated environmental conditions & mitigation measure uploaded in APSEZ website.
13.	The project proponent shall also submit six monthly reports on the status of compliance of the stipulated EC conditions including results of monitoring data (both in hard copies as well as by e-mail) to the respective Regional Office of MoEF, the respective Zonal Office of CPCB and the SPCB.	Complied. The Six-monthly reports on the status of compliance of the stipulated EC conditions including results of monitoring data (both in hard copies as well as by e-mail) to the respective Regional Office of MoEF, the respective Zonal Office of CPCB and the SPCB submitted on dated: 05th Nov'2025 vide letter No: GPL/ENV/2025-26/28.
14.	The environmental statement for each financial year ending 31st March in Form-V	Complied.

	as is mandated to be submitted by the project proponent to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall be put on the website of the company along with the status of compliance of EC conditions and shall also be sent to the respective Regional Offices of MoEF& CC by e-mail.	The last Environmental statement in FORM-V has been submitted to concern State Pollution Control Board & Regional office vide letter No: GPL/ENV/25-26/09 dated: 08th May 2025.
Additional Conditions of the EC Validity Extension Order dated 14th August 2018		
1.	The Project Proponent will submit a Certified Compliance Report within 03 months issued by the MoEF&—CC, Regional Office or concerned Regional Office of the Central Pollution Control Board or the Member Secretary of the respective State Pollution Control Board for the conditions stipulated in the Environmental and CRZ Clearance issued earlier	Complied
2.	The development plan shall be implemented strictly in accordance to the Coastal Zone Management Plan as drawn up in compliance to the orders of the NGT in this regard. A copy of the compliance report shall be submitted within 30 days to the MoEF& CC.	Complied
3.	As per the Ministry's Office Memorandum F.No22-65/2017-Ia.III dated 1st May 2018, the project proponent is required to prepare and implement Corporate Environment Responsibility (CER) Plan. As per the para 6(II) of the said O.M appropriate funds shall be earmarked for the activities such as infrastructure creation for drinking water supply, sanitation, health, education, skill	As per Para 6 (IX) of the said notification which states that *the CER is not applicable in name change, transfer, amendment involving no additional project investment*; this is not applicable to us, as there is no additional project investment.

	development, roads, cross drains, electrification including solar power, solid waste management facilities, scientific support and awareness to local farmers to increase yield of crop and fodder, rain water harvesting, soil moisture conservation works, avenue plantation, plantation in community areas etc. The activities proposed under CER shall be restricted to the affected area around the project. The entire activities proposed under the CER shall be treated as project and shall be monitored. The monitoring report shall be submitted to the regional office as a part of half yearly compliance report, and to the District Collector. It should be posted on the website of the Project Proponent.	

ENVIRONMENTAL MONITORING REPORT
FOR THE MONTH OF OCTOBER-2025 to MARCH-2026

Submitted to

GOPALPUR PORT LIMITED

At & Po-Arjeepalli, Chatrapur, Ganjam, 761020, Odi sha

GOPALPUR PORT

New Era in Maritime Logistics

Prepared by:

WCS
MY WORLD CONSULTANCY SERVICES

My World Consultancy Services Private Limited
Plot No. 766, Telengapentha,
Cuttack, Odisha 754001
(NABL Approved Laboratory)
NABL TC-11225

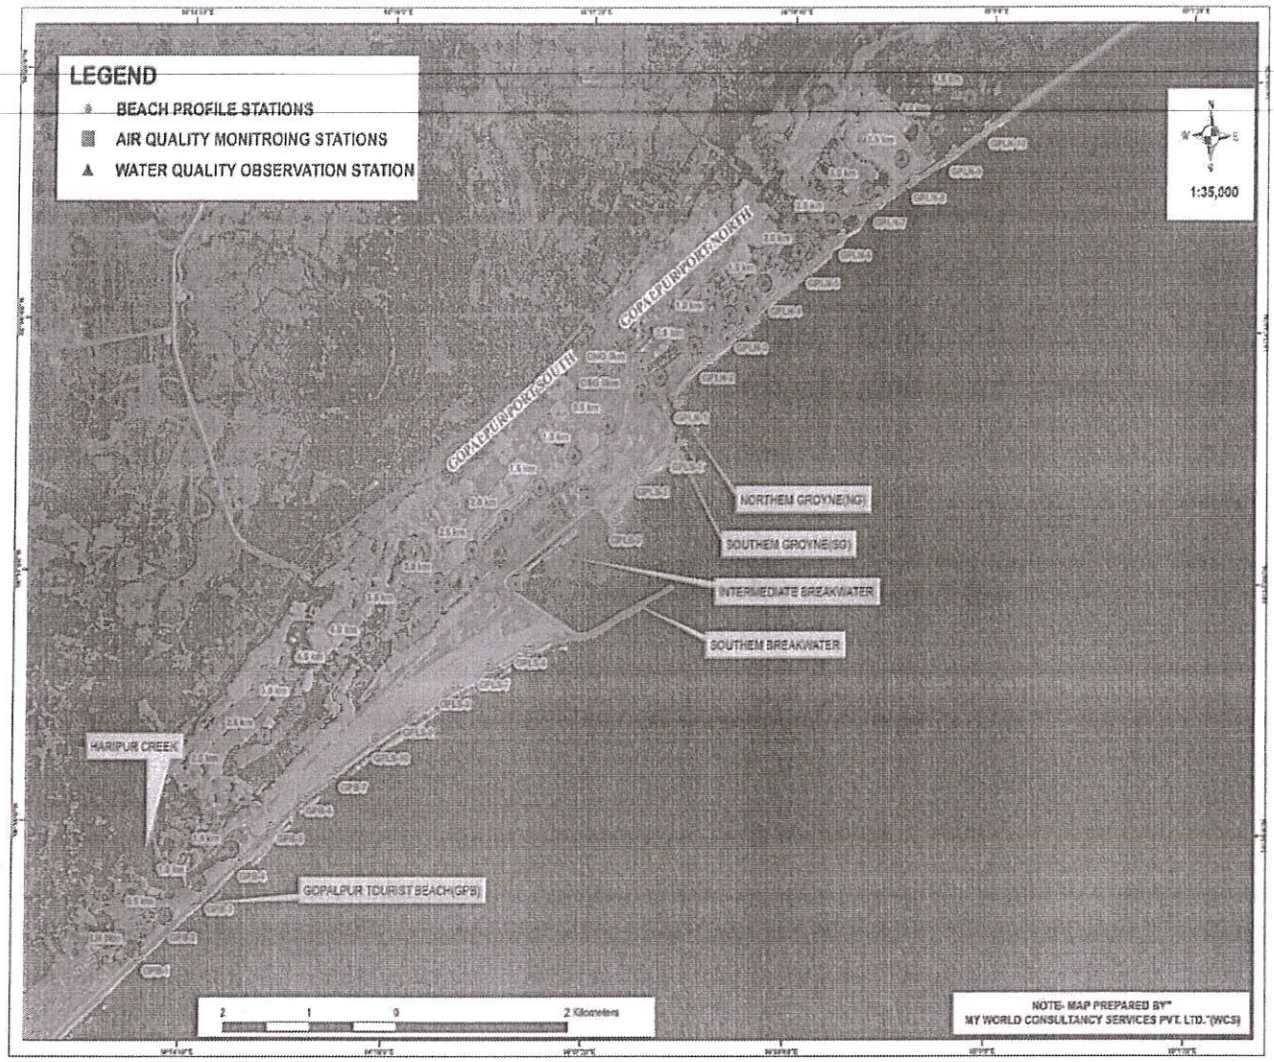


Figure 1 : Sampling locations of different parameters near Gopalpur coast Map

MY WORLD CONSULTANCY SERVICES PVT. LTD.

OBJECTIVES:

1. Shoreline Monitoring

Monitoring the erosion/accretion environment, shoreline change along a stretch of approximately 13km (from Gopalpur light house to Arjipalli village), which lies within the Port limit, on monthly basis.

2. Monitoring of Ambient Air Quality

Monitoring of Ambient Air Quality were carried out at 4 stations; two in the windward side and two in the leeward side within the port premises for PM_{10}, $PM_{2.5}$, SO_2, NO_2, NH_3, O_3, As, C_6H_6, BaP, Pb, Ni & CO to measure the maximum ground level concentration (Fig.1).

3. Noise level monitoring

The noise level monitoring was carried out at 4 stations: two in the windward side and two in the leeward side within the port premises.

4. DG stack monitoring

DG stack monitoring was carried out on monthly basis from six DGs available in the port premises.

5. Domestic effluent

The Domestic effluent water was collected from the outlet of the sewage treatment plant available in the port for analysis of different parameters such as pH, BOD, COD, Total suspended solid, Oil and grease & Faecal Coliform.

6. Marine Water Sample

Chemical and microbial parameters

Coastal water samples were collected monthly from the harbour area for analysis of different Chemical parameters like Odour, Colour, pH, DO, BOD, Nitrate, Fluoride, Iron, Total Chromium, Hexavalent Chromium, Phosphorous, Lead, Copper, Manganese, Cadmium, Nickel, Faecal Coliform, Vanadium, Cyanide, Zinc, Selenium, Sulphide, Phenolic Compound & Bio-assay were analysed soon after the collection.

7. Sediment Sample

Chemical Parameters

Sediment samples were collected every month at same location near berth area and analysed for the Chemical parameters like pH, Texture, Sodium, Potassium, Phosphate, Chlorides, Sulphate, PHC, Lead, Mercury, Hexavalent Chromium and Organic Carbon.

8. Ground Water Analysis

Ground water samples were collected from the port premises every month and analysed for colour, order, turbidity, pH, Total hardness, Iron, Chloride, TDS, Calcium, Magnesium, Sulphate, Fluoride, Alkalinity, Salinity, Zine, Lead and E. Coil.

9. Coal Stack yard

The water samples from the coal stack yard were collected monthly basis from coal stack yard available inside the port premises for analysis of different parameters such us colour, odour, TSS, pH, Temperature, Oil & Grease, TRC, Ammonical Nitrogen, TKN, Free Ammonia, BOD, COD, As & Hg.

10. Biological Parameters

Biological parameters such as light penetration, chlorophyll, primary productivity, phytoplankton, zooplankton, benthic meio fauna and benthic macro fauna within the harbour were analysed at every three-month interval.

GOPALPUR PORTS LIMITED ODISHA INDIA

MY WORLD CONSULTANCY SERVICES PVT. LTD. CUTTACK



Figure2: Sampling activities and field observation.


Observation Schedule

Table 1: Types and frequency of Observations

Types of Observation	**Schedule of Observation**	**Spatial Variability of observation**
Shoreline (ARCPAD_DGPS)	Monthly	Mapping the berm line, representing the shoreline, within the port limit covering 13 km stretch.
Ambient air quality (PM10, PM2.5, SO2, NO2, NH3, O3, As, C6H6, BaP, Pb, Ni & CO)	Twice in a Week	From the four sampling stations within the port environment (Fig. 2)
Noise level	Monthly	Within the port environment as per the guidelines of Central Pollution Control Board (CPCB)
DG Stack Monitoring	Monthly	Monitoring was carried out for the six DGs available inside the port premises.
Domestic effluents	Monthly	pH, BOD, COD, Suspended Solids, Oil & Grease
Coastal Water Sample	Monthly	Odour, Colour, pH, DO, BOD, Nitrate, Fluoride, Iron, Total Chromium, Hexavalent Chromium, Phosphorous, Lead, Copper, Manganese, Cadmium, Nickel, Faecal Coliform, Vanadium, Cyanide, Zinc, Selenium, Sulphide, Phenolic Compound & Bio-assay
Sediment Sample a. Chemical parameters	Monthly	pH, Texture, Sodium, Potassium, Phosphate, Chlorides, Sulphate, PHC,

		Lead, Mercury, Hexavalent Chromium and Organic Carbon
Ground Water	Monthly	colour, order, turbidity, pH, Total hardness, Iron, Chloride, TDS, Calcium, Magnesium, Sulphate, Fluoride, Alkalinity, Salinity, Zine, Lead and E. Coil
Effluent from Coal stack yard	Monthly	colour, odour, TSS, pH, Temperature, Oil & Grease, TRC, Ammonical Nitrogen, TKN, Free Ammonia, BOD, COD, As & Hg
b. Biological Parameters	Quarterly	as light penetration, chlorophyll, primary productivity, phytoplankton, zooplankton, benthic meio fauna and benthic macro fauna





1. Shoreline monitoring

Table-1.1 and Figure 3 present monthly measurements of shoreline distances (in meters) between the berm line and a reference line along Gopalpur Port South from October-2025 to March-2026. Measurements were taken at 0 km, 0.5 km, 1.0 km, 2.5 km. 3.0 km. 3,5 km, 4.0 km, and 4.5 km intervals. In Oct-2025, shoreline length ranged from 661.997 meters at 0 km to 793.764 meters at 4.5 km. peaking at 1150.212 meters at 2.5 km. At 0 km, the values remain relatively stable, ranging from 674.585 (Oct 25) to 675.968 (Mar 26). At 0.5 km, values remain stable from 616.225 (Oct 25) to 622.174 (March 26). At 1.0 km, values peak in Feb 2026 (815.636) and remain consistent across months. The highest variations occur at 2.5 km, where values remain stable between 1150.212 (Oct 2025) and 1151.018 (Jan 26). Beyond 3.0 km, values show some fluctuations but remain relatively higher in Feb 2026 and March 2026 compared to following months. These monthly fluctuations, particularly at the 2.5 km mark, reflect dynamic coastal processes influenced by seasonal changes and geomorphological factors.

Table 1.2 and Figure 4 illustrate shoreline distances along Gopalpur Port North from the dataset represents monthly variations in shoreline characteristics from October 2025 to March 2026 across different distances (0 km to 4.5 km). At the Northern Groin (0 km) a fluctuating trend is observed, with values range between 316.2 (Oct 2025) to 315.985 (Mar 2026). The lowest value occurs in Oct 2025, suggesting gradual sediment reduction or possible erosion at the groin location. particularly at 0.5 km, where values are stable in between 203.132 (Oct 25) to 198.352 (March 26). The relatively values peaking at 1.0 km (233.552) and 1.5 km (171.264) experiencing alternating sediment deposition and erosion. At 2.0 km to 3.0 km North a consistent decrease in values is observed, with a peak in October 2025 (259.398 at 3.5 km), At 4.0 km to 4.5 km North a consistent increase in values is observed, with a peak in October 2025 (387.825 at 4.5 km), suggesting significant sediment build-up further north of the groin. This pattern indicates that sediment is being transported northward and deposited at greater distances from the groin.

Table1.3 and Figure 5 provide shoreline distances from October 2025 to March 2026 along Gopalpur Tourist Beach, measured from 0 km to 3.0 km. The shoreline observations at Gopalpur Tourist Beach (GPB) from October 2025 to March 2026 reveal seasonal variations in shoreline distribution. In October 2025, shoreline levels were relatively low near the beach (0 km- 1.5 km), while higher values at 2.5 km (750.762m) and 3.0 km (765.681m). From October 2025, a slight decline was observed in nearshore areas, possibly due to seasonal erosion or sediment redistribution, while the 2.0 km - 3.0 km section remained consistently high (745.384-765.681 m), confirming it as a stable sediment deposition zone, By Mar 2026, nearshore values stabilized, and maximum sediment accumulation was recorded at 2.5 km (754.958m) and 3.0 km (771.548m). These trends suggest that Gopalpur Tourist Beach experiences dynamic shoreline changes influenced by wave action.

GOPALPUR PORT LIMITED ODISHA INDIA

MV WORLD CONSULTANCY SERVICES PVT. LTD. CUTTACK

Shoreline monitoring

Table 1.1: Shoreline (m) analysis along Gopalpur Port South (Shoreline represents the distance in meter between berm line and the reference line in Fig. 1) from October 2025 to March 2026.

GPLS	SG 0 km	0.5 km	1.0 km	2.5 km	3.0 km	3.5 km	4.0 km	4.5 km
Oct-25	661.997	616.225	811.099	1150.212	1030.211	930.646	814.132	793.764
Nov-25	674.585	618.548	810.574	1152.352	1028.254	932.541	815.241	790.522
Dec-25	676.584	620.244	812.654	1151.145	1026.345	931.748	816.365	788.385
Jan-26	677.174	619.385	813.425	1151.018	1025.218	931.215	816.118	786.525
Feb-26	676.158	621.854	815.636	1160.582	1030.254	933.658	820.378	790.585
Mar-26	675.968	622.174	814.998	1158.695	1031.574	932.625	821.548	788.695

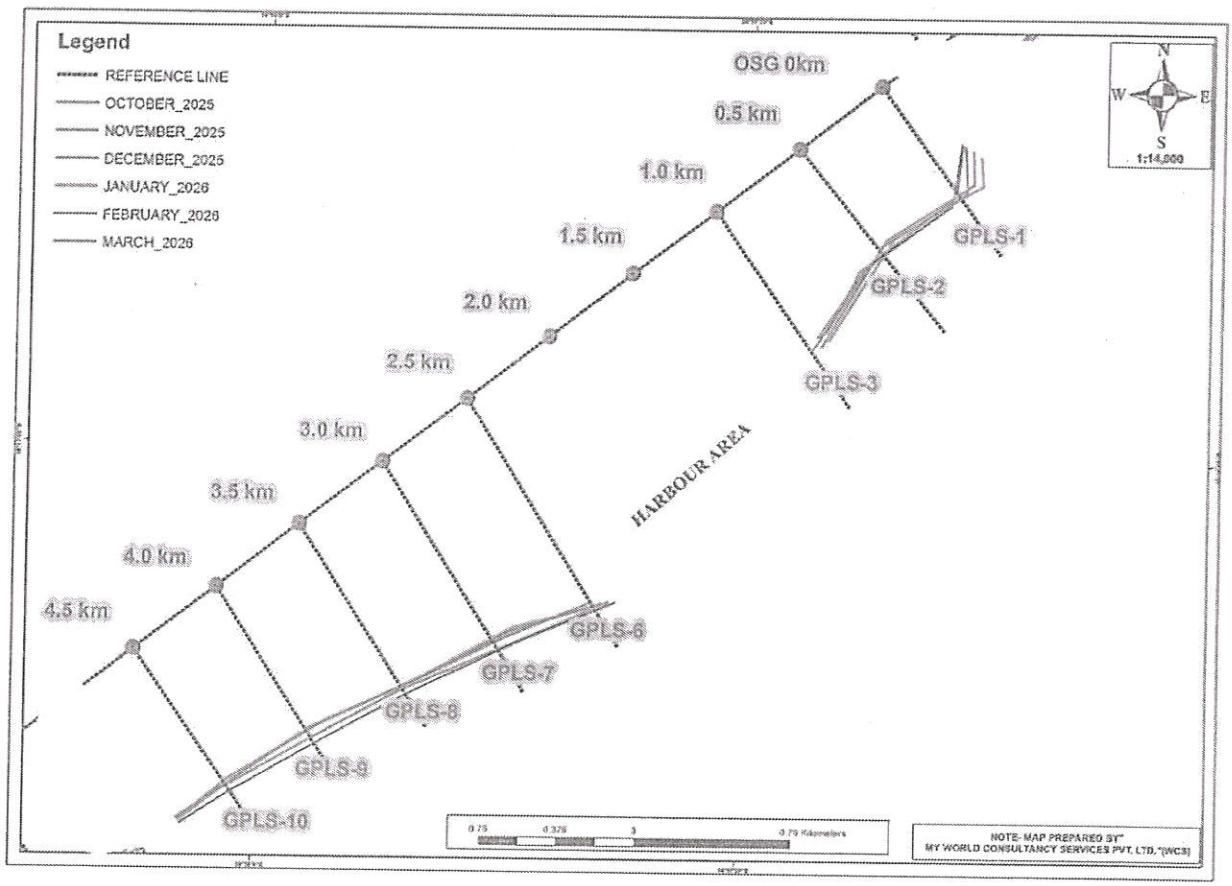


Figure 3: Shoreline change at south of Gopalpur port from October 2025 to March 2026

GOPALPUR PORTS LIMITED ODISHA - INDIA

MY WORLD CONSULTANCY SERVICES PVT. LTD. CUTTACK

Table 1.2: Shoreline (m) analysis along Gopalpur Port north (Shoreline represents the distance in meter between berm line and the reference line in Fig. 2) from October 2025 to March 2026.

GPLN	NG 0 km	0.5 km	1.0 km	1.5 km	2.0 km	2.5 km	3.0 km	3.5 km	4.0 km	4.5 km
Oct-25	316.2	203.132	233.552	171.264	219.767	192.215	159.154	259.398	337.091	387.825
Nov-25	315.696	198.254	210.544	168.255	218.574	190.521	156.347	257.639	330.412	385.694
Dec-25	316.251	198.696	211.365	166.362	219.254	188.659	155.634	255.235	329.858	383.636
Jan-26	314.269	197.569	209.385	166.124	219.12	187.285	155.219	254.369	329.458	380.968
Feb-26	316.245	197.158	208.255	167.345	220.362	185.241	156.258	253.474	330.241	380.548
Mar-26	315.985	198.352	210.285	166.858	221.336	184.524	157.695	250.548	328.659	381.298

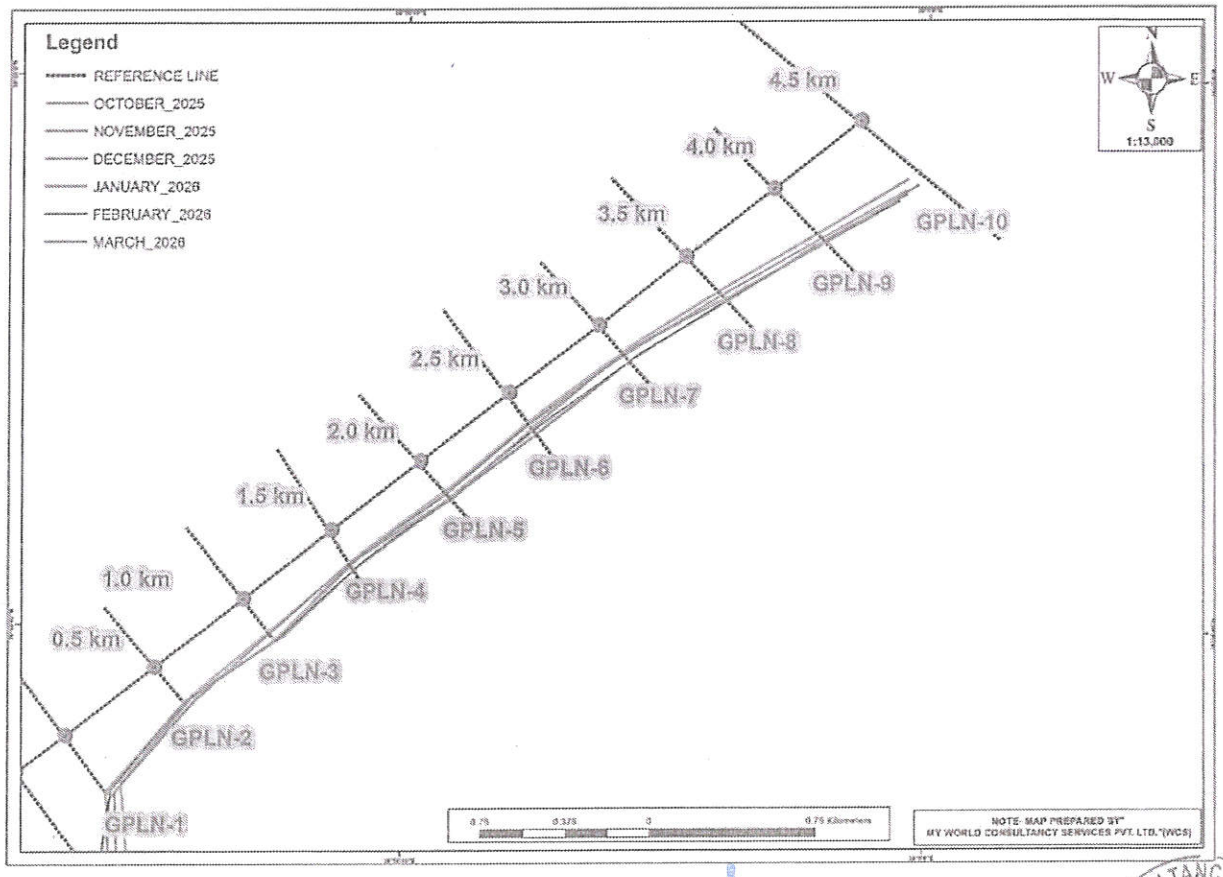


Figure 4: Shoreline change at north of Gopalpur port from October 2025 to March 2026

MY WORLD CONSULTANCY SERVICES PVT. LTD. CUTTACK

Table 1.3: Shoreline (m) analysis along Gopalpur tourist beach (Shoreline represents the distance in meter between berm line and the reference line in Fig. 3) from October 2025 to March 2026.

GPB	LH 0 km	0.5 km	1.0 km	1.5 km	2.0 km	2.5 km	3.0 km
Oct-25	81.245	100.19	96.23	120.833	745.384	750.762	765.681
Nov-25	82.144	101.241	97.52	118.352	744.585	751.258	767.222
Dec-25	83.214	100.542	96.245	119.625	746.585	753.352	766.152
Jan-26	84.266	100.248	97.625	119.565	748.698	752.354	768.544
Feb-26	90.458	105.635	100.365	121.658	750.285	755.622	770.336
Mar-26	90.212	106.214	99.584	121.258	751.185	754.958	771.548

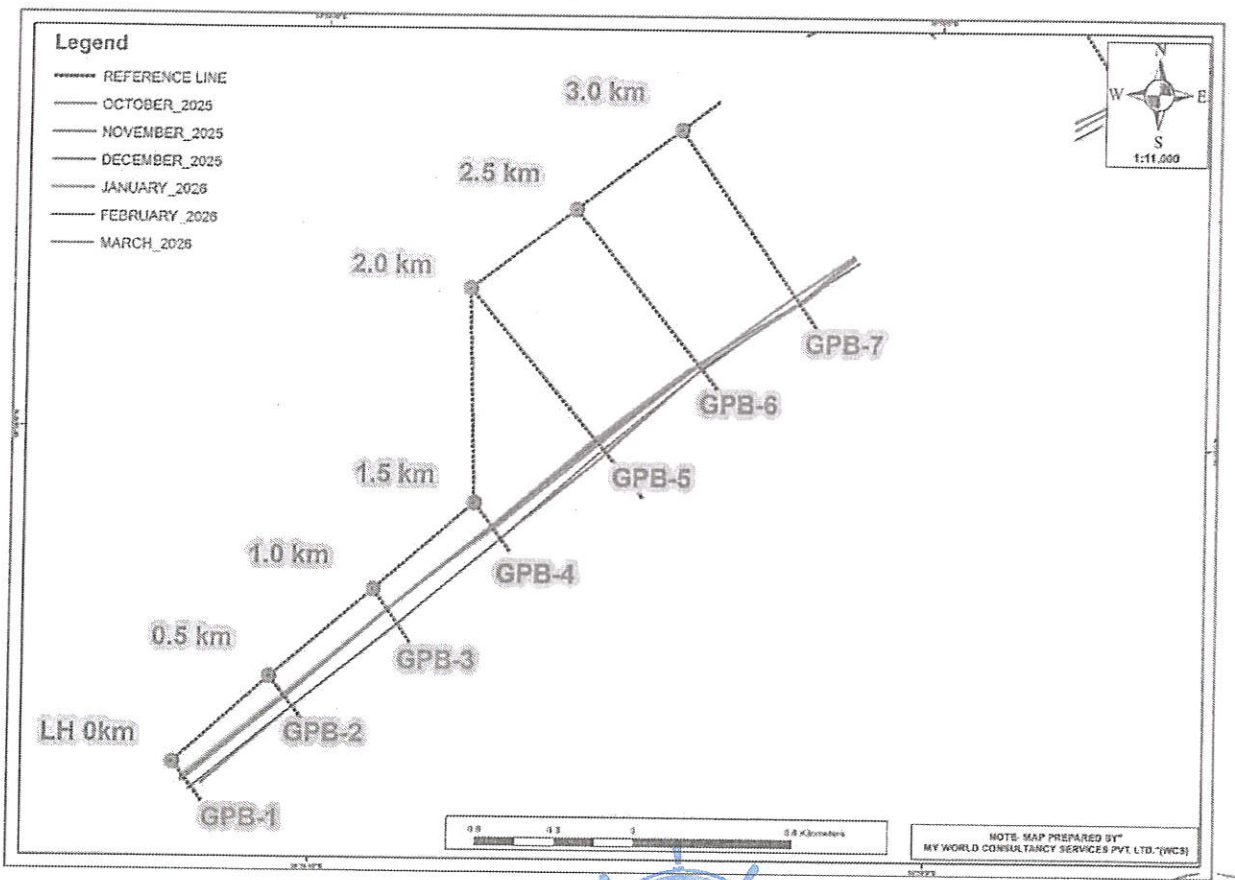


Figure 5: Shoreline change at tourist beach of Gopalpur port from October 2025 to March 2026

MY WORLD CONSULTANCY SERVICES CUTTACK

2. Ambient air quality

Ambient air quality (PM10, PM2.5, SO2, NO2, NH3, O3, As, C6H6, BaP, Pb, Ni & CO) was monitored around the Port premises at four points, two in the windward and two in the leeward sides (Figure 2) from October 2025 to March 2026. The coordinates of the four stations of air quality monitoring are; A-19°18'51.59" N 84°58'6.88" E (Near Main Gate), B-19°18'29.18" N 84°57'40.84" E (At Signal Station), C-19°17'45.3" N 84°57'19.79" E (At Substation-2),D-19°17'17.72" N 84°56'51.72" E (At Substation-4), (Figure 1). The four points of monitoring are fixed in such a way that the impact of the port on air quality can be assessed up to a distance in down wind direction (both during strong sea breeze and land breeze time) where maximum ground level concentration is anticipated. Table-2.1. 2.2, 2.3 and 2.4 depict the air quality values for the study period at the four points within the port premises along with the national ambient air quality standard (NAAQS) norms stipulated by MoEFCC.

The maximum PM10 (78.83/m³) and PM2.5 value (44.54 µg/m³) were recorded during the month of Jan-2026 at station 'B' due to large number of vehicular emission and road dust whereas the minimum PM 10 (35.79 µg/m³) and PM2.5 (18.17 µg/m³) were recorded during the month of October 2025 at station 'D' and station 'C'. The maximum SO2 (8.83 µg/m³) and NO2 (24.7 µg/m³) were recorded during the month of January 2026 at station 'B' respectively due to high vehicular emission. Whereas the minimum SO2 (4.01 µg/m³) was recorded and NO2 (11.21 µg/m³) was recorded at station 'D' during the month of October 2025.

The average value of Pm10 was recorded at station A, B, C and D are 65.82,66.15,63.90 and 58.74. respectively whereas the average PM2.5 at station was A, B, C and D are 33.75,37.37,34.17 and 29.82 respectively the average value of SO_2 was recorded at station A, B, C and D are 7.37,7.41,7.16 and 6.59 respectively whereas the average value of NO2 at station A, B, C and D are 20.63,20.73,20.02 and 18.41 respectively.

The ambient air quality monitored parameters at the four points within the port premises from October 2025 to March 2026 are well within the NAAQ threshold limit stipulated by CPCB. Thus, the ongoing port operational activities are not detrimental to the air quality in the terrestrial environment.

MY WORLD CONSULTANCY SERVICES PVT. LTD. CUTTACK

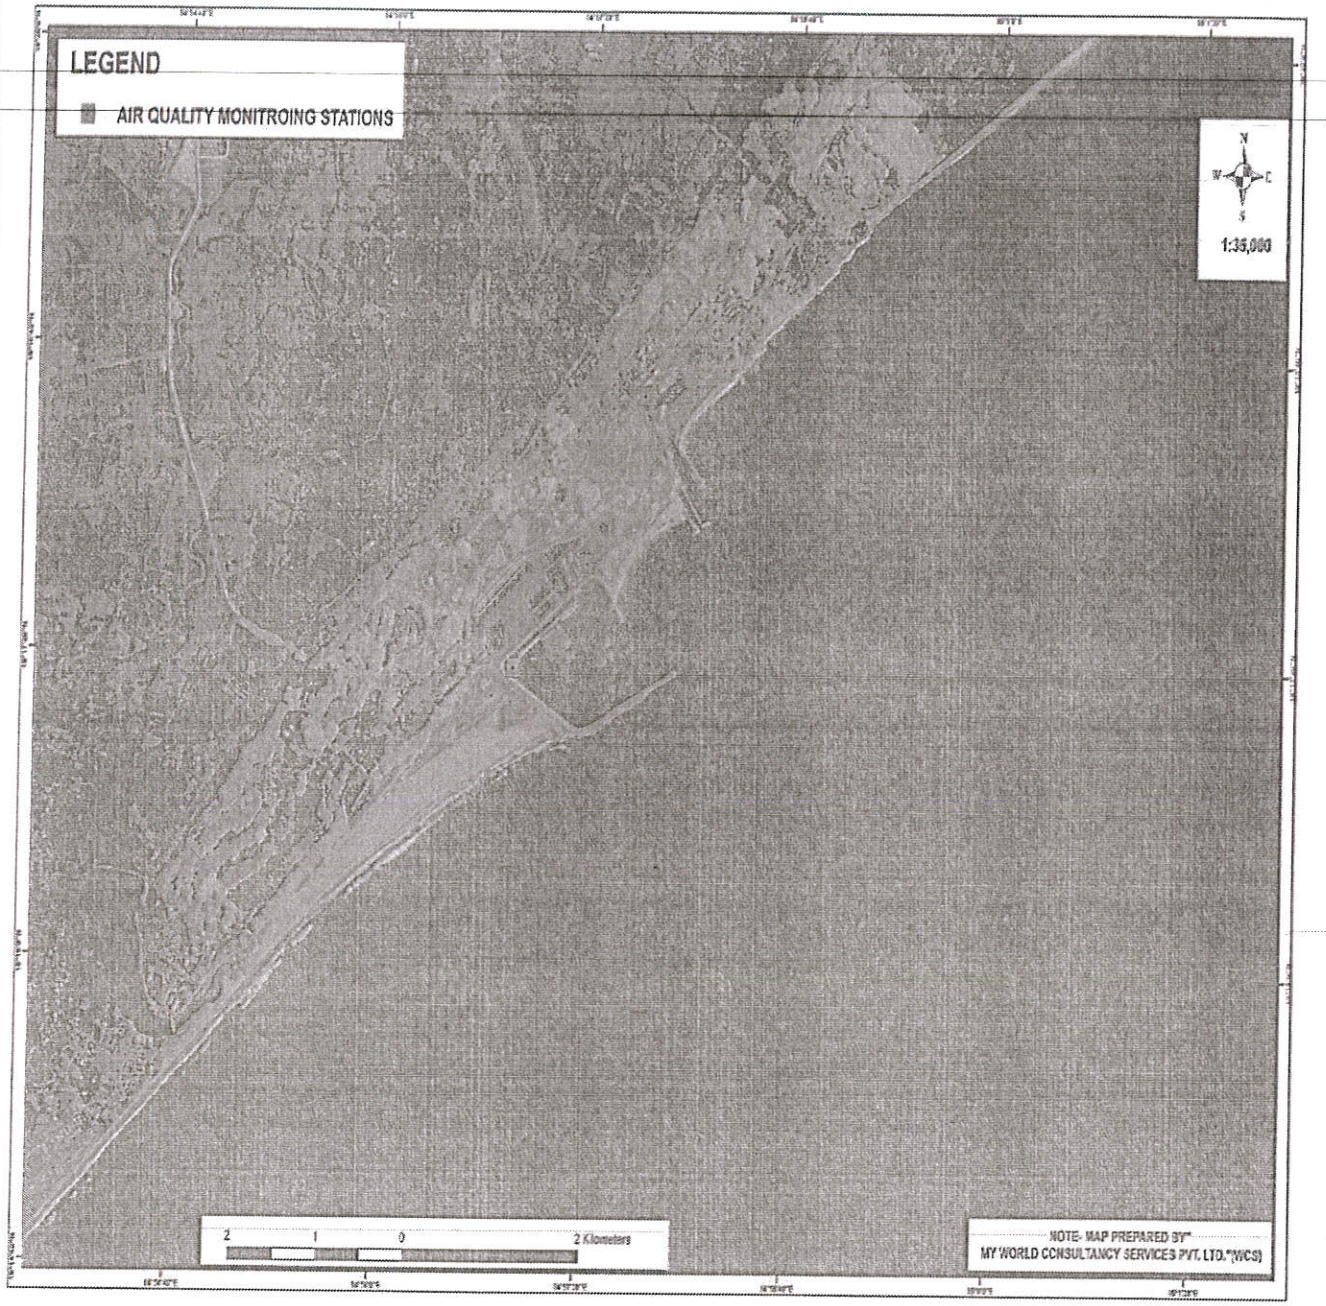


Figure 7: Location of air quality monitoring stations within the Gopalpur port area.

GOPALPUR PORTS LIMITED ODISHA INDIA

MY WORLD CONSULTANCY SERVICES PVT. LTD. CUTTACK

Table 2.1: Ambient Air Quality within Gopalpur Port premises Near Main Gate (Station-A) (PM10, PM2.5, SO2, NO2, NH3, O3, As, C6H6, BaP, Pb, Ni & CO)

Near Main Gate (Station-A)													
	Date	PM10 (µg/m³)	PM2.5 (µg/m³)	SO2 (µg/m³)	NO2 (µg/m³)	NH3 (µg/m³)	O_3 (µg/m³)	CO (mg/m³)	AS (ng/m³)	C_6H_6 (µg/m³)	BaP (ng/m³)	Pb (µg/m³)	Ni (µg/m³)
Oct-2025	03.10.2025	62.49	32.04	7.00	19.58	26.43	13.12	0.261	<1.0	<1.0	<1.0	<0.1	<1.0
	06.10.2025	59.00	30.26	6.61	18.49	24.96	12.39	0.247	<1.0	<1.0	<1.0	<0.1	<1.0
	09.10.2025	52.54	26.94	5.89	16.46	22.22	11.03	0.220	<1.0	<1.0	<1.0	<0.1	<1.0
	14.10.2025	50.94	26.13	5.71	15.96	21.55	10.70	0.213	<1.0	<1.0	<1.0	<0.1	<1.0
	17.10.2025	48.36	24.80	5.42	15.15	20.46	10.15	0.202	<1.0	<1.0	<1.0	<0.1	<1.0
	21.10.2025	51.54	26.43	5.77	16.15	21.80	10.82	0.216	<1.0	<1.0	<1.0	<0.1	<1.0
	24.10.2025	52.44	26.89	5.88	16.43	22.18	11.01	0.219	<1.0	<1.0	<1.0	<0.1	<1.0
	27.10.2025	40.10	20.56	4.49	12.57	16.96	8.42	0.168	<1.0	<1.0	<1.0	<0.1	<1.0
Nov-2025	03.11.2025	63.22	32.42	7.08	19.81	26.74	13.28	0.265	<1.0	<1.0	<1.0	<0.1	<1.0
	06.11.2025	59.93	30.73	6.71	18.78	25.35	12.59	0.251	<1.0	<1.0	<1.0	<0.1	<1.0
	10.11.2025	57.33	29.40	6.42	17.97	24.25	12.04	0.240	<1.0	<1.0	<1.0	<0.1	<1.0
	13.11.2025	66.05	33.87	7.40	20.70	27.94	13.87	0.276	<1.0	<1.0	<1.0	<0.1	<1.0
	17.11.2025	61.48	31.53	6.89	19.27	26.01	12.91	0.257	<1.0	<1.0	<1.0	<0.1	<1.0
	20.11.2025	60.36	30.95	6.76	18.91	25.53	12.67	0.253	<1.0	<1.0	<1.0	<0.1	<1.0
	24.11.2025	57.96	29.72	6.49	18.16	24.52	12.17	0.243	<1.0	<1.0	<1.0	<0.1	<1.0
	27.11.2025	62.95	32.28	7.05	19.73	26.63	13.22	0.263	<1.0	<1.0	<1.0	<0.1	<1.0
Dec-2025	01.12.2025	68.16	34.95	7.64	21.36	28.83	14.31	0.285	<1.0	<1.0	<1.0	<0.1	<1.0
	04.12.2025	70.15	35.97	7.86	21.98	29.67	14.73	0.294	<1.0	<1.0	<1.0	<0.1	<1.0
	08.12.2025	62.59	32.10	7.01	19.61	26.47	13.14	0.262	<1.0	<1.0	<1.0	<0.1	<1.0
	11.12.2025	65.47	33.57	7.34	20.52	27.69	13.75	0.274	<1.0	<1.0	<1.0	<0.1	<1.0
	15.12.2025	63.38	32.50	7.10	19.86	26.81	13.31	0.265	<1.0	<1.0	<1.0	<0.1	<1.0
	18.12.2025	68.16	34.95	7.64	21.36	28.83	14.31	0.285	<1.0	<1.0	<1.0	<0.1	<1.0
	22.12.2025	72.04	36.94	8.07	22.58	30.47	15.13	0.301	<1.0	<1.0	<1.0	<0.1	<1.0
	25.12.2025	74.23	38.07	8.32	23.26	31.40	15.59	0.311	<1.0	<1.0	<1.0	<0.1	<1.0
Jan-2026	02.01.2026	72.37	37.11	8.11	22.68	30.61	15.20	0.303	<1.0	<1.0	<1.0	<0.1	<1.0
	05.01.2026	74.34	38.12	8.33	23.30	31.44	15.61	0.311	<1.0	<1.0	<1.0	<0.1	<1.0
	09.01.2026	66.85	34.28	7.49	20.95	28.28	14.04	0.280	<1.0	<1.0	<1.0	<0.1	<1.0
	15.01.2026	69.65	35.72	7.80	21.83	29.46	14.63	0.291	<1.0	<1.0	<1.0	<0.1	<1.0
	19.01.2026	68.61	35.18	7.69	21.50	29.02	14.41	0.287	<1.0	<1.0	<1.0	<0.1	<1.0
	22.01.2026	72.42	37.14	8.11	22.69	30.63	15.21	0.303	<1.0	<1.0	<1.0	<0.1	<1.0
	27.01.2026	76.30	39.13	8.55	23.91	32.27	16.02	0.319	<1.0	<1.0	<1.0	<0.1	<1.0
	30.01.2026	78.44	40.22	8.79	24.58	33.18	16.47	0.328	<1.0	<1.0	<1.0	<0.1	<1.0
Feb-2026	02.02.2026	70.15	35.97	7.86	21.98	29.67	14.73	0.294	<1.0	<1.0	<1.0	<0.1	<1.0
	05.02.2026	73.25	37.57	8.21	22.96	30.99	15.38	0.306	<1.0	<1.0	<1.0	<0.1	<1.0
	09.02.2026	68.79	35.28	7.71	21.56	29.10	14.45	0.288	<1.0	<1.0	<1.0	<0.1	<1.0
	12.02.2026	70.90	36.36	7.94	22.22	29.99	14.89	0.297	<1.0	<1.0	<1.0	<0.1	<1.0
	16.02.2026	65.98	33.84	7.39	20.68	27.91	13.86	0.276	<1.0	<1.0	<1.0	<0.1	<1.0
	19.02.2026	70.47	36.14	7.90	22.08	29.81	14.80	0.295	<1.0	<1.0	<1.0	<0.1	<1.0
	23.02.2026	72.67	37.27	8.14	22.77	30.74	15.26	0.304	<1.0	<1.0	<1.0	<0.1	<1.0
	26.02.2026	74.98	38.45	8.40	23.50	31.72	15.75	0.314	<1.0	<1.0	<1.0	<0.1	<1.0
Mar-2026	02.03.2026	72.24	37.04	8.09	22.64	30.56	15.17	0.302	<1.0	<1.0	<1.0	<0.1	<1.0
	05.03.2026	70.17	35.98	7.86	21.99	29.68	14.74	0.294	<1.0	<1.0	<1.0	<0.1	<1.0
	09.03.2026	66.78	34.25	7.48	20.93	28.25	14.02	0.279	<1.0	<1.0	<1.0	<0.1	<1.0
	12.03.2026	68.98	35.38	7.73	21.62	29.18	14.49	0.289	<1.0	<1.0	<1.0	<0.1	<1.0
	16.03.2026	75.25	38.59	8.43	23.58	31.83	15.80	0.315	<1.0	<1.0	<1.0	<0.1	<1.0
	19.03.2026	67.66	34.70	7.58	21.20	28.62	14.21	0.283	<1.0	<1.0	<1.0	<0.1	<1.0
	23.03.2026	74.50	38.20	8.35	23.35	31.51	15.64	0.312	<1.0	<1.0	<1.0	<0.1	<1.0
	26.03.2026	66.63	34.17	7.46	20.88	28.18	13.99	0.279	<1.0	<1.0	<1.0	<0.1	<1.0
	Mean (range)	65.82	33.75	7.37	20.63	27.84	13.82	0.275	<1.0	<1.0	<1.0	<0.1	<1.0
Reference value (NAAQS, 2009)		100 (24 Hours)	60 (24 Hours)	80 (24 Hours)	80 (24 Hours)	400 (24 Hour)	180 (1 Hour)	4 (1 Hour)	6 (Annual)	5 (Annual)	1 (Annual)	1.0 (24 Hour)	20 (Annual)

GOPALPUR PORTS LIMITED
WORLD CONSULTANCY SERVICES PVT. LTD. CUTTACK


Table 2.2: Ambient Air Quality within Gopalpur Port premises Near Signal Station (Station-B) (PM10, PM2.5, SO2, NO2, NH3, O3, As, C6H6, BaP, Pb, Ni & CO)

Near Signal Station (Station-B)													
	Date	PM10 (µg/m³)	PM2.5 (µg/m³)	SO2 (µg/m³)	NO2 (µg/m³)	NH3 (µg/m³)	O_3 (µg/m³)	CO (mg/m³)	AS (ng/m³)	C_6H_6 (µg/m³)	BaP (ng/m³)	Pb (µg/m³)	Ni (µg/m³)
Oct-2025	03.10.2025	62.80	35.48	7.03	19.68	26.56	13.19	0.264	<1.0	<1.0	<1.0	<0.1	<1.0
	06.10.2025	59.30	33.50	6.64	18.58	25.08	12.45	0.249	<1.0	<1.0	<1.0	<0.1	<1.0
	09.10.2025	52.80	29.83	5.91	16.55	22.33	11.09	0.222	<1.0	<1.0	<1.0	<0.1	<1.0
	14.10.2025	51.20	28.93	5.73	16.05	21.66	10.75	0.215	<1.0	<1.0	<1.0	<0.1	<1.0
	17.10.2025	48.60	27.46	5.44	15.23	20.56	10.21	0.204	<1.0	<1.0	<1.0	<0.1	<1.0
	21.10.2025	51.80	29.27	5.80	16.23	21.91	10.88	0.218	<1.0	<1.0	<1.0	<0.1	<1.0
	24.10.2025	52.70	29.77	5.90	16.52	22.29	11.07	0.221	<1.0	<1.0	<1.0	<0.1	<1.0
	27.10.2025	40.30	22.77	4.51	12.63	17.05	8.46	0.169	<1.0	<1.0	<1.0	<0.1	<1.0
Nov-2025	03.11.2025	63.54	35.90	7.12	19.91	26.88	13.34	0.267	<1.0	<1.0	<1.0	<0.1	<1.0
	06.11.2025	60.23	34.03	6.74	18.87	25.48	12.65	0.253	<1.0	<1.0	<1.0	<0.1	<1.0
	10.11.2025	57.62	32.55	6.45	18.06	24.37	12.10	0.242	<1.0	<1.0	<1.0	<0.1	<1.0
	13.11.2025	66.38	37.50	7.43	20.80	28.08	13.94	0.279	<1.0	<1.0	<1.0	<0.1	<1.0
	17.11.2025	61.79	34.91	6.92	19.36	26.14	12.98	0.260	<1.0	<1.0	<1.0	<0.1	<1.0
	20.11.2025	60.66	34.27	6.79	19.01	25.66	12.74	0.255	<1.0	<1.0	<1.0	<0.1	<1.0
	24.11.2025	58.25	32.91	6.52	18.25	24.64	12.23	0.245	<1.0	<1.0	<1.0	<0.1	<1.0
	27.11.2025	63.27	35.75	7.09	19.83	26.76	13.29	0.266	<1.0	<1.0	<1.0	<0.1	<1.0
Dec-2025	01.12.2025	68.50	38.70	7.67	21.47	28.98	14.39	0.288	<1.0	<1.0	<1.0	<0.1	<1.0
	04.12.2025	70.50	39.83	7.89	22.09	29.82	14.81	0.296	<1.0	<1.0	<1.0	<0.1	<1.0
	08.12.2025	62.90	35.54	7.04	19.71	26.61	13.21	0.264	<1.0	<1.0	<1.0	<0.1	<1.0
	11.12.2025	65.80	37.18	7.37	20.62	27.83	13.82	0.276	<1.0	<1.0	<1.0	<0.1	<1.0
	15.12.2025	63.70	35.99	7.13	19.96	26.95	13.38	0.268	<1.0	<1.0	<1.0	<0.1	<1.0
	18.12.2025	68.50	38.70	7.67	21.47	28.98	14.39	0.288	<1.0	<1.0	<1.0	<0.1	<1.0
	22.12.2025	72.40	40.90	8.11	22.69	30.63	15.20	0.304	<1.0	<1.0	<1.0	<0.1	<1.0
	25.12.2025	74.60	42.15	8.35	23.38	31.56	15.67	0.313	<1.0	<1.0	<1.0	<0.1	<1.0
Jan-2026	02.01.2026	72.73	41.09	8.14	22.79	30.76	15.27	0.306	<1.0	<1.0	<1.0	<0.1	<1.0
	05.01.2026	74.71	42.21	8.37	23.41	31.60	15.69	0.314	<1.0	<1.0	<1.0	<0.1	<1.0
	09.01.2026	67.19	37.96	7.52	21.06	28.42	14.11	0.282	<1.0	<1.0	<1.0	<0.1	<1.0
	15.01.2026	70.00	39.55	7.84	21.94	29.61	14.70	0.294	<1.0	<1.0	<1.0	<0.1	<1.0
	19.01.2026	68.95	38.95	7.72	21.61	29.17	14.48	0.290	<1.0	<1.0	<1.0	<0.1	<1.0
	22.01.2026	72.78	41.12	8.15	22.81	30.79	15.28	0.306	<1.0	<1.0	<1.0	<0.1	<1.0
	27.01.2026	76.68	43.32	8.59	24.03	32.44	16.10	0.322	<1.0	<1.0	<1.0	<0.1	<1.0
	30.01.2026	78.83	44.54	8.83	24.70	33.35	16.55	0.331	<1.0	<1.0	<1.0	<0.1	<1.0
Feb-2026	02.02.2026	70.50	39.83	7.89	22.09	29.82	14.81	0.296	<1.0	<1.0	<1.0	<0.1	<1.0
	05.02.2026	73.62	41.59	8.24	23.07	31.14	15.46	0.309	<1.0	<1.0	<1.0	<0.1	<1.0
	09.02.2026	69.14	39.06	7.74	21.67	29.25	14.52	0.291	<1.0	<1.0	<1.0	<0.1	<1.0
	12.02.2026	71.26	40.26	7.98	22.33	30.14	14.96	0.299	<1.0	<1.0	<1.0	<0.1	<1.0
	16.02.2026	66.31	37.46	7.43	20.78	28.05	13.93	0.279	<1.0	<1.0	<1.0	<0.1	<1.0
	19.02.2026	70.82	40.01	7.93	22.19	29.96	14.87	0.298	<1.0	<1.0	<1.0	<0.1	<1.0
	23.02.2026	73.04	41.27	8.18	22.89	30.90	15.34	0.307	<1.0	<1.0	<1.0	<0.1	<1.0
	26.02.2026	75.36	42.58	8.44	23.62	31.88	15.83	0.317	<1.0	<1.0	<1.0	<0.1	<1.0
Mar-2026	02.03.2026	72.60	41.02	8.13	22.75	30.71	15.25	0.305	<1.0	<1.0	<1.0	<0.1	<1.0
	05.03.2026	70.52	39.84	7.90	22.10	29.83	14.81	0.296	<1.0	<1.0	<1.0	<0.1	<1.0
	09.03.2026	67.12	37.92	7.52	21.03	28.39	14.10	0.282	<1.0	<1.0	<1.0	<0.1	<1.0
	12.03.2026	69.33	39.17	7.76	21.73	29.33	14.56	0.291	<1.0	<1.0	<1.0	<0.1	<1.0
	16.03.2026	75.63	42.73	8.47	23.70	31.99	15.88	0.318	<1.0	<1.0	<1.0	<0.1	<1.0
	19.03.2026	68.00	38.42	7.61	21.31	28.76	14.28	0.286	<1.0	<1.0	<1.0	<0.1	<1.0
	23.03.2026	74.87	42.30	8.38	23.46	31.67	15.72	0.315	<1.0	<1.0	<1.0	<0.1	<1.0
	26.03.2026	66.96	37.83	7.50	20.98	28.32	14.06	0.281	<1.0	<1.0	<1.0	<0.1	<1.0
	Mean (range)	66.15	37.37	7.41	20.73	27.98	13.89	0.278	<1.0	<1.0	<1.0	<0.1	<1.0
Reference value (NAAQS, 2009)		100 (24 Hours)	60 (24 Hours)	80 (24 Hours)	80 (24 Hours)	400 (24 Hour)	180 (1 Hour)	4 (1 Hour)	6 (Annual)	5 (Annual)	1 (Annual)	1.0 (24 Hour)	20 (Annual)

GOPALPUR PORTS LIMITED ODISHA INDIA
MV WORLD CONSULTANCY SERVICES PVT. LTD. CUTTACK

Table 2.3: Ambient Air Quality within Gopalpur Port premises SubStation-2 (Station-C) (PM10, PM2.5, SO2, NO2, NH3, O3, As, C6H6, BaP, Pb, Ni & CO)

SubStation-2 (Station-C)													
	Date	PM10 (µg/m³)	PM2.5 (µg/m³)	SO2 (µg/m³)	NO2 (µg/m³)	NH3 (µg/m³)	O_3 (µg/m³)	CO (mg/m³)	AS (ng/m³)	C_6H_6 (µg/m³)	BaP (ng/m³)	Pb (µg/m³)	Ni (µg/m³)
Oct-2025	03.10.2025	60.66	32.44	6.80	19.01	25.66	12.74	0.254	<1.0	<1.0	<1.0	<0.1	<1.0
	06.10.2025	57.28	30.63	6.42	17.95	24.23	12.03	0.240	<1.0	<1.0	<1.0	<0.1	<1.0
	09.10.2025	51.00	27.28	5.72	15.98	21.58	10.71	0.213	<1.0	<1.0	<1.0	<0.1	<1.0
	14.10.2025	49.46	26.45	5.54	15.50	20.92	10.39	0.207	<1.0	<1.0	<1.0	<0.1	<1.0
	17.10.2025	46.95	25.11	5.26	14.71	19.86	9.86	0.196	<1.0	<1.0	<1.0	<0.1	<1.0
	21.10.2025	50.04	26.76	5.61	15.68	21.17	10.51	0.209	<1.0	<1.0	<1.0	<0.1	<1.0
	24.10.2025	50.91	27.22	5.71	15.95	21.53	10.69	0.213	<1.0	<1.0	<1.0	<0.1	<1.0
	27.10.2025	38.93	20.82	4.36	12.20	16.47	8.18	0.163	<1.0	<1.0	<1.0	<0.1	<1.0
Nov-2025	03.11.2025	61.38	32.82	6.88	19.24	25.96	12.89	0.257	<1.0	<1.0	<1.0	<0.1	<1.0
	06.11.2025	58.18	31.11	6.52	18.23	24.61	12.22	0.243	<1.0	<1.0	<1.0	<0.1	<1.0
	10.11.2025	55.66	29.77	6.24	17.44	23.54	11.69	0.233	<1.0	<1.0	<1.0	<0.1	<1.0
	13.11.2025	64.12	34.29	7.19	20.09	27.12	13.47	0.268	<1.0	<1.0	<1.0	<0.1	<1.0
	17.11.2025	59.69	31.92	6.69	18.71	25.25	12.53	0.250	<1.0	<1.0	<1.0	<0.1	<1.0
	20.11.2025	58.60	31.34	6.57	18.36	24.79	12.31	0.245	<1.0	<1.0	<1.0	<0.1	<1.0
	24.11.2025	56.27	30.09	6.31	17.63	23.80	11.82	0.235	<1.0	<1.0	<1.0	<0.1	<1.0
	27.11.2025	61.12	32.68	6.85	19.15	25.85	12.83	0.256	<1.0	<1.0	<1.0	<0.1	<1.0
Dec-2025	01.12.2025	66.17	35.39	7.42	20.74	27.99	13.90	0.277	<1.0	<1.0	<1.0	<0.1	<1.0
	04.12.2025	68.10	36.42	7.63	21.34	28.81	14.30	0.285	<1.0	<1.0	<1.0	<0.1	<1.0
	08.12.2025	60.76	32.49	6.81	19.04	25.70	12.76	0.254	<1.0	<1.0	<1.0	<0.1	<1.0
	11.12.2025	63.56	33.99	7.13	19.92	26.89	13.35	0.266	<1.0	<1.0	<1.0	<0.1	<1.0
	15.12.2025	61.53	32.91	6.90	19.28	26.03	12.92	0.257	<1.0	<1.0	<1.0	<0.1	<1.0
	18.12.2025	66.17	35.39	7.42	20.74	27.99	13.90	0.277	<1.0	<1.0	<1.0	<0.1	<1.0
	22.12.2025	69.94	37.40	7.84	21.92	29.58	14.69	0.293	<1.0	<1.0	<1.0	<0.1	<1.0
	25.12.2025	72.06	38.54	8.08	22.58	30.48	15.13	0.302	<1.0	<1.0	<1.0	<0.1	<1.0
Jan-2026	02.01.2026	70.26	37.57	7.88	22.02	29.72	14.75	0.294	<1.0	<1.0	<1.0	<0.1	<1.0
	05.01.2026	72.17	38.59	8.09	22.62	30.53	15.16	0.302	<1.0	<1.0	<1.0	<0.1	<1.0
	09.01.2026	64.91	34.71	7.28	20.34	27.46	13.63	0.272	<1.0	<1.0	<1.0	<0.1	<1.0
	15.01.2026	67.62	36.16	7.58	21.19	28.60	14.20	0.283	<1.0	<1.0	<1.0	<0.1	<1.0
	19.01.2026	66.61	35.62	7.47	20.87	28.17	13.99	0.279	<1.0	<1.0	<1.0	<0.1	<1.0
	22.01.2026	70.31	37.60	7.88	22.03	29.74	14.76	0.294	<1.0	<1.0	<1.0	<0.1	<1.0
	27.01.2026	74.07	39.61	8.30	23.21	31.33	15.56	0.310	<1.0	<1.0	<1.0	<0.1	<1.0
	30.01.2026	76.15	40.72	8.54	23.86	32.21	15.99	0.319	<1.0	<1.0	<1.0	<0.1	<1.0
Feb-2026	02.02.2026	68.10	36.42	7.63	21.34	28.81	14.30	0.285	<1.0	<1.0	<1.0	<0.1	<1.0
	05.02.2026	71.12	38.03	7.97	22.29	30.08	14.93	0.298	<1.0	<1.0	<1.0	<0.1	<1.0
	09.02.2026	66.79	35.72	7.49	20.93	28.25	14.03	0.279	<1.0	<1.0	<1.0	<0.1	<1.0
	12.02.2026	68.84	36.81	7.72	21.57	29.12	14.46	0.288	<1.0	<1.0	<1.0	<0.1	<1.0
	16.02.2026	64.06	34.25	7.18	20.07	27.10	13.45	0.268	<1.0	<1.0	<1.0	<0.1	<1.0
	19.02.2026	68.41	36.58	7.67	21.44	28.94	14.37	0.286	<1.0	<1.0	<1.0	<0.1	<1.0
	23.02.2026	70.56	37.73	7.91	22.11	29.85	14.82	0.295	<1.0	<1.0	<1.0	<0.1	<1.0
	26.02.2026	72.80	38.93	8.16	22.81	30.79	15.29	0.305	<1.0	<1.0	<1.0	<0.1	<1.0
Mar-2026	02.03.2026	70.13	37.50	7.86	21.98	29.67	14.73	0.293	<1.0	<1.0	<1.0	<0.1	<1.0
	05.03.2026	68.12	36.43	7.64	21.35	28.82	14.31	0.285	<1.0	<1.0	<1.0	<0.1	<1.0
	09.03.2026	64.84	34.67	7.27	20.32	27.43	13.62	0.271	<1.0	<1.0	<1.0	<0.1	<1.0
	12.03.2026	66.97	35.81	7.51	20.99	28.33	14.06	0.280	<1.0	<1.0	<1.0	<0.1	<1.0
	16.03.2026	73.06	39.07	8.19	22.90	30.90	15.34	0.306	<1.0	<1.0	<1.0	<0.1	<1.0
	19.03.2026	65.69	35.13	7.36	20.59	27.79	13.79	0.275	<1.0	<1.0	<1.0	<0.1	<1.0
	23.03.2026	72.32	38.68	8.11	22.67	30.59	15.19	0.303	<1.0	<1.0	<1.0	<0.1	<1.0
	26.03.2026	64.68	34.59	7.25	20.27	27.36	13.58	0.271	<1.0	<1.0	<1.0	<0.1	<1.0
	Mean (range)	63.90	34.17	7.16	20.02	27.03	13.42	0.267	<1.0	<1.0	<1.0	<0.1	<1.0
Reference value (NAAQS, 2009)		100 (24 Hours)	60 (24 Hours)	80 (24 Hours)	80 (24 Hours)	400 (24 Hour)	~~180~~ (1 Hour)	~~4~~ (1 Hour)	~~6~~ (Annual)	5 (Annual)	1 (Annual)	1.0 (24 Hour)	20 (Annual)








Table 2.4: Ambient Air Quality within Gopalpur Port premises SubStation-4 (Station-D) (PM10, PM2.5, SO2, NO2, NH3, O3, As, C6H6, BaP, Pb, Ni & CO)

SubStation-4 (Station-D)													
	Date	PM10 (µg/m³)	PM2.5 (µg/m³)	SO2 (µg/m³)	NO2 (µg/m³)	NH3 (µg/m³)	O_3 (µg/m³)	CO (mg/m³)	AS (ng/m³)	C_6H_6 (µg/m³)	BaP (ng/m³)	Pb (µg/m³)	Ni (µg/m³)
Oct-2025	03.10.2025	55.77	28.31	6.25	17.48	23.59	13.22	0.233	<1.0	<1.0	<1.0	<0.1	<1.0
	06.10.2025	52.66	26.73	5.90	16.50	22.27	12.48	0.220	<1.0	<1.0	<1.0	<0.1	<1.0
	09.10.2025	46.89	23.80	5.26	14.69	19.83	11.11	0.196	<1.0	<1.0	<1.0	<0.1	<1.0
	14.10.2025	45.47	23.08	5.10	14.25	19.23	10.78	0.190	<1.0	<1.0	<1.0	<0.1	<1.0
	17.10.2025	43.16	21.91	4.84	13.52	18.26	10.23	0.181	<1.0	<1.0	<1.0	<0.1	<1.0
	21.10.2025	46.00	23.35	5.16	14.42	19.46	10.90	0.192	<1.0	<1.0	<1.0	<0.1	<1.0
	24.10.2025	46.80	23.76	5.25	14.67	19.80	11.09	0.196	<1.0	<1.0	<1.0	<0.1	<1.0
	27.10.2025	35.79	18.17	4.01	11.21	15.14	8.48	0.150	<1.0	<1.0	<1.0	<0.1	<1.0
Nov-2025	03.11.2025	56.42	28.64	6.33	17.68	23.87	13.37	0.236	<1.0	<1.0	<1.0	<0.1	<1.0
	06.11.2025	53.48	27.15	6.00	16.76	22.62	12.68	0.224	<1.0	<1.0	<1.0	<0.1	<1.0
	10.11.2025	51.17	25.97	5.74	16.03	21.64	12.13	0.214	<1.0	<1.0	<1.0	<0.1	<1.0
	13.11.2025	58.95	29.92	6.61	18.47	24.93	13.97	0.247	<1.0	<1.0	<1.0	<0.1	<1.0
	17.11.2025	54.87	27.85	6.15	17.20	23.21	13.00	0.230	<1.0	<1.0	<1.0	<0.1	<1.0
	20.11.2025	53.87	27.34	6.04	16.88	22.79	12.77	0.225	<1.0	<1.0	<1.0	<0.1	<1.0
	24.11.2025	51.73	26.26	5.80	16.21	21.88	12.26	0.216	<1.0	<1.0	<1.0	<0.1	<1.0
	27.11.2025	56.18	28.52	6.30	17.61	23.77	13.32	0.235	<1.0	<1.0	<1.0	<0.1	<1.0
Dec-2025	01.12.2025	60.83	30.88	6.82	19.06	25.73	14.42	0.255	<1.0	<1.0	<1.0	<0.1	<1.0
	04.12.2025	62.60	31.78	7.02	19.62	26.48	14.84	0.262	<1.0	<1.0	<1.0	<0.1	<1.0
	08.12.2025	55.86	28.35	6.26	17.50	23.63	13.24	0.234	<1.0	<1.0	<1.0	<0.1	<1.0
	11.12.2025	58.43	29.66	6.55	18.31	24.72	13.85	0.244	<1.0	<1.0	<1.0	<0.1	<1.0
	15.12.2025	56.57	28.71	6.34	17.73	23.93	13.41	0.237	<1.0	<1.0	<1.0	<0.1	<1.0
	18.12.2025	60.83	30.88	6.82	19.06	25.73	14.42	0.255	<1.0	<1.0	<1.0	<0.1	<1.0
	22.12.2025	64.29	32.64	7.21	20.15	27.20	15.24	0.269	<1.0	<1.0	<1.0	<0.1	<1.0
	25.12.2025	66.24	33.63	7.43	20.76	28.02	15.70	0.277	<1.0	<1.0	<1.0	<0.1	<1.0
Jan-2026	02.01.2026	64.58	32.78	7.24	20.24	27.32	15.31	0.270	<1.0	<1.0	<1.0	<0.1	<1.0
	05.01.2026	66.34	33.68	7.44	20.79	28.06	15.72	0.278	<1.0	<1.0	<1.0	<0.1	<1.0
	09.01.2026	59.66	30.29	6.69	18.70	25.24	14.14	0.250	<1.0	<1.0	<1.0	<0.1	<1.0
	15.01.2026	62.16	31.55	6.97	19.48	26.29	14.73	0.260	<1.0	<1.0	<1.0	<0.1	<1.0
	19.01.2026	61.23	31.08	6.86	19.19	25.90	14.51	0.256	<1.0	<1.0	<1.0	<0.1	<1.0
	22.01.2026	64.63	32.81	7.25	20.25	27.34	15.32	0.270	<1.0	<1.0	<1.0	<0.1	<1.0
	27.01.2026	68.09	34.56	7.63	21.34	28.80	16.14	0.285	<1.0	<1.0	<1.0	<0.1	<1.0
	30.01.2026	70.00	35.53	7.85	21.94	29.61	16.59	0.293	<1.0	<1.0	<1.0	<0.1	<1.0
Feb-2026	02.02.2026	62.60	31.78	7.02	19.62	26.48	14.84	0.262	<1.0	<1.0	<1.0	<0.1	<1.0
	05.02.2026	65.37	33.19	7.33	20.49	27.65	15.49	0.274	<1.0	<1.0	<1.0	<0.1	<1.0
	09.02.2026	61.40	31.17	6.88	19.24	25.97	14.55	0.257	<1.0	<1.0	<1.0	<0.1	<1.0
	12.02.2026	63.28	32.12	7.09	19.83	26.77	15.00	0.265	<1.0	<1.0	<1.0	<0.1	<1.0
	16.02.2026	58.88	29.89	6.60	18.45	24.91	13.96	0.246	<1.0	<1.0	<1.0	<0.1	<1.0
	19.02.2026	62.89	31.92	7.05	19.71	26.60	14.90	0.263	<1.0	<1.0	<1.0	<0.1	<1.0
	23.02.2026	64.86	32.92	7.27	20.33	27.44	15.37	0.271	<1.0	<1.0	<1.0	<0.1	<1.0
	26.02.2026	66.92	33.97	7.50	20.97	28.31	15.86	0.280	<1.0	<1.0	<1.0	<0.1	<1.0
Mar-2026	02.03.2026	64.47	32.73	7.23	20.20	27.27	15.28	0.270	<1.0	<1.0	<1.0	<0.1	<1.0
	05.03.2026	62.62	31.79	7.02	19.62	26.49	14.84	0.262	<1.0	<1.0	<1.0	<0.1	<1.0
	09.03.2026	59.60	30.26	6.68	18.68	25.21	14.13	0.249	<1.0	<1.0	<1.0	<0.1	<1.0
	12.03.2026	61.57	31.25	6.90	19.29	26.04	14.59	0.258	<1.0	<1.0	<1.0	<0.1	<1.0
	16.03.2026	67.16	34.09	7.53	21.05	28.41	15.92	0.281	<1.0	<1.0	<1.0	<0.1	<1.0
	19.03.2026	60.38	30.65	6.77	18.92	25.54	14.31	0.253	<1.0	<1.0	<1.0	<0.1	<1.0
	23.03.2026	66.48	33.75	7.45	20.84	28.12	15.76	0.278	<1.0	<1.0	<1.0	<0.1	<1.0
	26.03.2026	59.46	30.18	6.67	18.63	25.15	14.09	0.249	<1.0	<1.0	<1.0	<0.1	<1.0
	Mean (range)	58.74	29.82	6.59	18.41	24.85	13.92	0.246	<1.0	<1.0	<1.0	<0.1	<1.0
Reference value (NAAQS, 2009)		100 (24 Hour)	60 (24 Hour)	80 (24 Hours)	80 (24 Hours)	400 (24 Hour)	180 (1 Hour)	4 (1 Hour)	6 (Annual)	5 (Annual)	1 (Annual)	1.0 (24 Hour)	20 (Annual)





3. Noise level monitoring:

The noise level monitoring was carried out at different selected locations according to its importance. The highest average noise level was recorded at station "A" (Near Main Gate) due to high Vehicular movement and the lowest value was recorded at station "D" (Substation-4). The average day and night noise And monitoring values al station A-19°18'51.59" N 84°58'6.88" E (Near Main Gate), B-19°18'29.18" N 84°57'40.84" E (At Signal Station), C-19°17'45.3" N 84°57'19.79" E (At Substation-2),D-19°17'17.72" N 84°56'51.72" E (At Substation-4), from October 2025 to March 2026 are presented in Table 3.1.

The noise level monitored during the day and night time is also well within the NAAQ thresholds stipulated by MoEFCC for industrial 75dB in day time and 70dB during night time zones.

Table 3.1: Noise level (dB) within Gopalpur Port premises at station A, B, C, and D during Day Time

Day Time					
Month	**Date**	**Station A**	**Station B**	**Station C**	**Station D**
Oct 2025	17.10.2025	63.8	61.3	57.9	59.6
Nov 2025	15.11.2025	62.8	63.3	58.9	58.4
Dec 2025	17.12.2025	63.8	62.5	56.8	57.9
Jan 2026	09.01.2026	64.1	62.8	55.4	58.2
Feb 2026	16.02.2026	63.6	64.5	57.2	55.3
Mar 2026	17.03.2026	62.8	64.7	58.3	54.4
Avg.		**63.5**	**63.2**	**57.4**	**57.3**

Table 3.2: Noise level (dB) within Gopalpur Port premises at station A, B, C, and D during Night Time

Night Time					
Month	**Date**	**Station A**	**Station B**	**Station C**	**Station D**
Oct 2025	17.10.2025	59.2	56.1	52.4	53.5
Nov 2025	15.11.2025	58.7	55.8	53.6	54.1
Dec 2025	17.12.2025	58.2	56.3	52.8	53.4
Jan 2026	09.01.2026	58.6	55.2	51.4	52.3
Feb 2026	16.02.2026	52.4	50.6	48.3	46.7
Mar 2026	17.03.2026	51.3	51.0	47.2	43.5
Avg.		**56.4**	**54.2**	**51.0**	**50.6**

4. The DG Stack Monitoring

DG Stack available inside the port premises and their observed value from October 2025 to March 2026 are presented in Table 4.1 and Table 4.2

Table 4.1: DG stack parameters with in Gopalpur port (DG-1, DG-2, DG-3)

Central Store DG-1 (100KVA)						
	Oct 2025	**Nov 2025**	**Dec 2025**	**Jan 2026**	**Feb 2026**	**March 2026**
Flue Gas Temperature (K)	438	443	435	429	431	423.6
Flue Gas Velocity	12.86	13.58	12.92	13.02	12.88	13.05
Quantity of gas flow in Nm3/hr	150.68	159.15	162.3	159.8	146.7	138.24
Particulate Metter (PM)	0.16	0.15	0.18	0.16	0.13	0.16
NOx+HC	0.22	0.18	0.2	0.17	0.21	0.23
Carbon Monoxide as CO	0.2	0.19	0.2	0.21	0.16	0.13
Concentration of Sulphur Dioxide as SO2	0.12	0.14	0.16	0.04	0.08	0.11

GOPALPUR PORT LIMITED

WORLD CONSULTANCY SERVICES PVT. LTD. CUTTACK

Meter Room DG-2 (100KVA)						
	Oct 2025	Nov 2025	Dec 2025	Jan 2026	Feb 2026	March 2026
Flue Gas Temperature (K)	449	448	445	461	455.3	441.5
Flue Gas Velocity	12.53	13.78	13.25	13.65	13.21	12.84
Quantity of gas flow in Nm3/hr	155.24	159.77	158.4	160.4	156.3	143.13
Particulate Metter (PM)	0.11	0.12	0.14	0.15	0.17	0.14
NOx+HC	0.2	0.19	0.22	0.2	0.24	0.24
Carbon Monoxide as CO	0.22	0.20	0.16	0.18	0.22	0.20
Concentration of Sulphur Dioxide as SO2	0.13	0.16	0.14	0.16	0.13	0.14

Substation-4 DG-3 (100KVA)						
	Oct 2025	Nov 2025	Dec 2025	Jan 2026	Feb 2026	March 2026
Flue Gas Temperature (K)	432	437	430	438	428.6	436.2
Flue Gas Velocity	12.48	12.4	12.53	12.22	13.07	11.7
Quantity of gas flow in Nm3/hr	148.63	147.41	144.80	145.22	141.60	134.71
Particulate Metter (PM)	0.15	0.17	0.16	0.14	0.16	0.17
NOx+HC	0.18	0.22	0.18	0.19	0.2	0.22
Carbon Monoxide as CO	0.18	0.16	0.18	0.21	0.24	0.27
Concentration of Sulphur Dioxide as SO2	0.15	0.13	0.15	0.12	0.15	0.17

Table 4.2: DG stack parameters with in Gopalpur port (DG-4, DG-5, DG-6)

Meter Room DG-4 (250KVA)						
	Oct 2025	Nov 2025	Dec 2025	Jan 2026	Feb 2026	Mar 2026
Flue Gas Temperature (K)	440	445	448	445	451.2	440.8
Flue Gas Velocity	11.85	12.76	11.86	11.36	12.64	11.93
Quantity of gas flow in Nm3/hr	158.02	148.96	151.7	150.6	153.2	140.64
Particulate Metter (PM)	0.18	0.16	0.14	0.17	0.14	0.15
NOx+HC	0.24	0.25	0.23	0.21	0.23	0.25
Carbon Monoxide as CO	0.16	0.18	0.22	0.23	0.2	0.23
Concentration of Sulphur Dioxide as SO2	0.12	0.15	0.18	0.13	0.11	0.12

Colony DG-5 (250KVA)						
	Oct 2025	Nov 2025	Dec 2025	Jan 2026	Feb 2026	Mar 2026
Flue Gas Temperature (K)	416	427	421	456	434.6	427.4
Flue Gas Velocity	12.05	12.4	12.64	13.24	11.82	12.57
Quantity of gas flow in Nm3/hr	152.81	150.82	149.20	148.45	132.60	144.85
Particulate Metter (PM)	0.14	0.13	0.12	0.13	0.18	0.16
NOx+HC	0.19	0.21	0.25	0.23	0.26	0.27
Carbon Monoxide as CO	0.2	0.15	0.14	0.17	0.18	0.2
Concentration of Sulphur Dioxide as SO2	0.11	0.14	0.12	0.14	0.16	0.15

GOPALPUR PORT LIMITED ODISHA INDIA

MY WORLD CONSULTANCY SERVICES PVT. LTD. CUTTACK

Substation-1 DG-6 (250KVA)						
	Oct 2025	Nov 2025	Dec 2025	Jan 2026	Feb 2026	Mar 2026
Flue Gas Temperature (K)	435	424	432	420	437.2	433.9
Flue Gas Velocity	11.64	12.63	13.12	13.68	12.47	13.14
Quantity of gas flow in Nm3/hr	154.04	154.66	157.2	156.33	146.3	137.25
Particulate Metter (PM)	0.16	0.18	0.15	0.17	0.15	0.18
NOx+HC	0.21	0.20	0.16	0.18	0.22	0.23
Carbon Monoxide as CO	0.24	0.14	0.18	0.2	0.16	0.18
Concentration of Sulphur Dioxide as SO2	0.14	0.12	0.16	0.12	0.1	0.13

5. Domestic effluent water


The domestic effluent water sample was collected from the outlet of the sewage treatment plant inside the Gopalpur port. Different water quality parameters were analysed to understand the water quality of the domestic effluent discharge. The average value of the different parameters like pH (7.701), BOD (7.0), COD (36.3), Suspended solid (62.72) and oil and grease (<4.0) during the last six months (October 2025 to March 2026) and the monthly analysed values are depicted in table 5.1.

Table 5.1 Domestic effluent parameters of the Gopalpur port

Table 5.1 Domestic effluent parameters of the Gopalpur port

Parameter	Oct 2025	Nov 2025	Dec 2025	Jan 2026	Feb 2026	Mar 2026
pH Value	8.015 at 26.8	7.942 at 25.1	7.654 at 25.4°C	7.182 at 25.0°C	7.759 at 25.3°C	7.654 at 25.7°C
Total Suspended Solid as TSS	61.8	69.9	61.9	56.2	67.9	58.6
Biochemical Oxygen Demand as BOD	6.2	7.4	6.5	8.1	7.2	6.8
Chemical Oxygen Demand as COD	32	38	36	40	35	37
Oil &Grease	<4.0	<4.0	<4.0	<4.0	<4.0	<4.0
Faecal Coliform	300	240	280	220	300	280





6. Marine Water quality

Water samples were collected from port berth area (19°17'21" N 84°56' 55" E) for determination of their physico-chemical and biological properties. The samples were taken to the laboratory soon after the collection, Due care was taken to avoid contamination during sampling. The chemical and biological properties of water and sediment samples were measured following prescribed methods by Indian Standards, The detail observed/analyzed parameters and their threshold values are provided below.

Water quality parameters such as pH, dissolved oxygen (DO), color and odour, faecal coliform, biological oxygen demand (BOD), Lead, Cadmium, Hexavalent Chromium, Total Chromium, Copper, Zinc, Selenium, Nickel, Cyanide, Fluoride, Phosphorous, Sulphide, Phenolic Compound, Bio-Assay, Manganese, Iron, Vanadium, Nitrate for the period from October 2025 to March 2026 of Gopalpur port (harbour area) are presented in Table 6.1. It is evident that most of the parameters are well within the permissible limit/standard. During the observation period it is noticed that pH of water ranged from 7.658-8.801 with mean value of 8.03, representing alkaline nature of the harbour area. The maximum and minimum values were recorded during October 2025 to March 2026 respectively The Dissolved Oxygen ranges from 5.8-6.6 with average value of 6.12 mg/l for last six month.

The maximum Dissolved Oxygen was recorded during Nov 2025 and the minimum value was recorded during Jan 2026. The Faecal coliform values ranged from 220-300 MPN/100ml with average value of 253.3 MPN/100ml. The maximum value was recorded during Nov 2025 & Feb 2026, and the minimum value was recorded during December 2025 & March 2026. The BOD value ranged from 3.6-4.8 with average value of 4.2 mg/l. The maximum value was recorded during December 2025 and the minimum value was recorded during Jan 2026.The Phosphate concentration was ranged between 0.054 to 0.098 with average value of 0.069 mg/l during last six months. Nitrate concentration ranged between 0.94 to 6.46 mg/l with average value of 2.75 mg/l, the maximum value recorded during the month of October 2025 and the minimum value recorded during the month of Jan 2026. The Hexavalent chromium varied from <0.01 to 0.33 mg/l with average value of 0.25 mg/l.

From the analysis of water quality parameters, it can be stated that the water quality of harbour area is good as almost all parameters are well within the permissible limits.


GOPALPUR PORT LIMITED ODISHA INDIA

MY WORLD CONSULTANCY SERVICES PVT. LTD. CUTTACK

Table 6.1: Marine Water Quality parameters during October 2025 to March 2026 from Gopalpur port, Harbor area.

Water Parameters	Oct 2025	Nov 2025	Dec 2025	Jan 2026	Feb 2026	Mar 2026	Average	Method
pH Value	8.801 at 27.1°C	7.982 at 24.8	8.223 at 24.6°C	7.681 at 25.1°C	7.845 at 25.5°C	7.658 at 25.2°C	8.03	IS 3025 (Part-11): 2022
Dissolve Oxygen as DO	6	6.6	6.2	5.8	6.1	6	6.12	IS 3025 (Part 38): 1989 RA 2019
Colour	10	5	5	3	5	3	5.2	IS 3025 (Part 4): 2021
Odour	Agreeable	Agreeable	Agreeable	Agreeable	Agreeable	Agreeable	Agreeable	IS 3025 (Part-5): 2018
Faecal Coliform	240	300	220	240	300	220	253.3	IS 1622: 1981 RA 2019
Biochemical Oxygen Demand as BOD (3 Days)	4.2	3.7	4.8	3.6	4.3	4.6	4.20	IS 3025 (Part 44): 2023
Lead as Pb	0.35	0.3	0.34	0.31	0.24	0.32	0.31	IS 3025(Part-47):2024
Cadmium as Cd	0.026	0.022	0.024	0.029	0.02	0.026	0.025	IS 3025(Part-41)1992 RA 2023
Hexavalent Chromium as Cr+6	<0.01	<0.01	0.33	0.24	0.19	0.22	0.25	IS 3025 (Part-52): 2003 RA 2019
Total Chromium as Cr	<0.01	<0.01	0.33	0.24	0.19	0.22	0.25	IS 3025 (Part-52): 2003 RA 2019
Copper as Cu	0.08	0.06	0.07	0.04	0.02	0.03	0.05	IS 3025 (Part 42): 2024
Zinc as Zn	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	IS 3025 (Part-49): 1994
selenium	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05	IS 3025(Part-56)2003 RA 2023
Nickel as Ni	0.034	0.031	<0.05	<0.05	<0.05	<0.05	<0.05	IS 3025(Part-54)2003 RA 2019
Cyanide as CN	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001	IS 3025 (Part-27): 1986
Fluoride as F	<0.02	<0.02	0.193	0.083	0.077	0.082	0.109	APHA 24th Ed. (4500-F- D): 2023
Phosphorus as P	0.072	0.068	0.098	0.062	0.058	0.054	0.069	IS 3025 (Part-31): Sec-1:2022
Sulphide	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001	IS 3025(Part-29)2022
Phenolic compounds as C_6H_5OH	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001	<0.001	IS 3025 (Part 43)1992 RA 2019
Bio-Assay	100 % Survival of the fish in 100% Raw water within 24 hr.	100 % Survival of the fish in 100% Raw water within 24 hr.	100 % Survival of the fish in 100% Raw water within 24 hr.	100 % Survival of the fish in 100% Raw water within 24 hr.	100 % Survival of the fish in 100% Raw water within 24 hr.	100 % Survival of the fish in 100% Raw water within 24 hr.	100 % Survival of the fish in 100% Raw water within 24 hr.	IS 6582 (Part 2) 2001 RA 2019
Manganese as Mn	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	Apha 24th Edition:2023 3111B
Iron as Fe	<0.02	<0.02	0.334	0.243	0.236	0.242	0.26	IS 3025 (Part 53): 2024
Vanadium	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05	IS 3025 : Part 74 : 2022
Nitrate as NO3	6.46	5.83	1.12	0.94	1.03	1.11	2.75	APHA 24th Ed. (4500-NO3-B):-2023





Sources:

1. Primary water quality criteria for class SW-IV waters (Harbour) as per EPA, 1986
2. Guidelines for coastal water quality, Dept. of Environment, Govt, of India, General notice ne 620 of 1999
3. Central Pollution Control Board, Pollution Control Acts, Rules and Notifications, Fourth Edition, Ministry of Environment and Forests, 2001, 897pp.

7. Sediment Quality

Sediment samples were collected from port berth area (19°17'21" N 84°56' 55" E) for determination of their physico-chemical properties. The sediment pH varied from 6.54-6.91 with mean value of 6.78 indicating prevalence of alkali medium within the sedimentary environment (Table 7.1). Sodium level in sediment varied from 731.62-745.6 mg/kg with mean value of 738.70 mg/kg. Maximum values were observed during Dec 2025 and minimum during March 2026. Potassium values are varied from 8.92-11.84 mg/kg with mean value of 10.41 mg/kg. The sediment phosphate value is ranged from 26.54-31.26 mg/kg with average value of 28.85 mg/kg, The maximum value recorded during the month of Jan 2026 where as the minimum value recorded during the month of Dec 2025. The sediment chloride value is varied from 2876-3008.8 mg/kg with average value of 2957.3 mg/kg. The maximum value was recorded during Oct 2025 whereas the minimum value recorded during Jan 2026, the maximum Sulphate value (233.4) was observed during Nov 2025 while it was minimum (227.83) in the month of March 2026. The value of petroleum hydro carbon (PHC) was ranged from 0.0028-0.0038pg/L with mean value of 0.0033 during the sampling period. The value of lead varied from 0.014-0.021 g/kg during the entire sampling period. The mercury value was varied from 0.001-0.004 with average value of 0.003.

The Levels of hexavalent chromium value is varied from 17.28-21.84 with average value of 19.65. The Percentage of organic carbon varied from 0.26 -0.34%. With average value of 0.31.

From the analysis of Sediment quality parameters of the harbour area from October 2025 to March 2026, it can be stated that the Sediment quality of harbour area is good as almost all parameters and parameters are well within the permissible limits.

Table 7.1 Sediment parameters during October 2025 to March 2026

	Oct 2025	Nov 2025	Dec 2025	Jan 2026	Feb 2026	March 2026	Average	Method
Texture	Fine & moderately well sorted	Fine & moderately well sorted	Fine & moderately well sorted	Fine & moderately well sorted	Fine & moderately well sorted	Fine & moderately well sorted	--	WCS/SOP/SOIL
pH Value	6.86 at 26.3	6.76 at 24.7	6.91at 24.2°C	6.75 at 24.5°C	6.54 at 25.0°C	6.87 at 25.7°C	6.78	IS 2720 (Part-26): 1987
Available Sodium as Na	738.5	741.25	745.6	734.7	740.5	731.62	738.70	USEPA 6010D,2014. Rev No.4:2014
Available Potassium as K	8.92	11.25	10.54	9.81	10.12	11.84	10.41	USEPA 6010D,2014. Rev No.4:2014
Available Phosphorous as P	27.54	29.31	26.54	31.26	28.36	30.06	28.85	WCS/SOP/SOIL
Chloride	3008.8	3005.07	3004.3	2876	2965.3	2884.2	2957.3	USDA:1954 US-affirmed 2010
Sulphate	230.4	233.4	229.3	232.5	230.61	227.83	230.67	WCS/SOP/SOIL
PHC	0.0038	0.0032	0.0036	0.0028	0.0033	0.003	0.0033	UNEP 1992
Lead	0.014	0.02	0.018	0.015	0.016	0.021	0.017	EPA 3050B
Mercury	0.001	0.003	0.002	0.004	0.003	0.002	0.003	EPA 3050B
Hexavalent Chromium	20.25	21.84	19.65	17.28	20.34	18.52	19.65	WCS/SOP/SOIL
Organic Carbon	0.26	0.33	0.28	0.34	0.32	0.3	0.31	IS 2720 (Part-22):1972 RA 2020

GOPALPUR PORTS LIMITED ODISHA INDIA
WORLD CONSULTANCY SERVICES PVT. LTD. CUTTACK


8. Ground Water

The potable water was collected from the drinking water available inside the port and analysed for different water quality parameters like, colour, order, turbidity, pH, Total hardness, Iron, Chloride, TDS, Calcium, Magnesium, Sulphate, Fluoride, Alkalinity, Salinity, Zine, Lead and E. Coil and the values are within the permissible limit. The monthly values and the average values are depicted in Table 8.1

Table 8.1 Ground Water parameters during October 2025 to March 2026

Canteen							Near new railway side	Requirement as per IS 10500:2012 Reaffirmed 2018
Ground water parameter	Oct 2025	Nov 2025	Dec 2025	Jan 2026	March 2026	Average	Feb 2026	
Colour	1	1	1	--	1	1	1	Max, 5
Odour	Agreeable	Agreeable	Agreeable	Agreeable	Agreeable	--	Agreeable	Agreeable
Turbidity	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1	0.4	1
pH Value	7.694 at 26.9°C	7.257 at 25.1°C	7.781 at 24.6°C	6.924 at 25.0°C	6.841 at 25.6°C	7.2994	8.052 at 24.3°C	6.5-8.5
Total Hardness as $CaCO_3$	158	174	162	144	156	158.8	193	200
Iron as Fe	<0.02	<0.02	<0.02	<0.02	<0.02	<0.02	0.132	1
Chloride as Cl	58.63	61.98	55.98	62.73	53.48	58.56	212.43	250
Total Dissolved Solid as TDS	218	226	230	223	216	222.6	344	500
Calcium as Ca	32.87	41.68	30.56	36.07	34.47	35.13	26.45	75
Magnesium as Mg	18.47	17.01	20.9	13.12	17.01	17.3	18.95	30
Sulphate as SO_4	1.46	1.5	1.76	1.65	1.72	1.62	24.5	200
Fluoride as F	<0.02	<0.02	<0.02	<0.02	<0.02	<0.02	0.668	1
Total Alkalinity as $CaCO_3$	115	125	110	140	125	123	130	200
Salinity	0.06	0.04	0.03	0.05	0.02	0.04	0.06	--
Zinc as Zn	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05	<0.05	5
Lead as Pb	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	0.01
E.Coli	<2.0	<2.0	<2.0	<2.0	<2.0	<2.0	<2.0	Shall not be detectable in any 100 ml sample






9. Effluent from coal stack yard


The water from the coal stack yard was collected from coal stack yard available inside the port premises for analysis of different parameters such as colour, odour, TSS, pH, Temperature, Oil & Grease, TRC, Ammonical Nitrogen, TKN, Free Ammonia, BOD, COD, As & Hg. The monthly average value of the parameters are depicted in table 9.1

Table 9.1 Coal stack yard parameters during October 2025 to March 2026

Settling pit-1							
parameter	Oct 2025	Nov 2025	Dec 2025	Jan 2026	Feb 2026	March 2026	Average
Colour	4	5	4	4	5	4	4.3
Odour	Agreeable	Agreeable	Agreeable	Agreeable	Agreeable	Agreeable	Agreeable
Suspended Solids as TSS	<5.0	<5.0	<5.0	<5.0	<5.0	<5.0	<5.0
pH Value	8.946 at 26.9	8.217 at 24.6	8.654 at 24.2°C	7.94 at 25.1°C	8.045 at 25.5°C	7.987 at 25.3°C	8.298
Temperature	26.8	25.4	24.6	25.2	25.6	25.2	25.5
Oil &Grease	<4.0	<4.0	<4.0	<4.0	<4.0	<4.0	<4.0
Total Residual Chlorine	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04
Amonical Nitrogen	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
Total Kajeldahl Nitrogen	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
Free Ammonia	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
Biochemical Oxygen Demand as BOD (5 Days at 20°C)	8.6	7.9	8.2	9	7.2	8.6	8.3
Chemical Oxygen Demand	18	20	19	22	16	20	19.2
Arsenic as As	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
Mercury as Hg	<0.0005	<0.0005	<0.0005	<0.0005	<0.0005	<0.0005	<0.0005

Settling pit-2							
parameter	Oct 2025	Nov 2025	Dec 2025	Jan 2026	Feb 2026	March 2026	Average
Colour	5	3	4	5	3	4	4.0
Odour	Agreeable	Agreeable	Agreeable	Agreeable	Agreeable	Agreeable	Agreeable
Suspended Solids as TSS	<5.0	<5.0	<5.0	<5.0	<5.0	<5.0	<5.0
pH Value	8.500 at 28.4	7.934 at 24.8	7.854 at 24.2°C	8.062 at 24.8°C	7.482 at 25.0°C	7.854 at 25.6°C	7.948
Temperature	27.8	24.3	25	24.7	25.5	24.2	25.3
Oil &Grease	<4.0	<4.0	<4.0	<4.0	<4.0	<4.0	<4.0
Total Residual Chlorine	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04
Amonical Nitrogen	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
Total Kajeldahl Nitrogen	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
Free Ammonia	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
Biochemical Oxygen Demand as BOD (5 Days at 20°C)	26.7	23.5	21.6	16.2	22.7	20.6	21.9
Chemical Oxygen Demand	42	41	38	32	40	42	39.2
Arsenic as As	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
Mercury as Hg	<0.0005	--	<0.0005	<0.0005	<0.0005	<0.0005	<0.0005






Settling pit-3							
parameter	Oct 2025	Nov 2025	Dec 2025	Jan 2026	Feb 2026	March 2026	Average
~~Colour~~	~~3~~	~~5~~	~~3~~	~~4~~	~~5~~	~~5~~	~~4.2~~
Odour	Agreeable	Agreeable	Agreeable	Agreeable	Agreeable	Agreeable	Agreeable
Suspended Solids as TSS	<5.0	<5.0	<5.0	<5.0	<5.0	<5.0	<5.0
pH Value	8.437 at 26.9	8.061 at 25.1	8.354 at 24.3	7.82 at 24.2°C	8.172 at 25.3°C	7.874 at 25.2°C	8.120
Temperature	26.8	25.4	25	24.8	25.2	24.9	25.4
Oil &Grease	<4.0	<4.0	<4.0	<4.0	<4.0	<4.0	<4.0
Total Residual Chlorine	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04
Amonical Nitrogen	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
Total Kajeldahl Nitrogen	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
Free Ammonia	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
Biochemical Oxygen Demand as BOD (5 Days at 20°C)	7.3	6.8	7.6	8	7.1	7.8	7.4
Chemical Oxygen Demand	18	15	20	22	16	18	18.2
Arsenic as As	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
Mercury as Hg	<0.0005	<0.0005	<0.0005	<0.0005	<0.0005	<0.0005	<0.0005

Drain (Near Settling Pit)							
parameter	Oct 2025	Nov 2025	Dec 2025	Jan 2026	Feb 2026	March 2026	Average
Colour	5	3	5	4	5	3	4.2
Odour	Agreeable	Agreeable	Agreeable	Agreeable	Agreeable	Agreeable	Agreeable
Suspended Solids as TSS	<5.0	<5.0	<5.0	<5.0	<5.0	<5.0	<5.0
pH Value	7.618 at 28.0	7.281 at 24.6	7.502 at 24.5	8.175 at 24.7°C	7.641 at 25.1°C	7.806 at 25.4°C	7.6705
Temperature	27.2	25	24.8	25	25.6	24.1	25.3
Oil &Grease	<4.0	<4.0	<4.0	<4.0	<4.0	<4.0	<4.0
Total Residual Chlorine	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04	< 0.04
Amonical Nitrogen	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
Total Kajeldahl Nitrogen	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
Free Ammonia	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
Biochemical Oxygen Demand as BOD (5 Days at 20°C)	22.6	25.5	23.2	26.4	22.2	24.6	24.1
Chemical Oxygen Demand	36	45	38	40	32	38	38.2
Arsenic as As	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01	<0.01
Mercury as Hg	<0.0005	<0.0005	<0.0005	<0.0005	<0.0005	<0.0005	<0.0005





Conclusion:

The shoreline, sediment, and wave dynamics at Gopalpur from October 2025 to March 2026 exhibit significant seasonal variations. Shoreline distances show fluctuations, with maximum variations at 2.5 km & 3.0 km along Gopalpur Port South, indicating dynamic sediment transport. The northern shoreline experiences erosion at the groin but gains sediment at farther distances, suggesting northward sediment transport. Gopalpur Tourist Beach nearshore areas experiences erosion.

Overall, the coastal processes at Gopalpur are highly dynamic, driven by seasonal effects, wave action, and sediment transport, shaping its shoreline evolution.

Ambient air quality such as PM10, PM2.5, SO_2, NO_2 were monitored twice in a week at the four points within the port premises from October 2025 to March 2026. It is observed that air pollution is mainly due to high particulate matter. The maximum Particulate matter recorded at station 'B' where major port activities are in progress and high vehicular movement. The maximum SO_2 was recorded at station 'B' and NO, were recorded at station "B" due to high vehicular movement. The values observed are well within the NAAQ norms stipulated by MoFFCC and Environment (protection) Act, 1956. Further, sound level monitored during the day and nighttime is within the permissible limits stipulated by CPCB for industrial 75dB in day time and 70dB in the night time. Thus, the ongoing port activities at present are not detrimental to the air quality and noise level and indicates a pollution free terrestrial port environment.

Water quality parameters of port harbour area monitored for the period from October 2025 to March 2026 include, pH, dissolved oxygen (DO), color and odour, faecal coliform, biological oxygen demand (BOD), Lead, Cadmium, Hexavalent Chromium, Total Chromium, Copper, Zinc, Selenium, Nickel, Cyanide, Fluoride, Phosphorous, Sulphide, Phenolic Compound, Bio-Assay, Manganese, Iron, Vanadium, Nitrate. All the parameters are well within the standard limit during the sampling period.

Sediment quality of port harbour area was assessed by examining sediment texture (mean grain size, sorting, skewness, and kurtosis), pH, sodium, potassium, phosphate, chloride, sulphate, PHC, lead, mercury, organic carbon and hexavalent chromium. Sediment is alkaline in nature while phosphate, PHC, mercury, organic carbon and hexavalent chromium are present in trace amount. The metal concentrations both in water and sediment are within the permissible limit.

References

APHA, 2000. Standard methods for examination of water and wastewater 18th Edition; Prepared and published jointly by: American Public Health Association (APHA), American Water Works Association (AWWA), Water Pollution Control Federation (WPCF), New York.

Cui, W., Meng, Q., Feng, Q., Zhou, L., Cui, Y., & Li, W. (2019). Occurrence and release of cadmium, chromium, and lead from stone coal combustion. International Journal of Coal Science & Technology, 6(4), 586-594.

Echegoyen, Y., Boyle, E. A., Lee, J. M., Gamo, T., Obata, H., & Norisuye, K. (2014). Recent distribution of lead in the Indian Ocean reflects the impact of regional emissions. Proceedings of the National Academy of Sciences, 111(43), 15328-15331.

Grasshoff, K., 1999. Methods of sea water analysis (Grasshoff, K., Ehrhardt, M.,and Kremling. K., Eds.). Verlag Chemic; Weinheim: pp.61-72.

Hasan, M. R., Khan, M. Z. H., Khan, M., Aktar, S., Rahman, M., Hossain, F., & Hasan, A. S. M. M. (2016). Heavy metals distribution and contamination in surface water of the Bay of Bengal coast. cogent environmental science, 2(1), 1140001. DOI:10.1080/23311843.2016.1140001. Swaine, D. J. (2013). Trace elements in coal. Butterworth-Heinemann., London, P.278.

GOPALPUR PORT LIMITED ODISHA INDIA

MV WORLD CONSULTANCY SERVICES PVT. LTD. CUTTACK
